Subcontract 2507007-1

Arch-Con Corporation
190 TC Jester, Suite 200
Houston, Texas 77007
Phone: (713) 533-1900

Project: 2507007 - Silos Springs
1235 Shadowdale Drive
Houston, Texas 77043

Countertops

SUBCONTRACTOR:	Golden Stones LP 7902 Hillmont Street Houston, Texas 77040 Phone: 7139347887 Fax: 7139347889
ESTIMATED START DATE:	10/01/2026
ESTIMATED COMPLETION DATE:	04/30/2028
CONTRACT DATE:	03/25/2026
RETAINAGE:	10.0%

ATTACHMENTS:
Silos - Construction Schedule.pdf, Silos - Drawing & Spec Logs.pdf

SCOPE OF WORK

SCOPE OF WORK: All specified materials shall be requisite. Subcontractor will be responsible for correct and accurate layout and placement of work, based upon basic control points or lines established by general contractor.

1. Furnish and install all COUNTERTOPS in accordance with the plans and specifications including, but not limited to:

    1. Supply and install all unit kitchen, island, peninsula and bar tops for all three hundred and forty-six (346) Apartment Units as described in the Contract Documents. All countertops in the Apartment Units shall be 3cm Eased Edge TQ Yukon (G3 OR G4) Quartz (ST-50).
    2. Supply and install unit bathroom vanity quartz countertops, backsplash and side splash for all three hundred and forty-six (346) Apartment Units as described in the Contract Documents. All vanity countertops in the Apartment Units shall be 3cm Eased Edge TQ Yukon (G3 OR G4) Quartz and the back and side splashes shall be 2cm Eased Edge TQ Yukon (G3 OR G4) Quartz (ST-50).
    3. Unit entry thresholds furnished and installed by others.
    4. The Subcontractor shall furnish and install all unit kitchen sinks. Kitchen sinks shall be GS-HM-2818S and GS-HM-3118S 18ga Stainless Steel undermount basin for all unit kitchens. The Subcontractor shall drill all kitchen sink faucet and valve holes including air gap holes, sprayer holes, garbage disposal push button and switches holes. The Subcontractor shall also provide an eased-edge, polished, finished sink opening and confirm with the plumbing subcontractor that the drainpipe and garbage disposal connections will fit properly to the sink prior to sink installation. The sink shall be installed with clips as per best industry practices.
    5. The Subcontractor shall furnish and install all unit bathroom vanity sinks. Vanity sinks shall be GS-W021 White Porcelain undermount sinks. The Subcontractor shall drill vanity sink faucet and valve holes. The Subcontractor shall also provide an eased-edge, polished, finish sink opening and confirm with the plumbing subcontractor that the drainpipe connections will fit properly to the sink prior to sink installation. The sink shall be installed with clips as per best industry practices. The Subcontractor shall provide all cut-out information for the sinks to the Contractor.
    6. Supply and install 3cm eased edge Galaxy Stone White Apollo (CO-10) at all Outdoor Grill Stations and at the Pool Fire Table Wall Cap Tops. Subcontractor shall provide all sink and fire feature cut outs in the stone. Subcontractor shall install the grill station sinks (sinks provided by others).
    7. Supply and install 2cm Eased Edge Daltile Lincoln White NQ59 Leather (SS-5) at all locations shown in the Café including at the Café Service Counter with Waterfall Legs, Café Food & Beverage with 12" Backsplash, Café Queue 1, 2, Cafe, Café Business, Café Lounge, and Café Men's and Women's restrooms with 4" Backsplash Tops.
    8. Install undermount kitchen sinks at the Café Food & Beverage and Café Service countertops. Sink supplied by others.
    9. Install undermount Vanity Sink at the Café Men's/Women's Restroom tops. Sink supplied by others.
    10. Supply and Install Mockett TM2B 8" x 2" Trash Grommet Black A5.52 at the Café Service Counter, Cafe, and Café Lounge Tops.
    11. Supply wall mounted steel overhang brackets at Café Lounge Tops (to be Installed by Others).
    12. Supply CSP-04 Cantilever overhang brackets at Café Lounge Tops (to be Installed by Others).

ARCH·CON CORPORATION

Subcontract 2507007-1

13. Supply and install all 2cm, 1.5" mitered edge, Cambria Luxury Abbey (SS-2) at Club north, Club kitchen, Club island with waterfall legs (polish interior legs).
14. Supply and install all 2cm, 1.5" mitered edge, Cambria Luxury Ironsbridge (SS-3) at Break Room with 4" splash, Open Office (Leasing), Business kitchen with 4" splash, Business island with waterfall legs (polished interior legs), Phone Room, and Fitness. Includes labor to cut out desk grommets at countertops.
15. Supply and install all 2cm, 1.5" mitered edge, Pomogranit Quartzite Ceilo (ST-1) at Lobby South Wall (eased edge), Lobby South countertops, Club Men's and Club Women's Restrooms, Fitness Men's and Fitness Women's Restrooms, and Mail trash.
16. Supply and install all 2cm, eased edge Pomogranit White Camouflage (ST-2) at Club fireplace with waterfall edge tops.
17. Subcontractor shall install all undermount kitchen sinks at Break Room, Club island, and Business Lounge. Sinks to be supplied by others.
18. Subcontractor shall install all undermount vanity sinks at Clubhouse Men's and Women's Restrooms and the Fitness Men's and Women's Restrooms. Sinks to be supplied by others.
19. Subcontractor shall cut out openings for all sink faucets, sink valves, disposal air switches, dishwasher air gaps, electrical devices, raceways, trash receptacles, desk grommets, and all other opening required in countertops and vertical stone provided by this Subcontractor.
20. Furnish all CSA-004 wall-mounted steel support brackets at Phone Rooms countertops. Brackets to be installed by others.
21. Furnish and install all CSP-002 overhang brackets at Club island and Business island countertops.
22. The Subcontractor shall submit SDS on all compounds / chemicals used on the site, including caulk.
23. Subcontractor shall produce shop drawings for all countertops and stone. Coordinate all dimensions and openings with the Cabinet, Plumbing, and Electrical subcontractors.
24. Supply and install all countertops, vanity tops and bar tops with a minimum clearance of 3/16" from any side splash or backsplash to the adjacent wall. Countertops shall not be permitted to have joints within 2’-0” of a sink cutout unless there is a corner condition within 2’-0” of the sink cutout.
25. The Subcontractor shall be responsible for pre-measuring each Apartment Unit scheduled to receive countertops to ensure an accurate fit.
26. The Subcontractor must meet the following requirements - countertops shall fit tight to wall with no visible gaps, provide and install the kitchen sinks and vanity sinks and there shall be no visible gaps at any sink, mitered joints shall be tight and even with no chipping, countertop ends and edges shall be attached and secured properly,
27. Upon completion of the installation of the countertops, the Subcontractor shall protect the countertops with thick, self-adhesive plastic, film cut to fit and held in place with tape.
28. The Subcontractor shall provide and install caulking on all kitchen and vanity to match the countertop color. Caulk shall be clean, smooth and uniform. The joint between the countertop and wall tile in the kitchen shall be grouted to match the wall tile color (by others).
29. Subcontractor shall not cut any stone materials inside the building, corridors, units, balconies, porches/patios, or the parking garage. Should a violation occur by cutting in these areas, a fine of $1,000 per notification will be assessed. This fine will be deducted from the next payment application.
30. All countertops shall be installed level and free from defects and variations in color. Stone is a natural product and may vary in color and texture. It is the Subcontractors’ responsibility to ensure that extreme variation does not occur between seemed areas. Colors should be uniform and variations in color should not be noticeable. Should color differentiation be noticeable, the countertop will be replaced by this Subcontractor.
31. This Subcontractor is responsible for and shall provide equipment for all fabrication, freight, shipping, receiving, offloading, staging, storing, relocating, distributing, stocking, and protecting all countertops prior to installation.
32. Subcontractor responsible for all mockups and mockup units. This includes early submission of submittals, partial and/or expedited delivery of materials, and early mobilization for the installation of mockups and mockup rooms as determined by the Contractor.
33. The Subcontractor shall provide all labor necessary for cleanup of all countertop debris and packaging on a daily basis and deposit it in the on-site dumpsters provided by the Contractor.
34. Quality control standards must be approved by the Contractor’s jobsite staff prior to start of job.
35. Prior to installation, the Subcontractor shall carefully inspect the installed work of all other trades and verify that all such work is complete to the point where installation may properly commence.
36. The Subcontractor shall provide all dishwasher brackets.
37. The Subcontractor shall obtain all cut out information for the fixtures from the plumbing subcontractor and appliance manufacturer. Subcontractor shall perform all work involved with cut outs.
38. Upon approval of the countertop shop drawings by the Contractor, the Subcontractor shall release the project for fabrication.
39. The countertop installation shall meet the requirements of the project schedule. The Subcontractor shall be responsible for placing the order for all countertops in order to meet the completion dates as per the project schedule.
40. The Subcontractor shall assist the Contractor in the coordination and scheduling of all work pertinent to his scope of work and shall inform the Contractor of his requirements to result in a well-coordinated job.
41. Completion of all countertops required as part of this project is included in this Subcontract.
42. All containers needed for the storage and safekeeping of materials shall be provided by the Subcontractor. These containers will be located in an area designated by the Contractor.
43. This Contract includes all mobilizations of the Subcontractor.
44. All sales tax included.

ARCH·CON CORPORATION

Subcontract 2507007-1

45. Subcontractor to provide competent on-site supervision and the proper manpower required to maintain the project schedule. Competent personnel supervision is required to be onsite at all times while Subcontractor's crews are working onsite.
46. If required by the General Contractor, the subcontractor will provide a detailed manpower schedule showing that adequate manpower is being furnished.
47. Provide daily trash removal of your work debris to Contractor provided dumpster. If cleanup is not performed in a reasonable manner, the general contractor will supplement cleanup at subcontractor's expense. Work areas to be broom cleaned at the time of crew's completion of work in that area.
48. Subcontractor agrees to provide one or more person(s) to participate in a composite cleanup crew for the entire duration of this scope of work. Personnel for the composite cleanup crew, by this subcontractor, will be required for only one day of the week, for every week that this subcontractor is performing work on the project. If manpower is not allocated by this subcontractor to the composite cleanup crew, the general contractor will supplement that day's cleanup at this subcontractor's expense.
49. Subcontractor and/or material suppliers understand and agree to furnish and/or install each system or item as a complete and operating system as required by all governing codes and jurisdictions, and as could be interpreted or inferred by the Contract Documents.
50. All work to be performed per the Contract Documents and to meet requirements of any codes and regulations of the authorities having jurisdiction for this Project.
51. Subcontractor agrees to follow all Keyed and General notes included within the Contract Documents.
52. All permitting associated with this scope of work. The general building permit is provided by Arch-Con Corporation, but all other permits or special permits, fees, and licenses for this scope of work (only) are included in this scope.
53. This Subcontractor to participate in the resolution process for any testing within this subcontractor's scope that fails to meet testing/inspection requirements.
54. This Subcontractor is responsible for all hoisting and material handling associated with completing its scope of work.
55. City of Houston certified flagmen as required for material deliveries and traffic entering and exiting the site associated with Subcontractor's Scope of Work.
56. Provide all Layout & Field Engineering (from Contractor Control Pts) required for this subcontractor's scope of work.
57. If required, Subcontractor is responsible for obtaining field dimensions required for the preparation of shop drawings, submittals, and final fabrication.
58. Subcontractor is responsible for protection of adjacent finished surfaces, adjacent structures, underground utilities, and other in-place construction during the installation of their work. Including protection of in-place concrete pavement and curbs.
59. Coordinate and assist testing/inspection agency and officials with all required tests and inspections. Subcontractor is responsible for any impact fees or back-charges for not properly notifying the testing lab or inspector(s) of cancellations three (3) days before scheduled inspection. Subcontractor is responsible for all re-inspection fees due to failed tests/inspections.
60. Contact utility one-call before excavation work begins.
61. Provide all dewatering of surface water necessary for this Subcontractor to perform its Work. Well pointing or deep dewatering not included in this Subcontract.
62. All Work in accordance with ADA and Fair Housing requirements
63. All warranties, special warranties and closeout documents in accordance with the Contract Documents. This includes any/all Owner usage trainings/demonstrations per the specifications. Closeout documents required for review four (4) months prior to scheduled substantial completion.
64. All submittals, samples, shop drawings, and mock-ups, and any LEED documentation as required; including any/all professional engineering as required. Submit all items in a timely manner as required to meet Project Schedule completion dates.
65. Subcontractor is responsible for completing adequate coordination/review efforts of plans and specifications ahead of all work to be performed. All concerns, missing information, and discrepancies are to be brought to the General Contractors attention in a timely manner ahead of the work to be performed, in order to prevent delays to the work in question and/or the project schedule. Any delay to the project due to the failure of this subcontractor notifying the General Contractor of said concerns in a timely manner will be rectified at the Subcontractor's expense.
66. Subcontractor agrees to work Saturdays as required to make-up weather days or if progress was delayed during the work week, in an effort to maintain the agreed upon construction schedule.
67. Subcontractor agrees to follow the dates and timelines within the provided construction schedule and agrees to participate in acceleration of activities as the schedule is updated and developed.
68. Mark up for changes is limited to 15% for profit/overhead.

2. This project requires all subcontractors to participate in subcontractor default insurance. Subcontractors are required to complete and submit a subcontractor prequalification questionnaire with related documents as requested by Arch-Con to qualify for the program. All information will be kept strictly confidential and only reviewed by key finance and risk management team members. Failure to participate in the program may result in payment delays or breach of contract.
3. This Subcontract is for the entirety of the scope of work set forth in this agreement and as per the Project Construction documents (plans and specifications). Any quantities, assumptions, clarifications, exclusions, terms or conditions indicated in Subcontractor's proposal will not be considered as a limitation of the work that Subcontractor is herein obligated to perform (furnish and properly install) for a complete application. Subcontractor acknowledge this obligation by executing this agreement.

ARCH·CON CORPORATION

Subcontract 2507007-1

4. Subcontractor is aware that overtime may be necessary if Subcontractor's lack of progress is apparent to Contractor, in Contractor's reasonable judgment, as insufficient to allow Subcontractor's completion of the work within the agreed scheduled duration of time. Subcontractor's lack of progress is due to his own negligence and not by delays from weather or other trades.
5. For this project Pay Applications are due on the 15th of the month for work completed through the current work period.
6. Coordinate all work with the Project Superintendent and other trades working on the project.
7. Prior to starting work in the field, verify with the Project Superintendent that your plans are inclusive of the latest changes if applicable.
8. If required by the General Contractor, the subcontractor will provide a detailed manpower schedule showing that adequate manpower is being furnished.
9. General Contractor reserves the right to joint check material and equipment suppliers as well as any sub-subcontractors of this Subcontractor, if deemed necessary from Contractor's reasonable assessment after review of Subcontractor's credit references or if the suppliers and/or sub-subcontractors give notification/reason to Contractor that Subcontractor is delinquent in or not paying bills due to Subcontractor's negligence.
10. Submittals, a Schedule of Values, and any LEED documentation (if required) are to be submitted to Arch-Con no later than Date: 04/03/26
11. Estimated Start Date: 11/01/26

SUBCONTRACT CLARIFICATIONS:

1. If this Subcontract references a Master Agreement, then all Terms and Conditions and Exhibits "A" through "F" of that agreement apply to this Subcontract. If this Subcontract does not reference a Master Agreement number, then the attached Exhibits "A" through "F" as listed below are made part of this Subcontract:

    1. Exhibit "A" – Standard Terms and Conditions
    2. Exhibit "B" – Application for Payment
    3. Exhibit "C" – Contractor's Insurance Requirements of Subcontract
    4. Exhibit "D" – Subcontractor/Supplier's Sub-Subcontractor/Sub-Supplier Listing
    5. Exhibit "E" – Agreement between GC and Subcontractor to Establish Independent Relationship
    6. Exhibit "F" – Safety Addendum to Arch-Con Corporation Subcontract

2. Commencement of any work on this Subcontract for the above referenced project means the subcontractor accepts all terms and conditions of this Subcontract.
3. This project will utilize Procore's (procore.com) project management and collaboration system for all project documentation. Applicable team members of this Subcontractor, as may be designated by Contractor from time to time, will be invited to, and are required to create a Procore username (email) and password if they do not already have one. This Subcontractor will be expected to obtain drawings, sketches, RFIs, meeting minutes, coordination drawings, change information, etc. via Procore's system. Contractor will notify subcontractors as relevant items are added. It will be the responsibility of this Subcontractor to regularly check and review updated documents as they are added. Subcontractor shall be responsible for its failure to properly monitor and utilize Procure on the Project, including but not limited to any subsequent errors, failures, or delays on the Project. Applicable team members of this Subcontractor are required to complete a free, one-hour subcontractor training certification course located at http://learn.procore.com/procore-certification-subcontractor within (2) two weeks following contract execution. There will be no cost to this Subcontractor for use of Procore. It is recommended that this Subcontractor provide mobile iOS or Android devices with the Procore App installed to at least one individual on-site to provide real-time access to current posted drawings, specifications, RFIs, submittals, project documents, as well as any deficient observations or punch list items. Providing mobile access will improve communication, efficiency, and productivity for all parties.
4. Subcontractor is required to use Procore Pay as provided by Procore Technologies, Inc. ("Procore Pay"), at its own cost and expense, when invoicing, executing lien waivers, and furnishing additional required documentation related to receiving payment from General Contractor;
5. Invoice General Contractor, via Procore Pay, only for amounts based on the percentage of completed work described in the Project Schedule of Values below no later than 15th of each month;
6. Maintain commercially reasonable controls designed to prevent unauthorized access to your use of Procore Pay through your credentials or other means and notify General Contractor in the event your use of the Procore Pay or your bank account has been or you suspect has been compromised, subject to fraud or any other adverse action;
7. Confirm with General Contractor that the Parties are accurately connected within Procore Pay for this contract; and
8. Provide and maintain a current list of Procore Pay Administrators authorized to manage payments related activities to the General Contractor.
9. Price is lump sum to include all materials, labor, equipment, markup/fee and any applicable sales tax on materials. Sales tax is not shown as a separate cost as this is a lump sum/new construction contract. There is no sales tax on labor as this project is new construction.
10. List of Drawings (Drawing Log Attached)
11. Job Site Delivery Address is 1235 Shadowdale Dr., Houston, TX 77043.
12. Schedule all work with Daniel Lopez dlopez@arch-con.com 713-670-4077.
13. This Subcontract is for work to be performed under the Prime Contract between the Owner, Moody National, and the Contractor, Arch-Con Corporation, dated January 30th, 2026.

ARCH·CON CORPORATION

Subcontract 2507007-1

#	Description	Amount
1	**Golden Stones SC - Countertops**	**$778,965.00**
	Grand Total:	**$778,965.00**

Arch-Con Corporation
190 TC Jester, Suite 200
Houston, Texas 77007

Golden Stones LP
7902 Hillmont Street
Houston, Texas 77040

Manager

SIGNATURE **TITLE** **DATE**

SIGNATURE **TITLE** **DATE**

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

EXHIBIT "A"
Standard Terms and Conditions

Arch-Con Corporation's Standard Terms and Conditions of this Subcontract Agreement are hereby made a part of the Subcontract by reference. For and in consideration of the mutual promises and covenants herein contained, the Subcontractor and the Contractor agree as follows:

1. **TERMS OF SUBCONTRACT:** Each of the parties hereto agrees and represents that this agreement and the exhibits thereto and the other Subcontract Documents comprise the full and entire agreement between the parties affecting the work contemplated, and no other agreement or understanding of any nature concerning the same has been entered into or will be recognized, and that all communications, representations, negotiations, acts, work performed, or payments made prior to or contemporaneous with the execution hereof shall be deemed merged in, integrated and superseded by these documents. This agreement can be modified only by written agreement signed by authorized representatives of each party hereto. The headings of the articles, in emphasized type, are for convenience and are not to be considered in construing the meaning of the paragraphs.

2. **THE WORK:** The Subcontractor covenants, promises and agrees to furnish all material, equipment and personal property and to diligently and fully perform and supervise all work herein described on the drawings and specifications and summarized in the description of work for the construction of the Project for the use and benefit of the Owner in strict accordance with the Prime Contract between the Owner and the Contractor, which is hereby made a part of the Subcontract by reference (hereafter the "work", "sublet work" or "subcontract work"). The Work shall be done to the satisfaction of the Contractor and the Owner and shall be done in timely, faithful and strict compliance with this Subcontract and all the Subcontract Documents defined below. If any part of the Subcontractor's Work depends upon proper execution of any completed work and services performed or otherwise provided by Contractor or other trades on the Project, the Subcontractor shall, prior to proceeding with its Work, inspect existing work and promptly report to Contractor any apparent or discovered discrepancies or defects. The failure of the Subcontractor to examine and report any such discrepancies shall bar any claims thereafter that any defects or delays in Subcontractor's Work are due to defects, delays or disruptions in the activities performed or otherwise provided by Contractor or other trades on the Project.

3. **INDEPENDENT CONTRACTOR:** The Contractor employs the Subcontractor, as an independent Contractor, to perform the part of the Work which the Contractor has contracted with the Owner to provide on the Project as set forth in the description of work. The Subcontractor agrees to provide and pay for all necessary management, supervision, labor, materials, tools, supplies, equipment and/or any other items customarily provided in Subcontractor's line of work or required to diligently and fully perform and complete the Work described above. Subcontractor shall be an independent contractor under this Subcontract and shall assume all of the rights, obligations, and liabilities applicable to it as such an independent contractor hereunder. Subcontractor is responsible for the means, methods, and details of the Subcontract Work.

4. **DIRECTION OF SUBLET WORK:** It is understood that Subcontractor is an independent contractor and Contractor shall have no right to direct the operations or employees of Subcontractor. Subcontractor agrees to maintain a familiarity with conditions existing over the entire Project on which the work is located so that he will be aware of dangerous conditions, whether obvious or hidden, and Subcontractor agrees to warn its employees, subcontractors and suppliers of unsafe conditions on the Project premises. Subcontractor shall immediately notify the Contractor of any unsafe working conditions including, but not limited to, the presence of asbestos and/or PCPs on the Project. The Subcontractor acknowledges that: it is being paid by the job, not by the hour or some other time measured basis; Subcontractor is free to hire as many helpers as he desires and to determine what each helper will be paid; and Subcontractor is free to work for other contractors, or to send helpers to work for other contractors, which are under contract to the Contractor.

5. **ASSIGNMENT/SUBLETTING:** Subcontractor cannot assign, transfer, convey, sublet, or otherwise dispose of this subcontract or any part thereof, or his right, title or interest therein, or his power to execute the same, or any proceeds or receivables under this subcontract, without the consent in writing of Contractor. If Subcontractor does, with approval, sublet this subcontract or any part thereof, he shall require that his subcontractor be bound to him and assume toward him all of the obligations and responsibilities that he has assumed toward Contractor.

6. **PRIME CONTRACT:** The "Prime Contract" is the contract between the Owner and the Contractor for the Project. The term "Prime Contract" includes the plans, specifications, general conditions, any and all special terms and conditions, addenda, and all other contract documents which are incorporated into that agreement by its terms. Each exhibit attached hereto or referred to herein (including any documents incorporated therein) is incorporated herein in its entirety for all purposes as if copied at length and attached hereto. The Prime Contract and the Subcontract, including all exhibits, constitute the Subcontract Documents. In the event of a discrepancy between the Prime Contract and this subcontract, the greater quantity or quality, or the more stringent requirement, as determined in Contractor's sole discretion, shall govern. Subcontractor agrees to be bound to the Contractor by the terms of said Prime Contract insofar as they relate in any part or in any way to the work undertaken herein and assumes towards Contractor all duties and obligations which Contractor assumes towards the Owner by way of the

Subcontractor Initial_____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

Prime Contract. Subcontractor's proposal or quote is expressly excluded from this Subcontract. Subcontractor represents that he is fully acquainted with all of the physical conditions surrounding the job site, insofar as the same effects or relates to the performance of the work required by the subcontract, and has made all necessary investigations essential to a full understanding of any and all difficulties that may be encountered in the performance of the work.

7. **SAFETY:** Subcontractor is to adhere to their Company's Safety Program or OSHA requirements, whichever is more stringent. Subcontractor is responsible to meet or exceed all OSHA Haz/Com and other Safety Program requirements. Subcontractor's Safety Program is to be kept on site in the Subcontractor's vehicle(s), tool boxes, containers, etc. Subcontractor is required to produce these documents at the request of the Contractor. Subcontractor shall provide SDS information for all materials brought onto the site. Subcontractor shall provide flagmen/traffic control as necessary to complete scope of work.

8. **CONTRACTOR SERVICES:** Contractor shall provide the following for Subcontractor's use: temporary toilet, trash dumpster, elevation benchmark and primary control dimensions. If Subcontractor utilizes any of Contractor equipment not described herein, additional costs may apply.

9. **PROJECT ADMINISTRATION:** Subcontractor shall coordinate all work through Contractor's designated Project Manager and/or Superintendent and other trades working on the project. Prior to starting work in the field, Subcontractor shall verify with the Project Superintendent that all plans are inclusive of the latest changes if applicable. Subcontractor shall provide a person authorized to make binding decisions regarding schedule and cost issues to attend weekly Progress Meetings as required. Subcontractor shall submit daily reports to the Contractor on a daily basis. As-Built drawings located in the jobsite trailer are to be updated monthly prior to Subcontractor receiving payment. If the Project is LEED, Contractor shall require additional documentation from the Subcontractor for submission to LEED Online, to be provided at the same time as Submittal requirements. Subcontractor is required to generate their own punch-list and submit to Contractor for review. Subcontractor is required to complete all punch-list items within two (2) weeks of receipt of the punch-list from the Contractor.

10. **PAYMENT:** The Contractor agrees to pay the Subcontractor for the full, faithful, timely and complete performance of this Subcontract the Subcontract Amount stated on page 1 of the Subcontract, including all applicable taxes, and subject to additions and deductions for changes agreed upon in writing and all terms and conditions of payment. Payment of the stipulated sum is conditioned upon the submittal of Contractor's Application for Payment (Exhibit "B") hereby made a part of this Subcontract by reference. No payment will be made for services provided that are not submitted according to these submittal requirements.

11. **PROGRESS PAYMENTS:** Draw requests are to be submitted on Contractor's Application for Payment form and in accordance with Contractor's Instructions for Invoicing and Completion of Application for Payment Form (Exhibit B) by the 15th of a month for work completed through the current work period. Payment will be made on or about the last day of the next month following the period covered by the Application for Payment, less 10% retainage, provided payment for same has been made by Owner to Contractor. The retainage will be paid within 60 days after acceptance of the Project by the Owner, provided payment for same has been made by Owner to Contractor. Contractor may require Subcontractor to furnish evidence satisfactory to Contractor, in the form of sworn affidavits, and/or waivers and release of liens, if requested, that all claims for labor, services, equipment and materials furnished under this subcontract have been paid. It shall be a condition precedent to Contractor's obligation to make each payment (progress or final or otherwise) to Subcontractor hereunder that the funds for such payment have first been paid by Owner to Contractor. It is the intent of the parties that if payment from the Owner for all or a portion of the Subcontract Work is never received by Contractor, then Contractor will never have any obligations to pay the Subcontractor for such portion of the Subcontract Work not paid by Owner. Subcontractor hereby expressly assumes the risk of Owner nonpayment for any reason, and the Subcontract Amount set out on page 1 of the Subcontract reflects the assumption of that risk. No payments will be made unless this Subcontractor's rate of progress, work done and material furnished are satisfactory to the Contractor and as herein agreed upon.

    In the event of non-payment by the Owner, and if the contingent payment provisions of this paragraph 11, or any other contingent payment provision herein, is held to be unenforceable for any reason, Contractor acknowledges it will be obligated to pay Subcontractor within a reasonable time for work completed in accordance with the Subcontract Documents, subject to all other terms and conditions of the Subcontract Documents. For the purposes of determining the timing of payment under these circumstances, the parties hereby acknowledge and agree that a reasonable time for payment to Subcontractor in the case of Owner non-payment is within 180 days after Contractor's submission of a payment request to Owner that includes the work for which Subcontractor seeks payment or, if litigation or arbitration between Contractor and Owner that involves the monies sought by Subcontractor is instituted within that time, then within 60 days of final adjudication of any such litigation or arbitration. As an alternative to, or in conjunction with, Contractor pursuing a claim against Owner for payments due to Subcontractor for work on the Project, Contractor may assign its contractual rights against Owner for such funds as Subcontractor may be entitled to for such work pursuant to the Subcontract, which remain unpaid due to failure of payment by Owner to Contractor for whatever reason, and such assignment shall operate as full accord and satisfaction of any remaining debt to Subcontractor by Contractor for work performed in accordance with the Subcontract. Subcontractor hereby agrees to accept such assignment in lieu of any other form of payment for its work, and to release and discharge any and all claims for those funds against Contractor upon receipt of such

Subcontractor Initial_____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

assignment. Contractor reserves the right to joint check material and equipment suppliers as well as any sub-subcontractors of this Subcontractor, if deemed necessary from Contractor's reasonable assessment after review of Subcontractor's credit references or if the suppliers and/or sub-subcontractors give notification/ reason to Contractor that Subcontractor is delinquent in or not paying bills due.

12. **FINAL PAYMENT:** Contractor shall make final payment to Subcontractor after the work is completed and accepted by Owner and/or the Project Architect or Engineer, providing like payment shall have been made by Owner to Contractor, and further providing that all other terms and conditions of payment have been satisfied, and Subcontractor shall have furnished Contractor with a waiver and release of lien executed by Subcontractor, and waivers and release of liens executed by Subcontractor's subcontractors and/or suppliers, or other satisfactory evidence that all labor and material accounts incurred by Subcontractor in connection with the sublet work have been paid in full. The meaning of the provisions of the Prime Contract, as it may be determined by any final judgment or award in or settlement of litigation or arbitration between Owner and Contractor will control with respect to measurement, quantities and payment, including payment for extras, changes and variations in plans and size conditions. Upon receipt of final payment, Subcontractor agrees that neither he nor his subcontractors, suppliers or mechanics or anyone claiming under them shall have any lien upon the sublet work, the Project, or the improvements, property or premises on which the work is performed, and Subcontractor hereby waives on behalf of himself and his subcontractors, suppliers and mechanics and those claiming under them, all right to any such lien. Subcontractor agrees to indemnify Contractor and Owner against all lien claims and bond claims, including expenses, costs of bonds to remove liens, and attorneys' fees related to such claims, which may be asserted by mechanics, materialmen, suppliers or subcontractors of Subcontractor or of his subcontractors and suppliers or anyone claiming under one of them. Subcontractor also agrees that if liens are placed on the work or the Project or the improvements, property or premises on which the work is performed, he will immediately obtain and record in the real property records of the county such bond which is necessary to remove such lien. If bond claims and/or lien claims are filed by any subcontractors, materialmen, suppliers or mechanics of Subcontractor, Contractor may suspend payments to Subcontractor and either hold money due Subcontractor or make payments directly to the claimants and charge the payments against sums allegedly due Subcontractor, without prejudice to any payment bond furnished by Subcontractor. It is the intent of the parties that any payment bond furnished by Subcontractor be for the benefit of Contractor and Owner, and not for the benefit of third parties except to the extent necessary to protect Contractor and Owner.

13. **PERFORMANCE:** Subcontractor agrees to perform the sublet work in a careful, good and workmanlike manner in accordance with the best construction practices and with this subcontract, and in strict accordance with the Prime Contract, and to assume and discharge all responsibilities which Contractor has assumed under the Prime Contract with respect to the sublet work, except as otherwise provided herein. Subcontractor agrees to procure materials and supplies in advance and to provide sufficient men, equipment and supervision to ensure that the sublet work will be prosecuted diligently and coordinated with other work at the site and completed within the time allotted and in accordance with the requirements of the Prime Contract. Subcontractor has satisfied himself, by his own investigation and research, regarding all conditions affecting the work to be done and materials to be furnished, and as to the meaning and intention of the Prime Contract. Subcontractor acknowledges and agrees that safety violations shall be grounds for termination for cause hereunder. Subcontractor is aware that overtime may be necessary, at Subcontractor's expense, if Subcontractor's lack of progress is apparent to Contractor, in Contractor's reasonable judgment, as insufficient to allow Subcontractor's completion of the work within the agreed scheduled duration of time. If required by the Contractor, Subcontractor will provide a detailed manpower schedule showing that adequate manpower is being furnished.

14. **APPROVAL AND PROGRESS DATA:** Subcontractor shall carefully examine specification requirements for approval material to be submitted such as shop drawings, data schedules, samples, etc., and then he shall submit such material at his own expense and in such form required by the Prime Contract in sufficient time to prevent any delay in the delivery of such materials and the installation thereof. "In-place" or "as-built" drawings shall be prepared and submitted to Contractor as a condition of final payment. Subcontractor shall complete and submit to Contractor if required, on a daily basis, a daily progress report form which will be furnished to Subcontractor by Contractor.

15. **COMMENCEMENT AND COMPLETION OF THE WORK:** Time is of the essence of this subcontract. Subcontractor agrees to supply materials, labor and equipment as necessary to commence his sublet work when directed by Contractor. He shall diligently pursue the completion of his sublet work and coordinate his sublet work with that being done on the project by Contractor and other trades so that his sublet work and the work of others shall not be delayed or impaired by any act or omission of an act by Subcontractor. Contractor shall have the right to decide the time and order in which the various portions of the work shall be undertaken or completed or the priority of the work of other subcontractors, and, in general, all matters representing the timely and orderly conduct of the sublet work of Subcontractor on the premises. Contractor may prepare a coordinated progress schedule, and if he does so, Subcontractor shall be required to perform his work in accordance with such schedule, and it may be modified by Contractor as work progresses and Contractor shall have no liability for damages, including, but not limited to overhead, extra costs, or increases in prices arising out of changes in the schedule. If the Subcontractor fails to timely perform its work in accordance with the current progress schedule of the Contractor, Subcontractor shall be liable to the Contractor for all damages occasioned by such failure, including but not limited to any liquidated damages for delay provided for in the Prime Contract. Further, in such event, Contractor may immediately terminate this agreement. Contractor shall not be liable to the Subcontractor for any claims, including but not limited to damages, increased costs, or an increase in the contract sum as the result of any delay to the Subcontractor's work resulting from the act, negligence or default of the Owner or the Project Architect

Subcontractor Initial_____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

or Engineer, or any other consultants or contractors of Owner, or by reason of fire or other casualty, or on account of risks, strikes, or other combined action of the workmen or others, or on account of any acts of God or any cause beyond the Contractor's control, or on account of any circumstance caused or contributed to by the Subcontractor. If the Contractor should delay the Subcontractor's work, then and in such event, Contractor shall owe the Subcontractor only an extension of time for completion equal to the delay caused and then only if written claim for delay is made to the Contractor not later than two (2) days from the beginning of the delay and such extension of time shall be Subcontractor's sole and exclusive remedy for such delay. Subcontractor shall perform his scope of work set forth in the time frame established by Contractor's Schedule.

16. **CHANGES IN THE WORK:** Should Contractor, at any time during the progress of the work, request any changes in or additions or reductions to the scope of the sublet work in this subcontract, he shall have the right and power to make such changes, additions or reductions, and Subcontractor shall promptly proceed with such changes, additions or reductions as directed in writing by Contractor, and any appropriate adjustment of Subcontract Amount may be made by written Change Order. If Subcontractor believes that any such change or addition entitles Subcontractor to an increase of the Subcontract Amount, Subcontractor shall, within a reasonable time not to exceed three (3) working days thereafter, submit an itemized claim to Contractor reflecting any cost increases as a result of such change or addition. Failure to provide such a claim within the specified time frame shall waive any and all of Subcontractor's rights to additional costs or time increases associated with the change. If requested by the Contractor, Subcontractor shall within three (3) working days submit a reasonable, itemized price quotation for any proposed changes. If the Subcontractor does not and the Contractor is required to submit a price quotation to the Owner which includes the subcontract change, Contractor shall use its best estimate of the proposed change, as it affects the Subcontractor in its quotation to the Owner, which estimate shall be the maximum equitable adjustment due to the Subcontractor. It is expressly understood and agreed, regardless of any changes in or additions to the scope of the work, that no changes shall be made in the Subcontract Amount or the time of completion, except by a subcontract Change Order issued by Contractor and then only when such order sets forth the amount of any addition or deduction and is signed by both parties thereto. If Subcontractor initiates a substitution, deviation or change in the work which affects the scope of the work or the sublet work or causes costs or expenses to Contractor, Subcontractor shall be liable for all costs and expenses thereof. Any change order which reduces the scope of the Subcontractors work need not to be signed by the Subcontractor if submitted by the Contractor prior to the actual performance of the work by the Subcontractor.

17. **CLEANUP:** Subcontractor acknowledges that the execution of his work will result in an indeterminate amount of debris, waste and trash, and Subcontractor agrees to retrieve, pick up and remove from the job site all such debris, waste and trash, during the course of his work and on final completion of his work. Disposal of debris, waste and trash shall be done on a day-to-day basis as is determined necessary by Contractor. If after 24 hours' notice by Contractor's representative to Subcontractor's representative at the job site, Subcontractor has not diligently proceeded with the cleanup as outlined in this paragraph, then the Contractor has the right to proceed with the cleanup work with his own labor at Subcontractor's expense. Subcontractor shall provide regular cleanup at the Project Superintendent's request.

18. **PERMITS:** All permits (except Contractor's main building permit), licenses, tap fees and easements necessary for the prosecution of the sublet work shall be procured and paid for by Subcontractor. Subcontractor shall give all notices and comply with all laws, ordinances, rules and regulations bearing on the conduct of the work as drawn and specified. If Subcontractor observes that plans and specifications are at variance with applicable, laws, ordinances, rules and regulations, or are at variance with actual conditions, he shall promptly notify Contractor in writing, and if Subcontractor performs any work contrary to such actual conditions, laws, ordinances, rules and regulations without such notice to Contractor, he shall bear all costs arising there from.

19. **LAYOUT RESPONSIBILITY:** Contractor shall establish principal axis lines and levels whereupon Subcontractor shall lay out, and Subcontractor shall be strictly responsible for the accuracy of his work and for any loss or damage to other contractors engaged in work on the site by reason of failure of Subcontractor to set out or perform his work correctly. Subcontractor shall exercise prudence so that actual final conditions and details shall result in perfect alignment of finished surfaces. All specified methods and materials will be requisite. Subcontractor shall be responsible for correct and accurate layout and placement of the work, based upon basic control points or lines established by Contractor.

20. **SUB-SUBCONTRACTOR:** Subcontractor must submit to Contractor for approval all his proposed subcontractors and sub-subcontractors, and Contractor may reject any proposed subcontractor or sub-subcontractor. Approval of a subcontractor or sub-subcontractor will not imply that Contractor assumes any responsibility for such subcontractor or sub-subcontractor, or that Subcontractor is relieved of any responsibility with respect to the sublet work. Before final payment will be made, Subcontractor shall furnish Contractor a list of all of subcontractors, sub-subcontractors and suppliers who furnished any labor or materials for the work, in the form attached hereto as Exhibit "D" and incorporated herein.

21. **DEFECTIVE WORK AND CLAIMS:** No payment made under this subcontract shall be construed to be an acceptance of defective or non-conforming work, improper materials, or quantities of materials. Payments otherwise due may be withheld by Contractor on account of defective work not remedied, claims filed, evidence indicating probability of filing of claims, failure of Subcontractor to make payments properly to its subcontractors of for material, equipment or labor, failure of Subcontractor to provide sufficient labor, materials or equipment or otherwise comply with the schedule for the work, failure of Subcontractor to abide by the terms of this subcontract, or a reasonable doubt that the subcontract can be completed for the Subcontract Amount

Subcontractor Initial_____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

balance then unpaid. If the said causes are not removed, within 48 hours after the date of written notice from Contractor, Contractor may rectify the same at Subcontractor's expense. Contractor may offset against any sums due Subcontractor hereunder the amount of any liquidated or unliquidated obligation of Subcontractor to Contractor, whether or not arising out of this subcontract. Subcontractor agrees to be bound by all the provisions of the Prime Contract, including but not limited to, provisions relating to quantities, measurement and payment, change orders, extra work, variations in plans and/or site conditions, time extensions and claims. Subcontractor agrees that it will present Contractor with written notice of any event or claim for which it seeks compensation within forty-eight hours of the event occurrence, so that Contractor can review and mitigate the impacts. Subcontractor's failure to comply with this notice requirement shall constitute a waiver and release by Subcontractor of any and all rights to pursue a claim for time or costs. Contractor agrees that it will present to Owner any reasonable claim for payment or time extension which Subcontractor in good faith chooses to submit, provided that Subcontractor prepares all notices in a proper manner sufficiently in advance of the time of notice to permit Contractor to submit the notice to Owner in accordance with the requirements of the Prime Contract, and Subcontractor prepares the documentation required, and complies with all other requirements of the Prime Contract, and does all things necessary to enable Contractor to present Subcontractor's claims. Contractor agrees to reasonably cooperate with Subcontractor in presenting Subcontractor's claims, and Subcontractor agrees to cooperate with Contractor and all other subcontractors of Contractor in presenting all claims. Contractor’s receipt of payment or any time extension from Owner shall be a condition precedent to any obligation of Contractor to Subcontractor with respect to any such claims presented, and Subcontractor may not recover more from Contractor than the amount or relief which Contractor recovers from Owner with respect to any Subcontractor claim. Subcontractor agrees to be bound by the terms of the Prime Contract with respect to any and all claims. All claims which Subcontractor has or wishes to assert against Contractor must be presented in writing to Contractor not later than two (2) days after Subcontractor is aware or should be aware that a claim will or does exist, or such longer time as may be required by law, even though the exact nature of the claim and the amount of the claim may not be determinable at that time. The exact nature of the claim and the amount of the claim must be presented to Contractor in writing as soon thereafter as Subcontractor has or should have such information. Subcontractor hereby waives all claims not presented as provided herein. Any default by Subcontractor under this Subcontract shall constitute a default under any other subcontract or agreement between Subcontractor and Contractor. Similarly, any default by Subcontractor under any other subcontract or agreement with Contractor shall constitute a default under this Subcontract, entitling Contractor to exercise any and all remedies available under this Subcontract, including but not limited to termination, withholding of payment, and pursuit of damages.

22. **INDEMNIFICATION, INSURANCE AND BONDS:**

A. EXCEPT WITH RESPECT TO CLAIMS RELATING TO BODILY INJURY OR DEATH OF AN EMPLOYEE AS DEFINED IN THE PARAGRAPH BELOW, TO THE FULLEST EXTENT PERMITTED BY LAW, SUBCONTRACTOR AGREES TO AND SHALL DEFEND, INDEMNIFY AND HOLD HARMLESS (COLLECTIVELY “INDEMNIFY”) CONTRACTOR, ITS PARTNERS, MEMBERS, DIRECTORS, OFFICERS, AGENTS, AND EMPLOYEES, AND ANY PARTIES REQUIRED TO BE INDEMNIFIED BY CONTRACTOR UNDER THE PRIME CONTRACT (COLLECTIVELY THE “INDEMNIFIED PARTIES” OR INDIVIDUALLY AN “INDEMNIFIED PARTY”) FROM AND AGAINST ANY AND ALL CLAIMS, LOSSES, DAMAGES, DEMANDS, INJURIES, JUDGEMENTS, CAUSES OF ACTION, SUITS, AND LIABILITY OF EVERY KIND, INCLUDING BUT NOT LIMITED TO ALL EXPENSES OF LITIGATION, COURT COSTS AND ATTORNEY’S FEES (COLLECTIVELY “CLAIMS”), FOR LOSSES OR DAMAGES, OR FOR BODILY OR PERSONAL INJURIES, INCLUDING DEATH, TO ANY PERSON, OR DAMAGES TO OR DESTRUCTION OF PROPERTY, INCLUDING THE LOSS OF USE THEREOF, ACTUALLY OR ALLEGEDLY OCCASIONED BY, CONTRIBUTED TO OR ARISING OUT OF, IN WHOLE OR IN PART, THE WORK, THE PERFORMANCE OF THE WORK, OR THIS AGREEMENT, INCLUDING BUT NOT LIMITED TO CLAIMS OCCASIONED BY, CONTRIBUTED TO OR ARISING OUT OF, IN WHOLE OR IN PART, THE NEGLIGENCE, GROSS NEGLIGENCE, BREACH OF WARRANTY, BREACH OF CONTRACT, VIOLATION OF ANY STATUTE, RULE OR REGULATION OR OTHER ACT OR OMISSION BY SUBCONTRACTOR, ITS EMPLOYEES, AGENTS OR ANY SUBCONTRACTOR OF SUBCONTRACTOR OF ANY TIER, OR THEIR RESPECTIVE AGENTS OR EMPLOYEES, OR ANY OTHER PARTY FOR WHOSE ACTS SUBCONTRACTOR IS LIABLE. NOTWITHSTANDING THE FOREGOING, IF SUBCHAPTER C OF CHAPTER 151 OF THE TEXAS INSURANCE CODE APPLIES TO THIS AGREEMENT, THIS INDEMNITY PROVISION SHALL NOT APPLY TO THE EXTENT THAT IT REQUIRES SUBCONTRACTOR TO INDEMNIFY AN INDEMNIFIED PARTY AGAINST A CLAIM CAUSED BY THE NEGLIGENCE OR FAULT, THE BREACH OR VIOLATION OF A STATUTE, ORDINANCE, GOVERNMENTAL REGULATION, STANDARD, OR RULE, OR THE BREACH OF CONTRACT OF THE INDEMNIFIED PARTY, ITS AGENT OR EMPLOYEE OR ANY THIRD PARTY UNDER THE CONTROL OR SUPERVISION OF THE INDEMNIFIED PARTY, OTHER THAN SUBCONTRACTOR OR ITS AGENT, EMPLOYEE OR SUBCONTRACTOR OF ANY TIER.

B. **INDEMNITY FOR EMPLOYEE CLAIMS**: SUBCONTRACTOR AGREES TO AND SHALL DEFEND, INDEMNIFY AND HOLD HARMLESS (COLLECTIVELY “INDEMNIFY”) CONTRACTOR, OWNER AND ANY OTHER PARTIES REQUIRED TO BE INDEMNIFIED BY CONTRACTOR UNDER THE PRIME CONTRACT AND THEIR REPRESENTATIVES, PARTNERS, MEMBERS, DIRECTORS, OFFICERS, AGENTS, EMPLOYEES, INVITEES OR LICENSEES (COLLECTIVELY THE “INDEMNIFIED PARTIES” OR INDIVIDUALLY AN “INDEMNIFIED PARTY”) FROM AND AGAINST ANY AND ALL CLAIMS, LOSSES, DAMAGES, DEMANDS, INJURIES, JUDGEMENTS, CAUSES OF ACTION, SUITS, AND LIABILITY OF EVERY KIND, INCLUDING BUT NOT LIMITED TO ALL EXPENSES OF

Subcontractor Initial_____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

LITIGATION, COURT COSTS AND ATTORNEY'S FEES (COLLECTIVELY "CLAIMS"), FOR BODILY INJURY OR DEATH OF ANY EMPLOYEE OF SUBCONTRACTOR, ITS AGENTS, OR ITS SUBCONTRACTORS OF ANY TIER (COLLECTIVELY "EMPLOYEE" FOR THE PURPOSE OF THIS SECTION), ACTUALLY OR ALLEGEDLY OCCASIONED BY, CONTRIBUTED TO OR ARISING OUT OF, IN WHOLE OR IN PART, THE WORK, THE PERFORMANCE OF THE WORK OR THIS AGREEMENT, INCLUDING BUT NOT LIMITED TO CLAIMS DUE TO NEGLIGENCE, GROSS NEGLIGENCE, BREACH OF WARRANTY, BREACH OF CONTRACT, VIOLATION OF ANY STATUTE, RULE OR REGULATION OR OTHER ACT OR OMISSION BY SUBCONTRACTOR, ITS EMPLOYEES, AGENTS OR ANY SUBCONTRACTOR OF SUBCONTRACTOR OF ANY TIER, OR THEIR RESPECTIVE AGENTS OR EMPLOYEES, OR ANY OTHER PARTY FOR WHOSE ACTS SUBCONTRACTOR IS LIABLE. SUBCONTRACTOR'S OBLIGATION TO INDEMNIFY SHALL APPLY EVEN IF SUCH CLAIMS ARE ACTUALLY OR ALLEGEDLY CAUSED IN WHOLE OR IN PART BY THE STRICT LIABILITY OR THE ACTS, OMISSIONS, OR NEGLIGENCE OF AN INDEMNIFIED PARTY, EVEN IF SUCH NEGLIGENCE OR OTHER ACTS OR OMISSIONS ARE ACTIVE OR PASSIVE, DIRECT OR INDIRECT, SOLE OR CONCURRENT. THIS INDEMNITY AGREEMENT IS INTENDED TO INDEMNIFY THE AFOREMENTIONED INDEMNIFIED PARTIES FROM THE CONSEQUENCES OF THEIR OWN NEGLIGENCE, AS PROVIDED ABOVE.

C. The indemnities provided by the Subcontractor under this paragraph 22 shall be in addition to and not in substitution for any other indemnity required to be provided by the Subcontractor contained in this Agreement and is not limited to but is in addition to the insurance required to be obtained by the Subcontractor under this Agreement. The defense and indemnification obligations under this Subcontract shall not be restricted in any way by any limitation on the amount or type of damages, compensation or benefits payable by or for the Subcontractor under any workers' compensation act, disability benefit act, or other employee benefit act, and shall extend to and include any actions brought by or in the name of any employee of the Subcontractor or of any third party to whom the Subcontractor may subcontract a part of all of the Subcontract Work. These indemnity obligations shall survive termination of this Subcontract.

D. See Exhibit "C", incorporated herein fully by reference, for insurance requirements.

E. In addition to any other insurance which Subcontractor may be required or choose to carry, Subcontractor at his sole expense shall maintain in effect the insurance coverage which is required under the Subcontract Documents with insurance companies acceptable to Contractor. Certificate(s) of insurance stating the limits and coverage required by Contractor shall be executed by Subcontractor's insurance carrier(s) as required by Exhibit C to this agreement. Until said certificate(s) of insurance is properly executed by insurance carrier(s) acceptable to Contractor and delivered to Contractor, the Subcontractor may not enter the Project to perform any portion of the sublet work. The cancellation either by the insured or the insurer of any portion of the insurance required to be carried by Subcontractor by this subcontract, or the lapse or suspension of the required insurance for any reason shall be considered a material breach of this subcontract by Subcontractor, and Contractor shall be entitled to exercise the termination rights set forth in paragraph 24 hereof and any other right contained in this subcontract and shall have the right to prohibit Subcontractor from entering the project.

F. Subcontractor shall cause his subcontractors to procure insurance covering the liabilities set out in Exhibit "C" under policies which, in form, and amounts are acceptable to Contractor, and Subcontractor will obtain said policies or certificates therefore, and deliver them to Contractor if requested to do so by Contractor. If acceptable insurance is not acquired by Subcontractor, the Contractor may acquire such insurance coverage and charge the expenses for such coverage to Subcontractor and deduct them from any sum due Subcontractor under this Agreement.

G. Subcontractor is fully responsible for all loss or damage to materials delivered and stored on the job site until such materials are actually installed and/or incorporated into the Project.

H. Performance and payment bond: Subcontractor shall provide performance and payment bonds if required by Contractor, on a form acceptable to Contractor, prescribed by and with a surety acceptable to Contractor in the full amount of this subcontract, for the faithful performance of this subcontract and the payment of all claims for labor, materials and/or equipment furnished under this subcontract. The premium for bonds shall be reimbursed to the Subcontractor by Contractor.

I. In addition to the foregoing insurance certificates, TEXAS WORKER'S COMPENSATION COMMISSION 85 FORM is attached hereto as Exhibit "E" and enclosed for your signature and must be returned with your signed Subcontract.

J. Subcontractor shall defend, indemnify and save harmless Contractor and Owner from any and all laborer's, material men's and mechanic's liens upon the Project and the property and premises on which the Subcontractor Work is being performed that arise out of the sublet work, and shall keep such property and improvements free and clear of all liens, claims and encumbrances arising out of the performance of this Subcontract, and Subcontractor shall defend, indemnify and save harmless Contractor and its surety from any such liens or claims or causes of action asserted against Contractor's surety bonds issued in connection with the Project, if any. Subcontractor shall defend, indemnify and save harmless Contractor and Owner from any claims or suits for infringement or violation of patents or patent rights by Subcontractor. If a lien is filed on the Project by one of Subcontractor's suppliers or sub-subcontractors, Subcontractor shall, within seven (7) days notice from Contractor, cause the lien to be removed or bonded around If Subcontractor fails to do any of the foregoing, Contractor may deduct from sums then or thereafter due

Subcontractor Initial_____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

Subcontractor under this Subcontract or other agreement with Contractor such amounts as Contractor may deem appropriate to defend, indemnify and save harmless Contractor and Owner from such liens, claim, encumbrances and suits.

23. **GUARANTY:** Subcontractor shall, before requesting final payment, provide any and all guaranties and warranties required by the Subcontract Documents. In addition to any specific guaranty required by the Subcontract Documents, Subcontractor, in signing this subcontract, agrees at his own expense to replace or repair any faulty or defective or non-conforming material or workmanship within ONE (1) YEAR from the date of substantial completion of the Project, or Owner's beneficial occupancy, whichever occurs later or such longer period, if stated in the Prime Contract. In addition, Subcontractor shall be responsible and pay for replacement or repair of adjacent materials or work or property which may be damaged due to the failure of Subcontractor's material or work and/or damaged as a result of the replacement or repairs thereof. This correction period shall apply solely to Subcontractor's duty to repair or replace any faulty or defective or non-conforming material or workmanship and shall not be construed as a period of limitation with respect to Contractor's other rights and remedies arising out of or related to this Subcontract.

24. **TERMINATION FOR CONVENIENCE:** Contractor has the right to terminate this subcontract in whole or in part at any time for Contractor's convenience by giving a written notice of termination to Subcontractor. In such event, Subcontractor may claim only properly documented out-of-pocket, direct termination costs plus payment of any amount due for the work already performed to the date of termination in accordance with the Subcontract Documents, and any such payment shall constitute Subcontractor's sole and exclusive remedy in the event of a termination for convenience. Under no circumstances shall Subcontractor be entitled to any unrecovered overhead or loss of anticipated profits on work not performed, and under no circumstances shall the cumulative amount of any payment due Subcontractor in the event of a termination for convenience and all previous payments to Subcontractor under the subcontract exceed the Subcontract Amount. Upon Contractor's written request, any specially fabricated materials or specially prepared products unique to this subcontract, any partially completed work or work in progress, or raw materials, or any equipment to be incorporated in the Project, shall be held by Subcontractor for disposition in accordance with Contractors written instruction. Notwithstanding the foregoing, Contractor reserves the right to terminate all or any part of the undelivered or uncompleted portion of this subcontract in accordance with paragraph 25 below, without liability, in addition to Contractor's other rights and remedies, if Subcontractor breaches any of the terms and conditions herein.

25. **FAILURE TO PERFORM:** Should Subcontractor at any time fail to supply a sufficient number of skilled workmen, or a sufficient quantity of equipment or materials of proper quality, or fail in any respect to prosecute the work covered by this subcontract with promptness and diligence, or fail to perform work of the quality required by the Subcontract Documents, or fail to promptly correct defective or nonconforming work, or fail to comply with all applicable laws, codes, ordinances and regulations, or fail in the performance of any of the agreements herein contained, or should any workmen performing work covered by this subcontract engage in a strike or other stoppage, or cease to work due to picketing or other such activity, such event shall constitute an event of default under this subcontract, and Contractor may, in any of such events at its option, after forty-eight hours written notice to Subcontractor, provide any such labor and materials, and deduct the cost thereof from any money then due or thereafter to become due Subcontractor, or, in any of such events, Contractor, may, at its option, a n d without forty-eight hours written notice, terminate the employment of Subcontractor for all or part of the work under this subcontract, and shall have the right to enter upon the Project premises and take possession, for the purpose of completing the work hereunder, of all the materials, tools, facilities, appliances and equipment thereon, and to finish the work and provide the materials, therefore, either with its own employees or other subcontractors; and in case of such discontinuance of the employment by Contractor, Subcontractor shall not be entitled to receive any further payments under this subcontract or otherwise, but shall nevertheless remain liable for any damages which Contractor incurs. If the expenses incurred by Contractor in completing the work shall exceed the unpaid balance, Subcontractor shall pay the difference to Contractor, along with any and all other damages and attorneys' fees incurred by Contractor as a result of Subcontractor's default. Contractor shall have a lien upon all materials, tools, facilities, appliances and equipment taken possession of to secure the payment hereof. Subcontractor shall be liable to Contractor for all costs and damages incurred by Contractor due to the default or failure of performance by Subcontractor, including but not limited to the failure of Subcontractor to keep the progress of work up to that of Contractor or other trades, or the failure to execute its work as directed by Contractor. In the event of any termination for default, Subcontractor agrees to execute any assignment necessary to make available to Contractor and the Owner the rights of Subcontractor under all purchase orders and subcontracts related to the sublet work. Contractor will credit Subcontractor's account with the value of the materials and supplies so used, but there will be no credit for rent on equipment. Subcontractor will reimburse Contractor in Harris County, Texas, promptly and within no more than ten (10) days from the date of Contractor's demand, to the extent that Contractor's damages and expenses, including attorney's fees, in completing the sublet work and proceeding under this article exceeds the balance which would have become due to Subcontractor under this subcontract had Subcontractor completed the sublet work in accordance with the Subcontract Documents. If Contractor's damages and expenses, including but not limited to attorneys' fees incurred, is less than such amount, then Contractor will pay the difference to Subcontractor. Subcontractor hereby waives all claims against Contractor for profits, rent or equipment or other damages related to any proceeding which Contractor institutes under this article. The parties agree that any determination by Contractor as to the adequacy of Subcontractor's performance are difficult to make and must be made under pressing circumstances, and Subcontractor agrees to be bound in accordance with this article by the Contractor's discretion in light of the circumstances confronting Contractor at the time such a decision is made. If any termination by Contractor for default under this paragraph 25 is found by any arbitrator(s) or court to be wrongful or otherwise improper, such termination shall be deemed a termination for convenience under paragraph 24 above, and Subcontractor's sole and exclusive remedy for such termination shall be the payments provided for in paragraph 24 above.

Subcontractor Initial_____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

26. **BANKRUPTCY:** If all or substantially all of Subcontractor's assets are placed in the hands of a receiver or trustee, or if Subcontractor makes an assignment for the benefit of creditors, or is adjudicated a bankrupt, or if Subcontractor institutes any proceedings under the bankruptcy act or any amendment thereto or under any other act relating to the subject of bankruptcy wherein Subcontractor seeks to be adjudicated a bankrupt, or to be discharged of its debts, or to effect a plan of liquidation, composition, or reorganization, or should any involuntary proceeding be filed against subcontractor under any such law and the Subcontractor consents thereto or acquiesces therein by pleading or default, or if Contractor is served with a U.S. Tax Levy seeking to reach assets of Subcontractor, then Contractor shall have the right, in addition to any other right or remedy under this subcontract or by law, including, but not limited to, the right to withhold payment from the Subcontractor, to request of Subcontractor or its successors, trustees or receivers, adequate assurances of future performance. In the event such adequate assurances are not given to the reasonable satisfaction of Contractor within seventy-two (72) hours of such request, Contractor shall have the right to immediately terminate this subcontract. Pending receipt of such adequate assurances of such future performance, Contractor may proceed with the sublet work on a temporary basis and deduct the costs, plus reasonable overhead and profit, from any amounts due or which may become due to Subcontractor under the subcontract or any other agreement with Contractor. In this regard, Contractor and Subcontractor agree that delays in performance could result in more damages to Subcontractor than would be sustained if Contractor failed to exercise such remedies. If the subcontract is so terminated, the parties' rights and recoveries shall be as provided in paragraph 24 above. Regardless whether Contractor elects to terminate this subcontract or pursue other rights, it is agreed that upon the happening of any of the foregoing events, Contractor may withhold payment from Subcontractor and offset against any payment otherwise due Subcontractor hereunder amounts sufficient to reimburse Contractor for sums which Subcontractor owes or will owe Contractor under this subcontract.

27. **COMPLIANCE WITH LAWS:** Subcontractor agrees to comply, at his own expense, with all laws and regulations applicable to the work covered by the Subcontract Documents, including but not limited to the Occupational Safety and Health Act of 1970 (Public Law 91-596); Construction Safety Act (Public Law 91-54); the Immigration Reform and Control Act of 1986, and the Civil Rights Act of 1970, as amended, including rules and regulations promulgated there under and including executive order 11246 and any successor executive order modifying or superseding that order; and Subcontractor agrees to save and hold harmless the Contractor from any and all liability and damages, fines, costs, and attorney's fees incurred by Contractor on account of Subcontractor's failure to comply with all laws and governmental regulations applicable to the work. Subcontractor agrees to not remove guards or safety appliances, except on authority of Contractor's superintendent, and to replace such guards and appliances promptly. Failure to make such replacement will authorize Contractor to do such work and charge the costs thereof to Subcontractor.

28. **TAXES:** Subcontractor will pay all social security and other taxes imposed upon him as an employer in connection with the performance of his subcontract, and will furnish evidence, when required by Contractor, showing that all such payments required to be made have been paid. Subcontractor shall pay all local, state and federal taxes in connection with this work, including, but not limited to, any sales tax or value added tax.

29. **GOVERNING LAW:** Except as otherwise provided herein, this subcontract shall be governed by the Law of the State of Texas, and the venue for any arbitration or litigation proceeding between Contractor and Subcontractor arising out of or related to this subcontract or any alleged breach hereof shall be in Harris County, Texas.

30. **ARBITRATION:** All controversies, claims or disputes between the Contractor and the Subcontractor arising out of, or relating to, the sublet work, this subcontract or the breach thereof shall be settled by arbitration in accordance with the construction industry arbitration rules of the American Arbitration Association then effective, unless the parties mutually agree otherwise. Notice of the demand of arbitration shall be filed in writing with the other party to the subcontract and with the American Arbitration Association and shall be made within a reasonable time after the dispute has arisen, not to exceed the period of any otherwise applicable statute of limitations. The award rendered by the arbitrators shall be final and binding, and judgment may be entered upon it in accordance with applicable law in any court having jurisdiction thereof. No arbitration rising out of or relating to this subcontract shall include, by consolidation, joinder or any other manner, any person or entity not a party to the agreement under which such arbitration arises, unless it is shown at the time the demand for arbitration is filed that (1) such person or entity is substantially involved in a common question of fact or law, or (2) the presence of such person or entity is required if complete relief is to be accorded in the arbitration, and the person or entity sought to be joined has given their written consent to be joined. The agreement herein among the parties to the agreement and any other written agreement to arbitrate referred to herein shall be specifically enforceable under the Federal Arbitration Act. Notwithstanding the foregoing or anything herein to the contrary, if Contractor is a party to a litigation or arbitration proceeding with the Owner, all or part of which arises out of or relates to the work, the performance of the work, or this subcontract, Subcontractor shall, upon Contractor's written request, join as a party to such arbitration or litigation proceeding. The Contractor shall be fully compensated for the cost of its in pursuing all controversies, claims, or disputes against Subcontractor, including the reasonable cost incurred for attorneys', consultants', and experts' fees.

31. **FUTURE RIGHTS:** Any waiver or failure to assert any right which either party has under this subcontract shall not constitute a continuing waiver of future rights. Rights can be waived only if expressed in writing signed by the waiving party. If any provision

Subcontractor Initial_____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

of this subcontract is held invalid or unenforceable under any present or future laws, then such invalid or unenforceable provision shall be severed from this subcontract, and the remainder of the subcontract shall remain in full force and effect.

32. **NOTICES:** Any notice required or permitted to be given hereunder, by one party to the other party shall be in writing and the same shall be given and shall be deemed to have been served and given if delivered in person to the address set forth on page 1 of the Subcontract, or placed in the United States Mail, postage prepaid, registered or certified, with return receipt requested, addressed to the party at the address set forth on page 1 of the Subcontract.

Subcontractor Initial_____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

EXHIBIT "B"

INSTRUCTIONS FOR INVOICING AND COMPLETION OF THE APPLICATION FOR PAYMENT FORM

1. Invoices shall be submitted with the following information:

   a. Subcontract Number must appear on the Invoice, (Reference Subcontract).
   b. Invoice Number.
   c. Date of Invoice.
   d. Detailed description of work completed (Referencing Cost Code if provided under Subcontract).
   e. The Gross amount of the Invoice, to include Retainage. The Retainage will be shown on the Application for Payment.

2. Each line of Application for Payment (Exhibit B, Page 2) must be filled out. If each line is not filled out, it will be returned to Subcontractor for corrections/completion. Subcontractor must submit a complete Schedule of Values (equal to the subcontract amount indicated on page 1 of the Subcontract) to be approved by Contractor on the Continuation Sheet (Exhibit B, Page 3) at time of Subcontract execution, and each month thereafter to include percentages billed by line item for the period work was performed.

3. Invoices, along with the Application for Payment and Continuation Sheet, shall be given to the Contractor on or before the Texas – 15th day of each month. If not received by 5:00 PM of the Texas – 15th day of the month, **it will not be entered and paid until the following month.**

4. Faxed or emailed copies of Invoices and Applications for Payment will be accepted. The originals are to be mailed and/or received by Contractor, no later than five (5) days after the copy is received. **This Document must be signed and notarized prior to submission to Arch-Con for payment. Original Applications for Payment must include original notarized signatures.**

5. Payment may be made to Arch-Con by the project lender's funds disbursement company. If so, payment shall be made to Subcontractor within 10 days after Contractor receives payment from the project lender, subject to all other terms and conditions of payment of this Subcontract.

6. Arch-Con reserves the right to require Subcontractor's and its subcontractors'/suppliers' execution of a joint check agreement when deemed necessary, and/or the right to issue joint checks to Subcontractor and its subcontractors/suppliers. If Subcontractor is deemed to be a "Joint Check" vendor for purposes of this Subcontract, Subcontractor shall provide a complete Supplier/2nd tier Subcontractor listing with EVERY application for payment to include name, contact information, and balances due, so Contractor may independently confirm balances and issue joint checks accordingly.

7. **When multiple cost codes (which may reflect different scopes of work or amendments) are listed within the Subcontract Agreement, Arch-Con shall require that Subcontractor submit invoices referencing scope of work, cost code and Request for Payment. Failure to do so will result in a delay of payment.**

Subcontractor Initial_____

Application For Payment

Note: Payment CANNOT be issued without a fully excuted subcontract on file with Arch-Con Corporation.
HANDWRITTEN FORMS ARE NOT ACCEPTED. FORMS MUST BE TYPED.

Job Number: _____ Cost Code #: _____

Job Name: _____ Date: _____ Subcontract #: _____

Application #: _____ Period Ending: _____ Master Agreement #: _____

Subcontract's Name And Address:

Remit Application To:
The Arch-Con Corporation
1335 West Gray, Suite 300
Houston, TX 77019

1. Original Contract Amount		$0.00
2. "Approved" Changes to the Subcontract		$0.00
3. Adjusted Contract Amount (Line1+ Line2)		$0.00
4. Total Value of Work Completed and Materi	#DIV/0!	entage Complete $0.00
5. (Less) Retainage	10%	$0.00
6. TOTAL EARNED LESS RETAINA	4 - Lin	$0.00
7. (Less) Previous Certificates for payment	from pr	certificate) $0.00
8. Current Payment Due (Lin	e 7)	$0.00
9. Balance to Finish, Plus Reta	ne 3 -	$0.00

CERTIFICATION OF PAY APPLI ON:

The undersigned Subcontra t to the best of Subcontractor's k ledge, inf tion and belief, the work covered by thi lication for ent has been completed in accorda th ntract uments, that all amounts have bee Contr tor for work for which previous Certificates ent issued and payments rec from the Contr current payment show is now due.

AP Re w:	Initial:
☐ ed for Paym t	
☐ In Contr ount	
☐ Inco der Amount	
☐ corre tions	
☐ ires N rized Application Form	
☐ _____	

PM Invoice Review:	Initial:
☐ Approved for Payment	
☐ Incorrect Cost Code	
☐ Incorrect Percent Complete	
☐ Other _____	

This instrument was executed and acknowledged before me

On this _____ day of _____ 20

by _____

known to me as the person whose name is subscribed, as

[title] _____ of [company] _____

on behalf of and as the autorized act of said entity.

EXECUTED this _____ day

of the month _____ 20

_____
COMPANY

_____
Signature (Must be an Officer or Owner)

_____
Signature — Notary Public in and for the State of Texas

_____
Print Name

My Commission Expires _____

Revised 08/18/2014

EXHIBIT ONLY

Subcontractor Initial _____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

CONTINUATION SHEET

AIA DOCUMENT G703

PAGE OF PAGES

AIA Document G702, APPLICATION AND CERTIFICATION FOR PAYMENT, containing Contractor's signed certification is attached.

In tabulations below, amounts are stated to the nearest dollar.

Use Column I on Contracts where variable retainage for line items may apply.

APPLICATION NO: 0
APPLICATION DATE 1/0/1900
PERIOD TO: 1/0/1900
ARCHITECT'S PROJECT NO: 0

A	B	C	D	E	F	G	H	I	J	K	L
ITEM NO.	DESCRIPTION OF WORK	SCHEDULED VALUE	CHAN DA	ADJU ED RACT	WORK COMPLETED FROM PREVIOUS PLICATIONS	WORK COMPLETED THIS PERIOD	MATERIALS PRESENTLY STORED (NOT IN F OR G)	TOTAL COMPLETED AND STORED TO DATE (F+G+H)	% (I÷E)	BALANCE TO FINISH (E - I)	RETAINAGE (IF VARIABLE RATE)
1								$0.00	#DIV/0!	$0.00	$0.00
2								$0.00	#DIV/0!	$0.00	$0.00
3				$0				$0.00	#DIV/0!	$0.00	$0.00
4				$				$0.00	#DIV/0!	$0.00	$0.00
5				$0				$0.00	#DIV/0!	$0.00	$0.00
6				$0.00				$0.00	#DIV/0!	$0.00	$0.00
7				$0.00				$0.00	#DIV/0!	$0.00	$0.00
8				$0.00				$0.00	#DIV/0!	$0.00	$0.00
9				$0.00				$0.00	#DIV/0!	$0.00	$0.00
10				$0.00				$0.00	#DIV/0!	$0.00	$0.00
11				$0.00				$0.00	#DIV/0!	$0.00	$0.00
12				$0.00				$0.00	#DIV/0!	$0.00	$0.00
13				$0.00				$0.00	#DIV/0!	$0.00	$0.00
14				$0.00				$0.00	#DIV/0!	$0.00	$0.00
15				$0.00				$0.00	#DIV/0!	$0.00	$0.00
16				$0				$	DIV/0!	$0.00	$0.00
17									#DIV/0!	$0.00	$0.00
18								0	#	$0.00	$0.00
19				0.00				0.00	#DIV	$0.00	$0.00
20				$0.00				$0.00	#DIV	$0.00	$0.00
21				$				$0.00	#	$0.00	$0.00
22								$0.00		$0.00	$0.00
23				$0				$0	/0!	$0.00	$0.00
24				$0.00				$0.00	#DIV/0!	$0.00	$0.00
25				$0.00				$0.00	#DIV/0!	$0.00	$0.00
26				$0.00				$0.00	#DIV/0!	$0.00	$0.00
27				$0.00				$0.00	#DIV/0!	$0.00	$0.00
28				$0.00				$0.00	#DIV/0!	$0.00	$0.00
29				$0.00				$0.00	#DIV/0!	$0.00	$0.00
30				$0.00				$0.00	#DIV/0!	$0.00	$0.00
	SUBTOTAL	$0.00	$0.00	$0.00	$0.00	$0.00	$0.00	$0.00	#DIV/0!	$0.00	$0.00

EXHIBIT ONLY

Users may obtain validation of this document by requesting of the license a completed AIA Document D401 - Certification of Document's Authenticity

Subcontractor Initial_____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

EXHIBIT "C"

CONTRACTOR'S INSURANCE REQUIREMENTS OF SUBCONTRACT

1. Definitions. For purposes of this Agreement:
   A. ISO. "ISO" means Insurance Services Office.
   B. Subcontractor. "Subcontractor" shall include subcontractors of any tier.
   C. Contractor Parties. "Contractor Parties" means (a) Owner, (b) Contractor, (c) Architect/Engineer, (d) any lender whose loan is secured by a lien against the Project, (e) their respective shareholders, members, partners, joint venturers, co- venturers, affiliates, subsidiaries, successors, and assigns, (f) any members, directors, officers, employees, or agents of such persons or entities, and (g) others as required by the Contract Documents.

2. Subcontractor Insurance Representations to Contractor Parties.
   A. It is expressly understood and agreed that the insurance coverages required herein:
      i. Represent Contractor Parties' minimum requirements and are not to be construed to void or limit Subcontractor's indemnity obligations as contained in this Subcontract nor represent in any manner a determination of the insurance coverages Subcontractor should or should not maintain for its own protection; and
      ii. Are being, or have been, obtained by Subcontractor in support of Subcontractor's liability and indemnity obligations under this Subcontract. Irrespective of the requirements as to insurance to be carried as provided for herein, the insolvency, bankruptcy or failure of any insurance company carrying insurance ofSubcontractor, or the failure of any insurance company to pay claims accruing, shall not be held to affect, negate or waive any of the provisions of this Subcontract.
   B. Failure to obtain and maintain the required insurance shall constitute a material breach of, and default under, this Subcontract. If Subcontractor shall fail to remedy such breach within five (5) business days after written notice by Contractor, Subcontractor will be liable for any and all costs, liabilities, damages and penalties resulting to Contractor Parties from such breach, unless a written waiver of the specific insurance requirements(s) is provided to Subcontractor by Contractor.

3. Conditions Affecting All Insurance Required Herein.
   A. Cost of Insurance. All insurance coverage shall be provided at Subcontractor's sole expense.
   B. Maintenance of Insurance. All insurance coverage shall be maintained in effect with limits not less than those set forth below at all times during the term of this Subcontract and for such longer period as may be required under this Subcontract.
   C. Status and Rating of Insurance Company. All insurance coverage shall be written through insurance companies admittedto do business in the State of Texas and rated no less that A: VIII in the most current edition of *A.M. Best's Key Rating Guide* and no less that A- in the most current edition of *Standard & Poor Insurance Solvency Review*.
   D. Restrictive, Limiting or Exclusionary Endorsements. All insurance coverage shall be provided to Contractor Parties in compliance with the requirements herein and shall contain no endorsements that restrict, limit, or exclude coverage in any manner without the prior express written approval of Contractor.
   E. Limits of Liability. The limits of liability may be provided by a single policy of insurance or by a combination of primary and umbrella policies, but in no event shall the total limits of liability available for any one occurrence or accident be less than the minimum amount required herein.
   F. Notice of Cancellation, Non-renewal, or Material Reduction in Coverage. All insurance coverage shall contain the following express provision:
      This is to certify that the policies of insurance described herein have been issued to the Insured for whom this certificate is executed and are in force at this time. In the event of cancellation, or material change in coverage, thirty (30) days prior written notice shall be given to the certificate holder by certified mail, return receipt requested, except in the event of cancellation for nonpayment, in which event fifteen (10) days prior written notice shall be given.
   G. Additional Insured Status. Additional insured status shall be provided in favor of Contractor Parties on all liability insurance required herein except workers' compensation/employer's liability. Additional insured status on the general liability insurance shall be provided on a combination of ISO forms CG 20 10 04 13 and CG 20 37 04 13. Such additionalinsured coverage shall be primary to and shall seek no contribution from all insurance available to Contractor Parties, with Contractor Parties' insurance being excess, secondary and non-contributing. All Additional Insured Endorsements shall be provided to the Contractor with the certificate of insurance.

Subcontractor Initial_____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

H. Waiver of Subrogation. All insurance coverage carried by Subcontractor, whether required herein or not, shall provide a waiver of subrogation in favor of Contractor Parties. Contractor and Subcontractor waive all rights against each other and each of their subcontractors, sub-subcontractors, officers, directors, agents, and employees for recovery for damages caused by fire and other causes of loss to the extent covered by insurance, Builder's Risk, or any other property insurance applicableto the Work.

I. Primary and Non-Contributory. All insurance coverage required herein shall be primary to and shall seek no contribution from all insurance available to Contractor Parties, with Contractor Parties' insurance being excess, secondary and non-contributing. Where necessary, coverage shall be endorsed to provide such primary liability, and the certificate of insurance shall reflect the same.

J. Deductibles/Retentions. Except as otherwise specified herein, no insurance required herein shall contain a deductible or self-insured retention in excess of $10,000 without prior written approval of Contractor. All deductibles and/or retentions shall be paid by, assumed by, for the account of, and at Subcontractor's sole risk. Subcontractor shall not be reimbursed for same. In addition, the Subcontractor acknowledges that the Builder's Risk or similar type property policy contains certain deductibles, which may apply to a loss. If the resulting loss was caused by, in whole or in part, the Subcontractor's failures, the Subcontractor shall be responsible for the costs of the deductible and promptly remit payment to Contractor for the same. Otherwise, the Subcontractor shall be responsible for a pro-rata portion of the applicable deductible, shared with all other parties included in the loss.

4. Commercial General Liability Insurance.
   A. Coverage: Such insurance shall cover liability arising out of all locations and operations of Subcontractor, including but not limited to liability assumed under this Subcontractor (including the tort liability of another assumed in a business contract). Defense shall be provided as an additional benefit and not included with the limit of liability.
   B. Form: Commercial General Liability Occurrence form basis (at least as broad as an unmodified current ISO edition of CG 00 01).
   C. Amount of Insurance: Coverage shall be provided with limits of not lessthan:
      i. Each Occurrence Limit
         a. $1,000,000
      ii. General Aggregate Limit
         $2,000,000
      iii. Product-Completed Operations Aggregate Limit
         $2,000,000
      iv. Personal and Advertising Injury Limit
         $1,000,000
      v. Electronic Data Liability (required if working in or around data transmission lines)
         $1,000,000
   D. Required Endorsements:
      i. Additional Insured status required in 3.G., above. Additional Insured coverage will afford coverage for both Ongoing and Products Completed operation in favor of all indemnified Contractor parties in this agreement. Such coverage shall be equivalent to a combination of ISO forms CG 20 10 04 13 and CG 20 37 04 13.
      ii. Aggregate Per Project: The aggregate limit shall apply separately to each project through use of an Aggregate Limit of Insurance Per Project endorsement (ISO CG 25 03 04 13 or its equivalent).
      iii. Notice of Cancellation, or Material Change in Coverage, as required in 3.F., above.
      iv. Personal Injury Liability: The personal injury contractual liability exclusion shall be deleted.
      v. Primary Liability and Non-Contributory, as required in 3.I., above
      vi. Waiver of Subrogation, as required in 3.H., above.
   E. Other Requirements:
      i. Broad form Contractual Liability coverage will be provided in the policy.
      ii. Policy coverage shall provide primary and non-contributing liability coverage, as required in 3.I above, to all indemnified Contractor parties in this agreement. All insurance coverage required shall seek no contribution from all insurance available to the indemnified Contractor parties, with the indemnified Contractor parties insurance being excess, secondary, and non-contributing.
      iii. The policy shall not contain any of the following exclusions/limitations (or their equivalents):
         - Personal Injury contractual liability exclusion
         - Contractual Liability Limitation CG 21 39
         - Amendment of Insured Contract Definition CG 2426
         - Limitation of Coverage to Designated Premises or Project, CG 21 44

Subcontractor Initial_____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

- Exclusion – Damage to Work Performed by Subcontractors On Your Behalf, CG 22 94 or CG 22 95
- Any Construction Defect Completed Operations exclusion
- Any endorsement modifying or deleting the exception to the Employer's Liability exclusion or any endorsement that excludes or limits coverage for bodily injury to a subcontractor of any tier or an independent contractor
- Any endorsement modifying or deleting explosion, collapse or underground coverage (X, C, and U)
- Any Habitational or Residential exclusion, including but not limited to Multi-Family, Apartments, Townhomes, Condominiums for Residential and/or Commercial use, that would in effect remove policy coverage for the type of project or Subcontractor's Scope of Work
- Any "Insured vs. Insured" exclusion
- Any Punitive, Exemplary or Multiplied Damages exclusion
- Any Subsidence exclusion
- Any depletion of policy limits for Defense Costs or Supplementary Payments exclusion
- If Subcontractor uses drones or helicopters on the project site, any aircraft or drone exclusion, unless there is specific separate liability insurance that applies
- If subcontractor is providing or operating power-operated equipment (as defined under OSHA 1926.1400a) to hoist, lower or otherwise suspend a load (of other's material or equipment" the policy shall be endorsed to provide coverage for rigger's liability. Such endorsement shall insure against physical loss or damage to the property or equipment and include sufficient limits to equal or exceed the full replacement cost value of the largest hoist intended to be made with the Subcontractor's scope of Work. Rigger's lability coverage may also be provided via a Rigger's Liability policy with Contractor named as a Loss Payee on the policy and otherwise complying with the requirements related to power operated equipment set forth herein. Any Rigger's liability policy shall waive all rights of subrogation against the indemnified Contractor parties in this agreement.

5. Auto Liability Insurance.
   A. Coverage: Such insurance shall cover liability arising out of any auto (Symbol 1) including owned, hired and/or scheduled (as applicable), and, if Subcontractor does not own any vehicles, non-owned (Symbols 8, and 9).
   B. Form: Business Auto form (at least as broad as an unmodified current ISO edition of CA 00 01).
   B. Amount of Insurance: Coverage shall be provided with a limit of not less than $1,000,000 per accident, or such higheramount as required by the Contract Documents.
   C. Required Endorsements:
      i. Additional Insured status required in 3.G. and 3.I., above. Endorsement shall be provided with the certificate of insurance.
      ii. Notice of Cancellation, or Material Change in Coverage, as required in 3.F.,above.
      iii. Waiver of Subrogation, as required in 3.H., above.

6. Workers' Compensation/Employer's Liability Insurance.
   A. Coverage: Such insurance shall cover liability arising out of Subcontractor's employment of workers and anyone for whom Subcontractor may be liable for worker's compensation claims. USL&H must be provided where such exposure exists. *Subcontractor shall complete the attached TWCC 85 Form.*
   B. Amount of Insurance: Coverage shall be provided with a limit of not lessthan:
      i. Workers' Compensation: Statutory Limits
      ii. Employer's Liability: $1,000,000 each accident and each disease
   C. Required Endorsements:
      i. Notice of Cancellation, or Material Change in Coverage, as required in 3.F. above.
      ii. Waiver of Subrogation, as required in 3.H., above.
      iii. Alternate Employer endorsement to be provided with the certificate of insurance covering the General Contractor and Owner.
   D. Other Requirements:
      i. The State in which work is to be performed must be listed under Item 3.A. on the Information/Declaration page.
      ii. Workers' Compensation insurance is required and no "alternative" forms of insurance shall be permitted as a substitute.
      iii. Where a Professional Employer Organization (PEO) or "leased employees" are utilized, Subcontractor shall require its leasing company to provide Workers' Compensation insurance for said workers and such policy shall be endorsed to provide an Alternated Employer endorsement in favor of indemnified Contractor parties in this agreement. Where Subcontractor uses leased employees with Workers'

Subcontractor Initial_____

Compensation insurance provided by a PEO or employee leasing company, Subcontractor is strictly prohibited from subletting any of its work without express written agreement of Contractor.

iv. If subcontractor of any tier is required to provide equipment or crane operators, subcontractor shall ensure that such equipment operators are covered by workers' compensation insurance.

7. Umbrella/Excess Liability Insurance.
   A. Coverage: Insurance shall be Occurrence basis. Such insurance shall be excess over and be no less broad (following form) than all coverages described above and shall includea drop-down provision. Coverage shall include General Liability, Auto Liability, Employer's Liability, Rigger's Liability (if applicable), Drone/Helicopter/Aviation Liability (if applicable), and Pollution Liability (if applicable).
   B. Form: This policy shall have the same inception and expiration dates as the commercial general liability insurance required above.
   C. Amount of Insurance: Coverage shall be provided, at a minimum, based on the Type of Subcontractor as described below unless such higher amounts are required by the Contract Documents or the Primary Contract. If higher limits are available than the minimum amount required to obtain the job, then the full limits of the policy shall be available to the indemnified Contractor parties in this agreement.

      i. Type I: For any subcontractor whose scope of work includes providing or operating a tower crane or any other type of crane, including any subcontractor whose scope of work includes the operation of such a crane regardless if subcontractor to a lower-tier subcontractor:

         - $10,000,000 Each Occurrence/Aggregate

      ii. Type II: For any subcontractor who will be performing any of the following scopes of work: concrete, masonry, steel, carpentry or framing, HVAC, plumbing, electrical, excavation, demolition, foundation, scaffolding, and elevator:

         - $5,000,000 Each Occurrence/Aggregate

      iii. Type III: For any subcontractor not defined as a Type I or Type II subcontractor:

         - $1,000,000 Each Occurrence/Aggregate

   D. Required Endorsements:
      i. Additional Insured status required in 3.G. and 3.I., above. Endorsement shall be provided with the certificate of insurance.

8. Professional Liability (E&O).
   A. Coverage: Shall be required whenever service provider and/or its consultants are required to be certified, licensed, or registered by a regulatory entity and/or where the provider's error in judgment in planning, design, engineering, etc. could result in economic loss through the service provider's negligent acts, errors and omissions, and/or wrongful acts in all professional services including, but not limited to, design or design/build services.
   B. Form: This policy shall be in place and cover all the work performed and shall remain in place for ten (10) years after the completion of the project or through the statute of repose, whichever is greater.
   C. Amount of Insurance: of not less than $1,000,000 each occurrence/$1,000,000 aggregate.
   D. Other Requirements:
      i. This insurance is not permitted to include any type of exclusion or limitation of coverage applicable to claims arising from:
         - Bodily injury or property damage where coverage is provided on behalf of design professionals or design/build contractors.
         - Habitational or residential operations including but not limited to Multi-Family, Apartments, Townhomes, Condominiums for Residential and/or Commercial use, that would in effect remove policy coverage for the type of project or Subcontractor's Scope of Work.
         - Habitational or residential operations.
         - Mold and/or microbial matter and/or fungus and/or biological substance.
         - Punitive, exemplary, or multiplied damages.

9. Pollution Liability.

Subcontractor Initial_____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

A. Coverage: Shall be required whenever work under this contract involves pollution risk to the environment. Must include sudden and gradual coverage for third party liability, including defense costs and completed operations. Shall be on an occurrence basis.
   - Must provide third party coverage for bodily injury, property damage, clean up expenses, and defense arising from the operations.
   - All coverage in the policy shall apply to operations and completed operations without separate restrictions for either of these time frames.
   - Mold and/or microbial matter and/or fungus and/or biological substance shall be specifically included within the definition of Pollutants in the policy.

B. Form: Pollution liability occurrence basis form.

C. Amount of Insurance: Coverage shall be provided with a limit of not less than $1,000,000 Each Occurrence/$1,000,000 Aggregate.

D. Required Endorsements:
   i. Additional Insured status required in 3.G., above. Endorsement shall be provided with the certificate of insurance.

E. Other Requirements:
   i. This insurance shall not include any type of exclusion or limitation of coverage applicable to claims arising from:
      - Asbestos or lead
      - Contractual assumption of liability
      - Impaired property that has not been physically injured
      - Materials supplied or handled by named insured. However, exclusions for the sale and manufacture of products are allowed. Exclusionary language pertaining to materials supplied by the insured shall be reviewed by the certificate holder for approval.
      - Property damage to work performed by the Subcontractor
      - Punitive, exemplary or multiplied damages
      - Work performed by subcontractors

10. Aviation/Drone Liability.
    A. Coverage: Shall be required if your work or product involves the use of an airplane, helicopter, drone, or any other type of aeronautical aircraft equipment (manned and unmanned). Must be on an occurrence basis. It must provide coverage for property damage, bodily injury, defense costs, and privacy infringement for all locations and sites where operations are performed. It must provide coverage for owned and non-owned aircraft.
    B. Form: Aviation/Drone liability insurance policy.
    C. Amount of Insurance: Coverage shall be provided with a limit of not less than $1,000,000 Each Occurrence.
    D. Required Endorsements:
       i. Additional Insured status required in 3.G., above. Endorsement shall be provided with the certificate of insurance.
    E. Other Requirements:
       i. If any cargo is being carried by the aeronautical equipment, insurance must be provided that will cover the full replacement cost of the cargo that is in its care, custody or control for the project. Proof of adequate coverage for cargo must be provided.
11. Subcontractor's Equipment/Installation Insurance. Subcontractor is fully responsible for loss and damage to its property on the site, including tools and equipment, and shall take necessary precautions to prevent vandalism, theft, burglary, pilferage and unexplained disappearance of property. Any insurance covering Subcontractor's or its sub-subcontractor's property shall be Subcontractor's and its sub-subcontractor's sole and complete means of recovery for any such loss. To the extent any loss is not covered by said insurance or subject to any deductible or co-insurance, Subcontractor shall not be reimbursed for same.
12. Use of Contractor's Equipment. Subcontractor, its agents, employees, subcontractors or suppliers shall use Contractor's equipment only with express written permission of Contractor's designated representative and in accordance with Contractor's terms and condition for such use. **IF SUBCONTRACTOR OR ANY OF ITS AGENTS, EMPLOYEES, SUBCONTRACTORS OR SUPPLIERS UTILIZE ANY OF CONTRACTOR'S EQUIPMENT FOR ANY PURPOSE, INCLUDING MACHINERY, TOOLS, SCAFFOLDING, HOISTS, LIFTS OR SIMILAR ITEMS OWNED, LEASED OR UNDER THE CONTROL OF CONTRACTOR, SUBCONTRACTOR ACCEPTS SUCH EQUIPMENT ON AN AS IS BASIS AND WITH ALL FAULTS, SUBCONTRACTOR SHALL UTILIZE SUCH EQUIPMENT AT ITS OWN RISK, SUBCONTRACTOR WAIVES AND RELEASES ANY CLAIM FOR, AND SUBCONTRACTOR SHALL DEFEND, INDEMNIFY, HOLD HARMLESS AND BE LIABLE TO CONTRACTOR PARTIES FOR ANY AND ALL LOSS, BODILY INJURY, DEATH, PROPERTY DAMAGE OR DAMAGE WHICH MAY ARISE FROM SUCH USE, EXCEPT TO THE EXTENT THAT SUCH LOSS, BODILY INJURY, DEATH, PROPERTY DAMAGE OR DAMAGE IS CAUSED BY THE NEGLIGENCE OR FAULT, BREACH OR**

Subcontractor Initial_____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

VIOLATION OF A STATUTE, ORDINANCE, GOVERNMENTAL REGULATION, STANDARD, OR RULE, OR BREACH OF CONTRACT OF CONTRACTOR PARTIES, THEIR RESPECTIVE AGENTS OR EMPLOYEES, OR ANY THIRD PARTY UNDER THE CONTROL OR SUPERVISION OF CONTRACTOR PARTIES, OTHER THAN SUBCONTRACTOR OR ITS AGENT, EMPLOYEE OR SUBCONTRACTOR OF ANY TIER.

13. Evidence of Insurance.
    A. Provision of Evidence. Evidence of the insurance coverage is required to be maintained by Subcontractor, represented by certificates of insurance, evidence of insurance, and endorsements issued by the insurance company or its legal agent, and must be furnished to Contractor prior to commencement of Work and not later than fifteen (15) days after Subcontractor's execution of this Subcontract. New certificates of insurance, evidence of insurance, and endorsements shall be provided to Contractor not later than prior to the termination date of the current certificates of insurance, evidence of insurance, and endorsements. Upon request, Subcontractor will provide the Contractor with unredacted copies of all applicable insurance polices required under this Subcontract.

    B. Form:
        i. All property insurance required herein shall be evidence by ACORD form 27, "Evidence of PropertyInsurance".
        ii. All liability insurance required herein shall be evidenced by ACORD form 25, "Certificate of Insurance".
    C. Specifications: Such certificates of insurance, evidence of insurance, and endorsements shall specify:
        i. Contractor as a certificate holder with correct mailing address.
        ii. Insured's name, which must match that on this Agreement.
        iii. Insurance companies affording each coverage, policy number of each coverage, policy dates of each coverage, allcoverages and limits described herein, and signature of authorized representative of insurance company.
        iv. Producer of the certificate with correct address and phone number listed.
        v. Additional insured status required herein.
        vi. Aggregate limits per project required herein.
        vii. Amount of any deductibles and/or retentions.
        viii. Cancellation and material change in coverage notification as required by this Agreement.
        ix. Primary and Non Contributory status required herein.
        x. Waivers of subrogation required herein.
    D. Required Endorsements. A copy of each required endorsement shall also be provided.
    E. Failure to Obtain. Failure to demand such certificate or other evidence of full compliance with these insurance requirements or failure of Contractor to identify a deficiency from evidence that is provided shall not be construed as a waiver of Subcontractor's obligations to maintain such insurance.
    F. Certified Copies. Upon request of any Contractor Party, Subcontractor shall provide to Contractor a certified copy of all insurance policies required herein within ten (10) days of any such request. Renewal policies, if necessary, shall be delivered to Contractor at least ten (10) days prior to the expiration of the previous policy.
    G. Commencement of Work. Commencement of the Subcontract Work without provisions of the required certificate of insurance, evidence of insurance and/or required endorsements, or without compliance with any other provision of this Subcontract, shall not constitute a waiver by Contractor of any rights. Contractor shall have the right, but not the obligation, of prohibiting Subcontractor of any sub-subcontractor from performing any Subcontract Work until such certificate of insurance, evidence of insurance and/or required endorsements are received and approved by Contractor.

14. Sub-Subcontractor's Insurance. Insurance similar to that required of Subcontractor shall be provided by all sub-subcontractors (or provided by Subcontractor on behalf of sub-subcontractors) to cover operations performed under any subcontract agreement. Subcontractor shall be held responsible for any modification in these insurance requirements as they apply to sub-subcontractors. Subcontractor shall maintain certificates of insurance from all sub-subcontractors containing provisions similar to those listed herein (modified to recognize that the certificate is from sub-subcontractor) enumerating, among other things, the waivers of subrogation, additional insured status, and primary liability as required herein, and make them available to Contractor upon request.

15. **RELEASE AND WAIVER: SUBCONTRACTOR HEREBY RELEASES, AND SHALL CAUSE ITS SUB-SUBCONTRACTORS TO RELEASE, CONTRACTOR PARTIES FROM ANY AND ALL CLAIMS OR CAUSES OF ACTION WHATSOEVER WHICH SUBCONTRACTOR AND/OR ITS SUB-SUBCONTRACTORS MIGHT OTHERWISE NOW OR HEREAFTER POSSESS RESULTING IN OR FROM OR IN ANY WAY CONNECTED WITH ANY LOSS COVERED BY INSURANCE, WHETHER**

Subcontractor Initial_____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

SUCH INSURANCE IS REQUIRED HEREIN OR NOT, OR ANY LOSS WHICH SHOULD HAVE BEEN COVERED BY INSURANCE REQUIRED HEREIN, INCLUDING THE DEDUCTIBLE AND/OR UNINSURED PORTION THEREOF, MAINTAINED AND/OR REQUIRED TO BE MAINTAINED BY SUBCONTRACTOR AND/OR ITS SUB-SUBCONTRACTORS PURSUANT TO THIS SUBCONTRACT.

16. Builder's Risk Costs and Claims.
    A. Time and Materials – Not to Exceed. Subcontractor agrees that, in the event of a loss that is covered or may be covered by the applicable Builder's Risk or similar type property insurance policy, that all costs for remediation, repair, or replacement of the damaged work shall be performed on a strict time and materials basis, with an agreed upon not to exceed amount. Subcontractor shall provide all signed time sheets, invoices, receipts, purchase orders, material take offs, and material delivery logs necessary to support the costs claimed by Subcontractor under the claim.
    B. Timing for Payment – Subcontractor acknowledges that, in the event of a covered loss, a claim under the applicable policy may take additional time to be verified, approved, and funded by the insurance carrier. As such, all contingent payment provisions described in Paragraphs 11 and 12 of Exhibit A shall apply to payments and claims under the Builder's Risk or similar type property policies, as if the payments coming from the applicable carrier are payments from the Owner. This specifically includes any "pay if paid" and "pay when paid" provisions.

Subcontractor Initial_____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

EXHIBIT "D"

SUBCONTRACTOR/SUPPLIER'S SUB-SUBCONTRACTOR/SUB-SUPPLIER LISTING

BEFORE ME, the undersigned authority, on this day personally appeared_____,_____ [title] of _____ [Subcontractor], and, upon oath, after first being duly sworn, deposed and stated:

"My name is _____ and I am the _____ [title] of _____ [Subcontractor], referred to in this affidavit as "Subcontractor." The facts set forth herein are within my personal knowledge and are true and correct, and I am competent and authorized to make this affidavit on behalf of Subcontractor. I hereby warrant and represent that the below is a true and complete listing of any and all subcontractors and/or suppliers whom Subcontractor has or will have utilized to perform work on the improvements and real property as listed below. I warrant and represent that all listed below have been paid in full for services/materials provided or will be paid in full upon receipt of the period progress payment from Contractor, through the period for which payment has been received. I acknowledge that Contractor may issue joint checks, at its sole discretion, to any/all suppliers/sub-subcontractors listed below. Subcontractor acknowledges that Contractor is relying on Subcontractor's statements and representations herein in making payment to Subcontractor. The undersigned affiant agrees to indemnify Contractor of and from any and all loss, cost or expense resulting from any false or incorrect information contained in this affidavit.

PROJECT NAME:_____NUMBER: _____

PROJECT ADDRESS:_____CITY/ST/ZIP _____

Sub-Subcontractor/Sub-Supplier Company/Contact Name	Contact Information Phone/Email	Contract Amount/Balance Due (if any) (Suppliers: List Anticipated Costs)

_____ _____
Signature Printed Name

_____ _____
Company Date

Subscribed and sworn before me this _____ day of_____ , 20___ .

_____
Notary Public, State of Texas

_____
Commission Expires

Subcontractor Initial_____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

EXHIBIT "E"

TEXAS DEPARTMENT OF INSURANCE, DIVISION OF WORKERS' COMPENSATION
7551 Metro Center Drive, Suite 100
Austin, Texas 78744

If you are not certain whether all parties meet the requirements for entering into this agreement, you may wish to consult an attorney.

Texas Workers' Compensation Act, Texas Labor Code, Section 406.121(2) defines "independent contractor" as follows: (1) "Independent contractor" means a person who contracts to perform work or provide a service for the benefit of another and who ordinarily: (A) acts as the employer of any employee of the contractor by [illegible]ing wages, directing activities, and performing other similar functions characteristic of an employer-employee relationship; (B) is free to determine the manner in which the work or serv[illegible] [illegible]rformed, including the hours of labor of or method of payment to any employee; (C) is required to furnish or have his employees, if any, furnish necessary tools, supplies, or materi[illegible] [illegible]orm the work or service; and (D) possesses the skills required for the specific work or service.

AGREEMENT BETWEEN GENERAL CONTRACTOR AN[illegible]TRACTOR
TO ESTABLISH INDEPENDENT RELA[illegible]SH[illegible]

Notice of Agreemen[illegible]

The undersigned General Contractor and the undersigned Su[illegible]r hereby declare that:

(A) the Subcontractor meets the qualifications of an Independent Co[illegible]der Texa[illegible]s' Compensation Act, Texas Labor Code, Section 406.121;
(B) the Subcontractor is operating as an independent contractor [illegible] term[illegible]der Section 406.121 of the Act;
(C) the Subcontractor assumes the responsibilities of an empl[illegible] work; and
(D) the Subcontractor and the Subcontractor's employees are no[illegible] of the [illegible]al Contractor for purposes of the Act.

TER[illegible]ES) O[illegible]ENT: FROM: _____

TO: _____

Arch-Con Corporation
Name of General Contractor

X
Name of Subcontractor

LOCATION OF EACH AFFECTED JOB S[illegible] WH[illegible]
THIS IS A BLANKET AGREEMENT):

This is a blanket agreem[illegible]

Estimated number of employees affecte[illegible]

THIS AGREEM[illegible] SHALL TAKE EFFECT NO SOONER THAN THE DATE IT IS S[illegible]

Texas Labor Code, Texa[illegible] [illegible]on 406.122.

General Contractor's Affirm[illegible]

If the General C[illegible]tor's workers' c[illegible]sation carrier changes during the ef[illegible] perio[illegible] coverage, [illegible]dvisable for the General C[illegible]or to [illegible]s form wit[illegible]e new insurance carrier.

0647851
[illegible] Tax I. D. Number

Signature of C[illegible]tract[illegible] Date

35 West Gray Street, Suite 300
[illegible]s (Street)

Michael G. C[illegible]
Printed Name of Gene[illegible]ractor

H[illegible]uston, TX 77019
Address (City, State, Zip)

Su[illegible]ctor's [illegible]mation

X
Federal Tax I. D. Number

Signature of Subcontractor Date

X
Address (Street)

X
Printed Name of Subcontractor

X
Address (City, State, Zip)

The General Contractor should retain the original. The Subcontractor should also retain a copy of the agreement.. This form is not required to be filed with the Division, and may be provided to the insurance carrier.

Division Data Stamp Here

DWC FORM-85 (Rev. 10/05) DIVISION OF WORKERS' COMPENSATION

EXHIBIT ONLY

Subcontractor Initial_____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

EXHIBIT "F"
Safety Addendum to Arch-Con Corporation Subcontract

1. **PRE-ENGAGEMENT REQUIREMENTS**

Prior to the start of any work on a Project for Arch-Con Corporation ("Arch-Con"), subcontractor and sub tier subcontractor(s) shall:

1.1. Submit a written copy of their Safety Program that includes a Hazard Communication Program, Safety Data Sheets (SDS) and a Project-specific chemical inventory list.

1.2. Safety programs will be maintained and updated as needed by subcontractor and lower tier subcontractor(s).

2. **PROJECT AND SAFETY ORIENTATION**

2.1. All workers are required to attend site safety orientations before they are allowed on any Arch-Con construction project. This is a general project safety orientation and does not relinquish the subcontractor or lower tier subcontractor(s) of its responsibilities to provide a safe working environment for its employees.

3. **DRUG TESTING**

3.1. Subcontractor and lower tier subcontractor(s) shall have a written company policy related to Drug and Alcohol Abuse.

3.2. At Arch-Con's discretion and upon request, subcontractor and lower tier subcontractor will provide written documentation from a licensed facility/clinic whether employees have passed or failed any drug or alcohol test.

4. **ACCIDENT NOTIFICATION**

4.1. Subcontractor is required to immediately notify Arch-Con's Safety Representative or Jobsite Superintendent when any accident, damage or injury has occurred. A written, fully documented accident report is to be furnished to Arch-Con no later than twenty-four (24) hours after the occurrence.

5. **GENERAL**

5.1. All subcontractors will perform daily housekeeping in accordance with Arch-Con requirements and Federal, State and/or Local safety related laws or regulations. In the event that Subcontractor fails to perform housekeeping in a timely manner, Arch-Con may, after a forty-eight-hour notice, rectify the problem at Subcontractor's expense.

5.2. Second and lower tier subcontractors shall abide by all safety requirements of subcontractor and Arch-Con and all Federal, State and/or Local safety related laws or regulations.

5.3. Subcontractors are responsible for providing work task lighting for its employees and second and lower tier subcontractors.

5.4. Smoking is only allowed in designated project areas as assigned by Arch-Con at its sole discretion.

5.5. No radios or head phones are allowed onsite.

5.6. In the event the subcontractor employs non-English speaking tradespeople, the subcontractor expressly agrees that it shall provide supervisory personnel (superintendent, general foreman or foreman) that is proficient in both English and the specific foreign language relevant to the tradespeople available to communicate and/or translate as needed. In the event that the subcontractor refuses, after forty-eight hours' notice, to provide supervisory personnel proficient in both English and the specific foreign language, Arch-Con may, at its discretion, retain a translator at the Subcontractor's expense.

5.7. Subcontractors are required to provide ALL safety related paperwork to Arch-Con as required by the project superintendent.

5.8. If cranes are in use on a project, the following will be required:

5.8.1. Subcontractor is required to provide a "Pick Plan" along with all supporting documentation, including but not limited to the following:

Subcontractor Initial_____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

5.8.1.1. A copy of subcontractor's crane operators license;
5.8.1.2. A completed crane operator evaluation form;
5.8.1.3. A copy of rigger/signal person certifications;
5.8.1.4. A copy of Crane Annual Inspection; and
5.8.1.5. A Site Specific erection Plan including a site layout an construction sequence in accordance with OSHA Subpart R.

The foregoing must be provided to Arch-Con before a crane can be assembled on the job site.

5.8.2. The subcontractor's competent person shall be responsible for the assembly and disassembly of any crane.
5.8.3. The subcontractor is responsible for the rigging, signaling, inspections and all operations of any crane. The operator of any crane must perform daily crane inspections and make them available to Arch-Con upon request.
5.8.4. All cranes shall have an Anti-Two Block device installed on the crane.
5.8.5. All crane lines will be given distinctive labels ("names") and such names will be provided to Arch-Con prior to use.
5.8.6. Crane lifts that equal or exceed 75% of the crane's chart are not permitted.

6. CLOTHING AND PERSONAL PROTECTIVE EQUIPMENT

6.1. Subcontractors and lower tier subcontractors are responsible for providing all personal protective equipment for its employees, including but not limited to: hard hats, safety harnesses, lanyards, ear plugs, face shields, safety glasses, reflective vests, and the like. All PPE must be utilized at all times while workers are onsite.
6.2. Construction work boots shall be worn at all times during the course of all construction activities.
6.3. Unaltered hard hats are required at all times except in break areas, offices, or parking lots that are not connected to the working area.
6.4. If subcontractor or lower tier subcontractor has the need to use a face shield, welding or cutting shields or other such devices, the subcontractor must provide and use the type of shield that attaches to hard hats in such a way that the hardhat may be worn 100% of the time.
6.5. Z87 safety glasses shall be worn at all times except in break areas, construction offices or parking lots that are not connected to the working area.
6.6. In addition to eye protection referenced in paragraph 6.5. above, a full face-shield must be worn where a danger of flying debris or splashing exists.
6.7. All shirts must have a minimum of a 4-inch sleeve.
6.8. All baggy attire will be tucked in and contained.
6.9. Long pants are required at all times.
6.10. No yoga or workout pants are allowed on the project.
6.11. OSHA acceptable hearing and respiratory equipment should be worn as required.
6.12. All workers, when exposed to a height of 6 feet or taller, are required to wear a full body harness with appropriate lanyard(s). The full body harness lanyards and connection points shall be compliant with all Federal, State and/or Local safety related laws, regulations and requirements. The lanyard(s) shall be securely attached to the worker's harness and appropriate connection point 100% of the time while the exposure exists.
6.13. All workers must wear metatarsal guards when operation operating equipment (i.e. jumping jack dirt compactor) that could cause crushing/compression injuries to a worker's lower extremities, including the feet and legs.

7. TASK HAZARD ANALYSIS (THA)

7.1. Every subcontractor or lower tier subcontractor shall complete a THA form before any work is performed on site. THA forms must be turned in electronically before subcontractor may start work. In the event

Subcontractor Initial_____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

that the subcontractor fails to turn in a THA, as required herein, three (3) or more times, Arch-Con may back-charge the subcontractor two thousand dollars and zero cents($2,000.00) for additional administration costs and time, per violation.

7.2. A competent person will work with their team and list all known hazards and what steps will be taken to eliminate or remove risks form working areas.

7.3. All team members (workers) are required to sign the THA form before they are allowed to perform any work on the Project.

7.4. All THA forms shall be turned into the Arch-Con superintendent daily.

8. **FLOOR AND WALL OPENINGS**

8.1. Subcontractor is fully responsible for covering floor and wall openings it has created for its use. All unprotected sides / edges must be protected by use of a guardrail system. Except for roof areas, no warning line can be used for unprotected sides and edges.

8.2. Covers may be used on all openings 6.25 square feet or less in area and if one dimension is 2.5 feet or less.

8.3. All other openings shall be barricaded with standard guardrails with the following considerations:

8.3.1. If the holes are to be used for worker access or to pass through materials, they should be barricaded with a handrail complete with gates, removable guardrails or chains.

8.3.2. All holes used for worker access or material handling shall be designated and locations disseminated to all individuals working on the Project site, including all other subcontractors and lower tier subcontractors.

8.3.3. Holes with a maximum horizontal dimension of 2 inches or greater shall be protected so materials cannot fall to levels below.

8.3.4. If an engineered cover is not used, ¾ inch plywood, at a minimum, must be used.

8.3.5. Covers must be secured from displacement, labeled with the word “HOLE” clearly marked on the cover, and capable of withstanding the maximum load intended.

8.3.6. Plywood shall NOT be used to cover holes greater than 12 inches in the maximum horizontal dimension.

9. **DISCIPLINARY POLICY**

9.1. All subcontractors or lower tier subcontractors agree to enforce compliance with Arch-Con’s Site-Specific Safety Program in addition to all Federal, State and/or Local safety related laws or regulations. The follow enforcement steps shall be taken should there be non-compliance:

9.1.1. 1st Offense – the worker is given a written warning.

9.1.2. 2nd Offense – the worker shall be removed from all Arch-Con projects for 2 full working days.

9.1.3. 3rd Offense – the worker shall be removed from all Arch-Con projects for no less than 1 year.

9.2. If there is an imminent danger safety violation occurring, the worker will be removed from the Project immediately and not allowed to return to ANY Arch-Con site until formal approval is given by Arch-Con.

9.3. In the event that a subcontractor’s or lower tier sub-subcontractor’s worker is removed from the project for disciplinary reasons, the subcontractor will ensure manpower needs are replenished within a 24-hour period. If the subcontractor or sub-tier subcontractor fails to replace labor accordingly, subcontractor or sub-tier subcontractor will be considered in breach of contract and will be liable for any costs related to schedule delays.

1.

Subcontractor Initial_____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

EXHIBIT "J"

CONSTRUCTION SCHEDULE

[See Attached]

Initials: _____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

Preconstruction				
5	Issue IFC Drawings	1	06/03/25	06/03/25
10	Prepare GMP	20	06/04/25	07/01/25
15	Finalize GMP Contract	156	07/02/25	02/09/26
20	Executed Contract	0		02/09/26
25	LOI to Release Contech System	0		06/27/25
30	Issue ETP Contract	0		02/09/26
Submittals/Shop Drawings				
35	Contech System	25	06/30/25	08/04/25
40	Parking Garage Tickets	20	02/10/26	03/09/26
Procurement				
45	Contech System - Fabrication	30	08/05/25	09/16/25
50	Parking Garage - Fabrication	60	03/10/26	06/02/26
Construction				
Milestones				
55	Permits	0		06/03/25
60	NTP for Construction	0		02/09/26
65	Paving Complete	0		09/04/26
Core Systems				
70	Water	0		08/12/26
75	Sanitary	0		08/14/26
80	Storm	0		04/27/26
85	Permanent Power	0		12/14/26
90	Switch Gear Delivery	0		08/05/26
95	Elevator Delivery	0		09/17/26
100	CPE Transfomer Release	0	08/07/26	
Phase 1				
105	Break Tank Delivery	0		03/20/23
110	Garage Foundations Complete	0		04/23/26
115	Pre-Cast Delivery	0	06/03/26	
120	Garage Erection Complete	0		07/29/26
125	Slab on Grade Complete	0		09/17/26
130	Top Out Structure	0		10/06/26
135	Building Dry In	0		10/13/26
140	Drywall Complete	0		12/08/26
150	Building Climatized	0		12/21/26
155	Substantial Completion (P1)	0		10/22/27
Phase 2				
160	Slab on Grade Complete	0		04/27/26
165	Top Out Structure	0		07/23/26
170	Building Dry In	0		08/05/26
175	Drywall Complete	0		01/21/27
185	Building Climatized	0		02/05/27
190	Substantial Completion (P2)	0		11/18/27
Phase 3				
195	Slab on Grade Complete	0		05/07/26
200	Top Out Structure	0		07/15/26
205	Building Dry In	0		07/29/26
210	Drywall Complete	0		02/24/27
220	Building Climatized	0		03/11/27
225	Substantial Completion (P3)	0		01/10/28
Phase 4				
230	Slab on Grade Complete	0		09/24/26
235	Top Out Structure	0		12/17/26
240	Building Dry In	0		01/04/27
245	Drywall Complete	0		04/05/27
255	Building Climatized	0		04/21/27
260	Substantial Completion (P4)	0		04/10/28
Core Systems				
265	Set Switch Gear	1	08/06/26	08/06/26

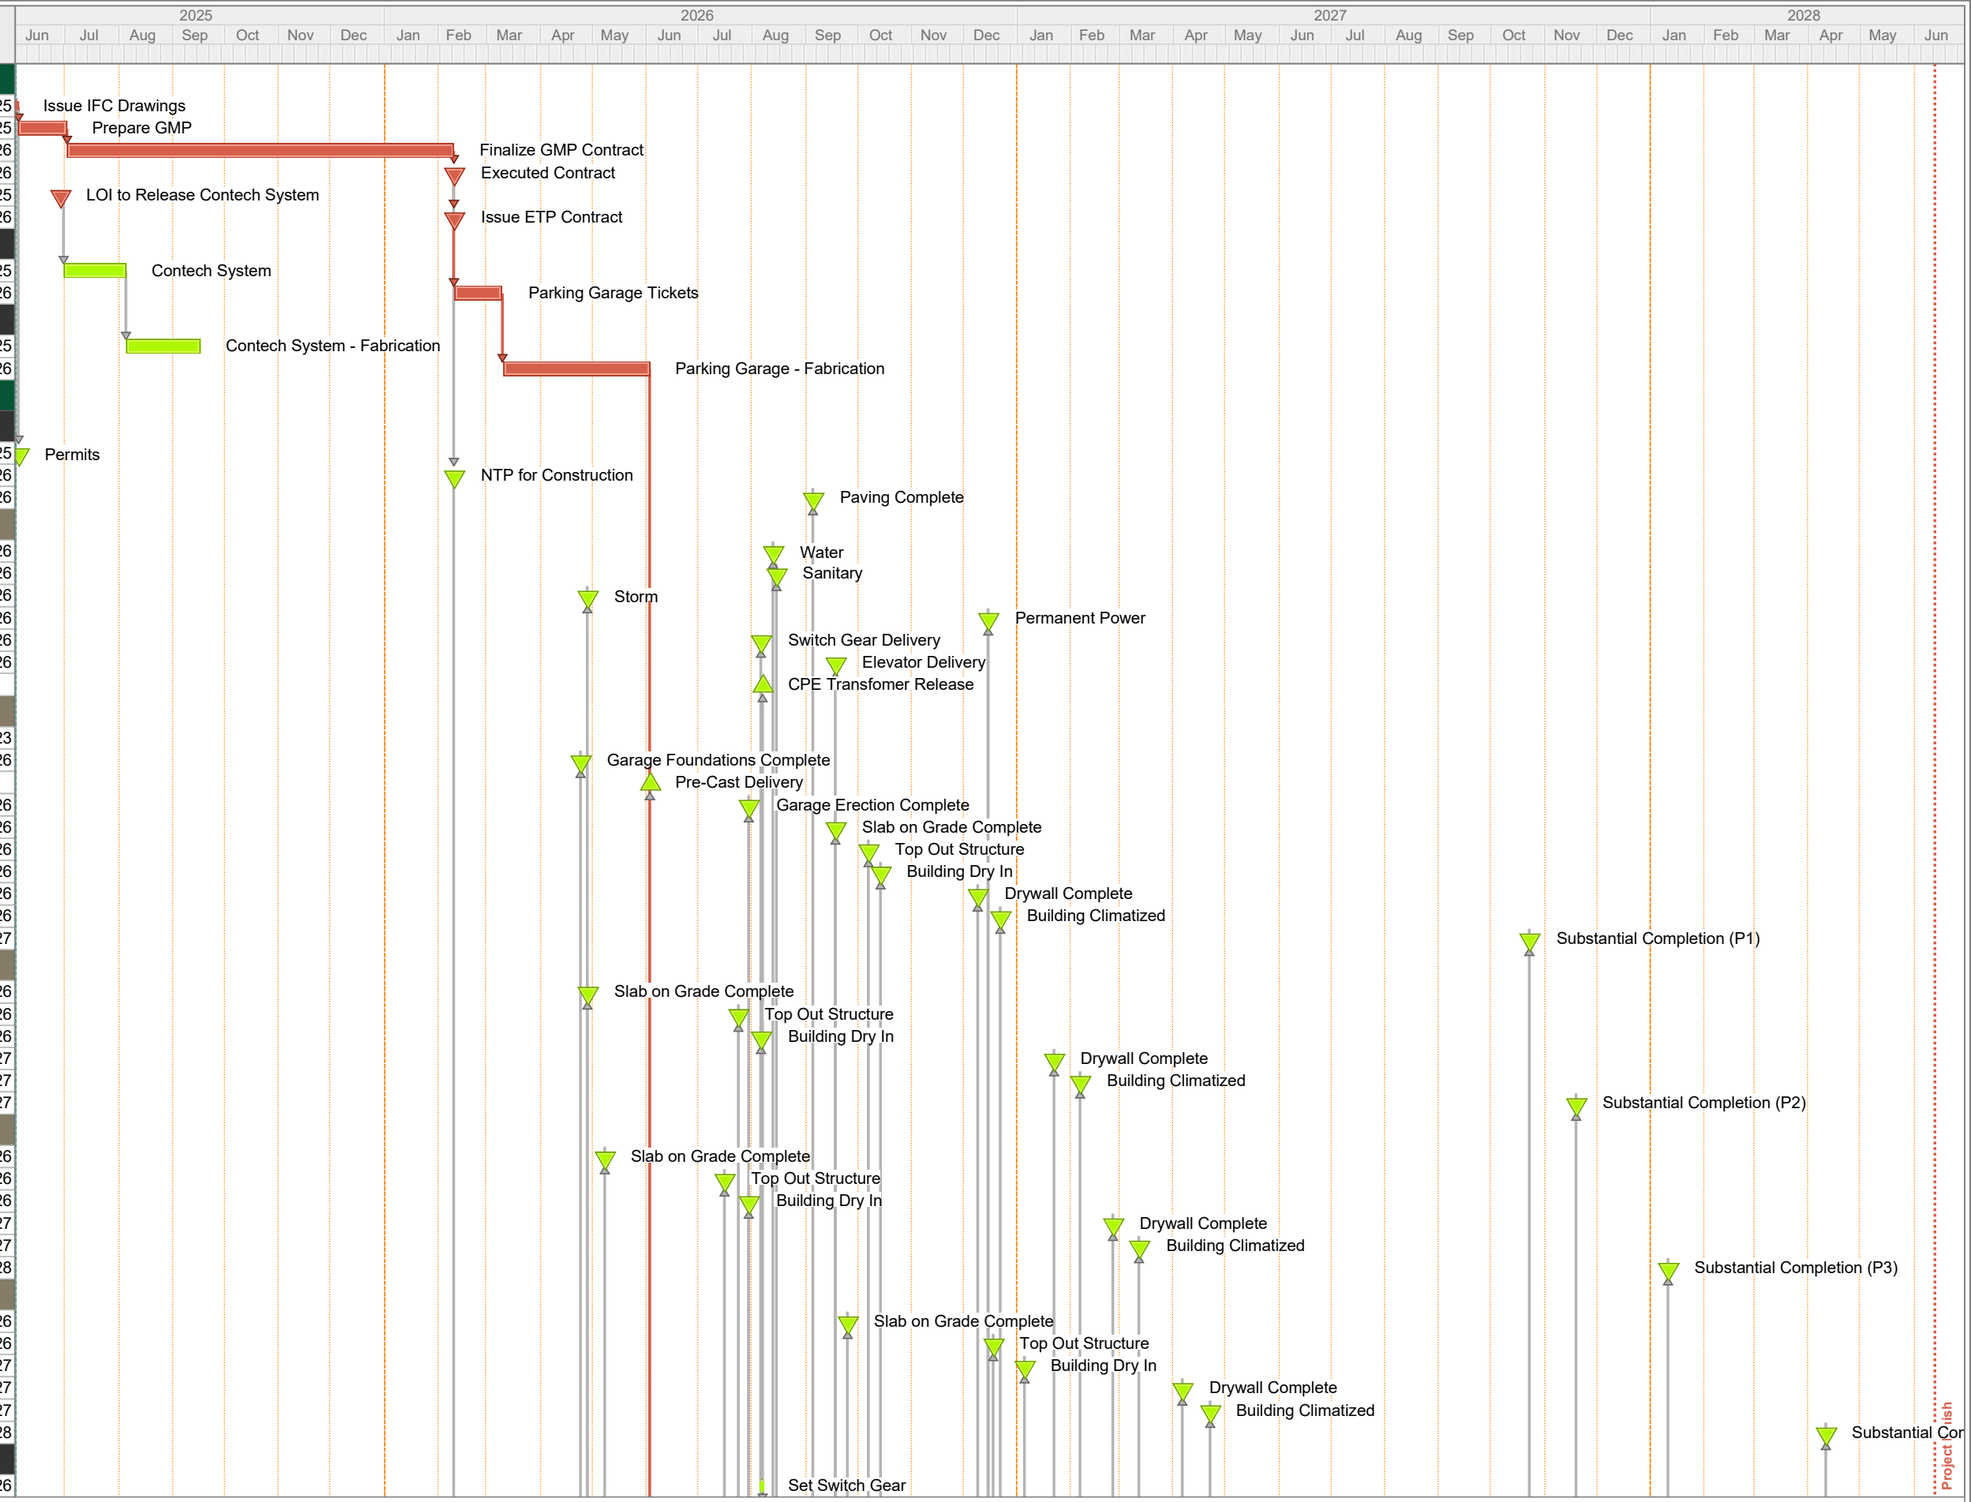

Start Date: 06/02/25
Finish Date: 06/12/28
Data Date: 06/02/25
Run Date: 01/27/26

The Silos

Moody

ARCH·CON CORPORATION

Initials: _____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

270	Switch Gear Final Connections	10	08/07/26	08/20/26
275	Set RTU's/AHU's	1	08/06/26	08/06/26
280	RTU's/AHU's Final Connections	10	08/07/26	08/20/26
285	Permanent Power	90	08/07/26	12/14/26
Mobilization				
290	Temp. Fence, Barricades & Signage	6	02/10/26	02/17/26
295	Office Trailer Delivery	1	02/18/26	02/18/26
300	Office Trailer Setup	3	02/19/26	02/23/26
Sitework				
Stormwater				
Area 1				
310	Storm Tie-In, SWQ Unit & Restrictor	3	02/26/26	03/02/26
315	Storm (24" & 36")	2	03/03/26	03/04/26
Inspections				
320	STORM TIE-IN, SWQ UNIT & RESTRI	3	03/03/26	03/05/26
325	STORM (24" & 36")	2	03/06/26	03/09/26
Area 2				
330	Contech System (84" CMP)	10	03/10/26	03/23/26
Area 3				
335	Contech System (84" CMP)	10	03/24/26	04/06/26
Area 4				
340	Contech System (CMP 84")	15	04/07/26	04/27/26
Area 5				
345	Contech System (CMP 96")	5	07/30/26	08/05/26
On-Site Utilities				
Area 1				
350	Domestic/Fire Water Main	5	04/28/26	05/04/26
355	Sanitary	5	05/05/26	05/11/26
360	Site Lighting & Power UG	3	05/12/26	05/14/26
Inspections				
365	Fire Marshal Hydro	1	05/05/26	05/05/26
Area 2				
370	Domestic/Fire Water Main	5	05/06/26	05/12/26
375	Sanitary	5	05/13/26	05/19/26
380	Site Lighting & Power UG	3	05/20/26	05/22/26
Inspections				
385	Fire Marshal Hydro	1	05/13/26	05/13/26
Area 3				
390	Domestic/Fire Water Main	5	05/14/26	05/20/26
395	Sanitary	5	05/21/26	05/28/26
400	Site Lighting & Power UG	3	05/29/26	06/02/26
Inspections				
405	Fire Marshal Hydro	1	05/21/26	05/21/26
Area 4				
410	Domestic/Fire Water Main	5	05/22/26	05/29/26
415	Sanitary	5	06/01/26	06/05/26
420	Site Lighting & Power UG	3	06/08/26	06/10/26
Inspections				
425	Fire Marshal Hydro	1	06/01/26	06/01/26
Area 5				
430	Domestic/Fire Water Main	5	08/05/26	08/11/26
435	Sanitary	5	08/10/26	08/14/26
440	Site Lighting & Power UG	3	08/13/26	08/17/26
Inspections				
445	Fire Marshal Hydro	1	08/12/26	08/12/26
Paving				
Area 1				
450	Lime Stabilize Subgrade	7	06/03/26	06/11/26
455	Final Grade	4	06/09/26	06/12/26
460	Prep & Form	6	06/11/26	06/18/26
465	Rebar	3	06/17/26	06/19/26

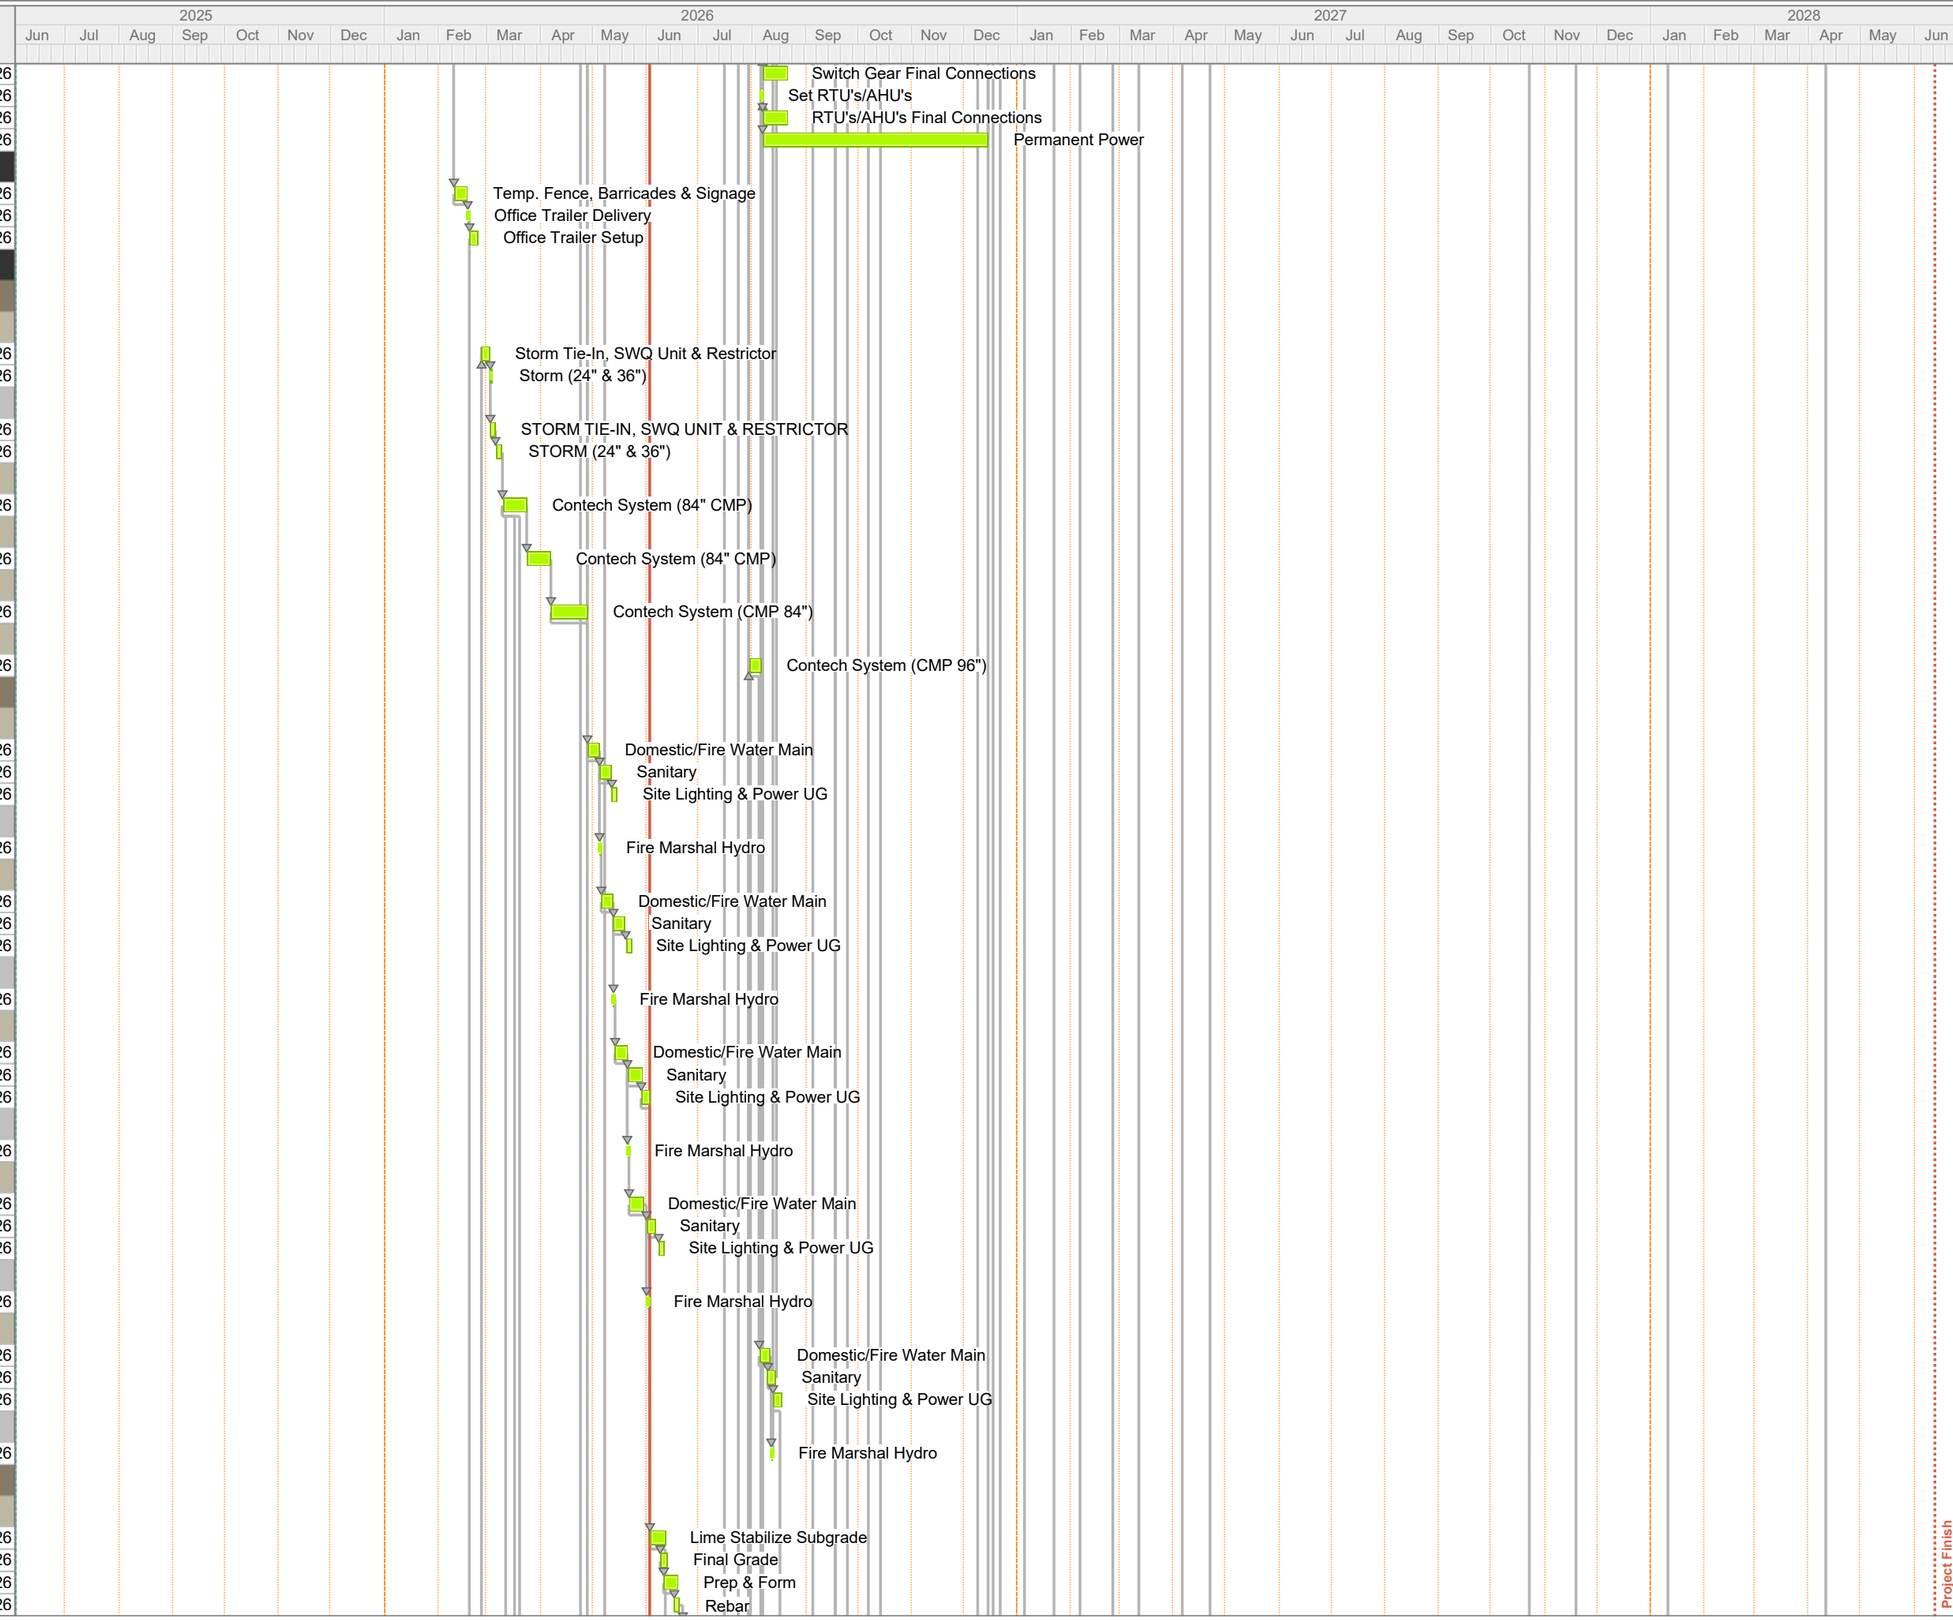

Initials: _____

470	Inspections	1	06/22/26	06/22/26
475	Pour	1	06/23/26	06/23/26
Area 2				
480	Lime Stabilize Subgrade	7	06/12/26	06/22/26
485	Final Grade	4	06/18/26	06/23/26
490	Prep & Form	6	06/22/26	06/29/26
495	Rebar	3	06/26/26	06/30/26
500	Inspections	1	07/01/26	07/01/26
505	Pour	1	07/02/26	07/02/26
Area 3				
510	Lime Stabilize Subgrade	7	06/23/26	07/01/26
515	Final Grade	4	06/29/26	07/02/26
520	Prep & Form	6	07/01/26	07/08/26
525	Rebar	3	07/07/26	07/09/26
530	Inspections	1	07/10/26	07/10/26
535	Pour	1	07/13/26	07/13/26
Area 4				
540	Lime Stabilize Subgrade	7	07/02/26	07/10/26
545	Final Grade	4	07/08/26	07/13/26
550	Prep & Form	6	07/10/26	07/17/26
555	Rebar	3	07/16/26	07/20/26
560	Inspections	1	07/21/26	07/21/26
565	Pour	1	07/22/26	07/22/26
Area 5				
570	Lime Stabilize Subgrade	7	08/17/26	08/25/26
575	Final Grade	4	08/21/26	08/26/26
580	Prep & Form	6	08/25/26	09/01/26
585	Rebar	3	08/31/26	09/02/26
590	Inspections	1	09/03/26	09/03/26
595	Pour	1	09/04/26	09/04/26
Earthwork				
305	Cut and Stockpile Strippings	5	02/19/26	02/25/26
Phase 1 (Garage)				
Foundation				
605	Grid Lines H.1-G	8	02/26/26	03/09/26
610	Grid Lines G-F	5	03/10/26	03/16/26
615	Grid Lines F-E	5	03/17/26	03/23/26
620	Grid Lines E-D	5	03/24/26	03/30/26
625	Grid Lines D-C	5	03/31/26	04/06/26
630	Grid Lines C-B.1	5	04/07/26	04/13/26
635	Grid Lines B.1-A.1	8	04/14/26	04/23/26
Earthwork				
600	Garage Building Pad	3	04/24/26	04/28/26
Pre-Cast				
640	Panel Erection - Grid Lines H.1-G	8	06/03/26	06/12/26
645	Panel Erection - Grid Lines G-F	5	06/15/26	06/19/26
650	Panel Erection - Grid Lines F-E	5	06/22/26	06/26/26
655	Panel Erection - Grid Lines E-D	5	06/29/26	07/03/26
660	Panel Erection - Grid Lines D-C	5	07/06/26	07/10/26
665	Panel Erection - Grid Lines C-B.1	5	07/13/26	07/17/26
670	Panel Erection - Grid Lines B.1-A.1	8	07/20/26	07/29/26
Topping Slabs				
675	Level 5	5	07/30/26	08/05/26
680	Level 4	5	08/06/26	08/12/26
685	Level 3	5	08/13/26	08/19/26
690	Level 2	5	08/20/26	08/26/26
695	Level 1 (SOG)	5	09/11/26	09/17/26
Buildout				
697	Garage Doors	1	09/18/26	09/18/26
Elevators A & B				
Pit				
700	Excavate	1	07/30/26	07/30/26
705	Waterproof Pit Floor	1	07/31/26	07/31/26
710	Pour Pit Floor	1	08/03/26	08/03/26
715	F/R/P Pit Walls	1	08/04/26	08/04/26

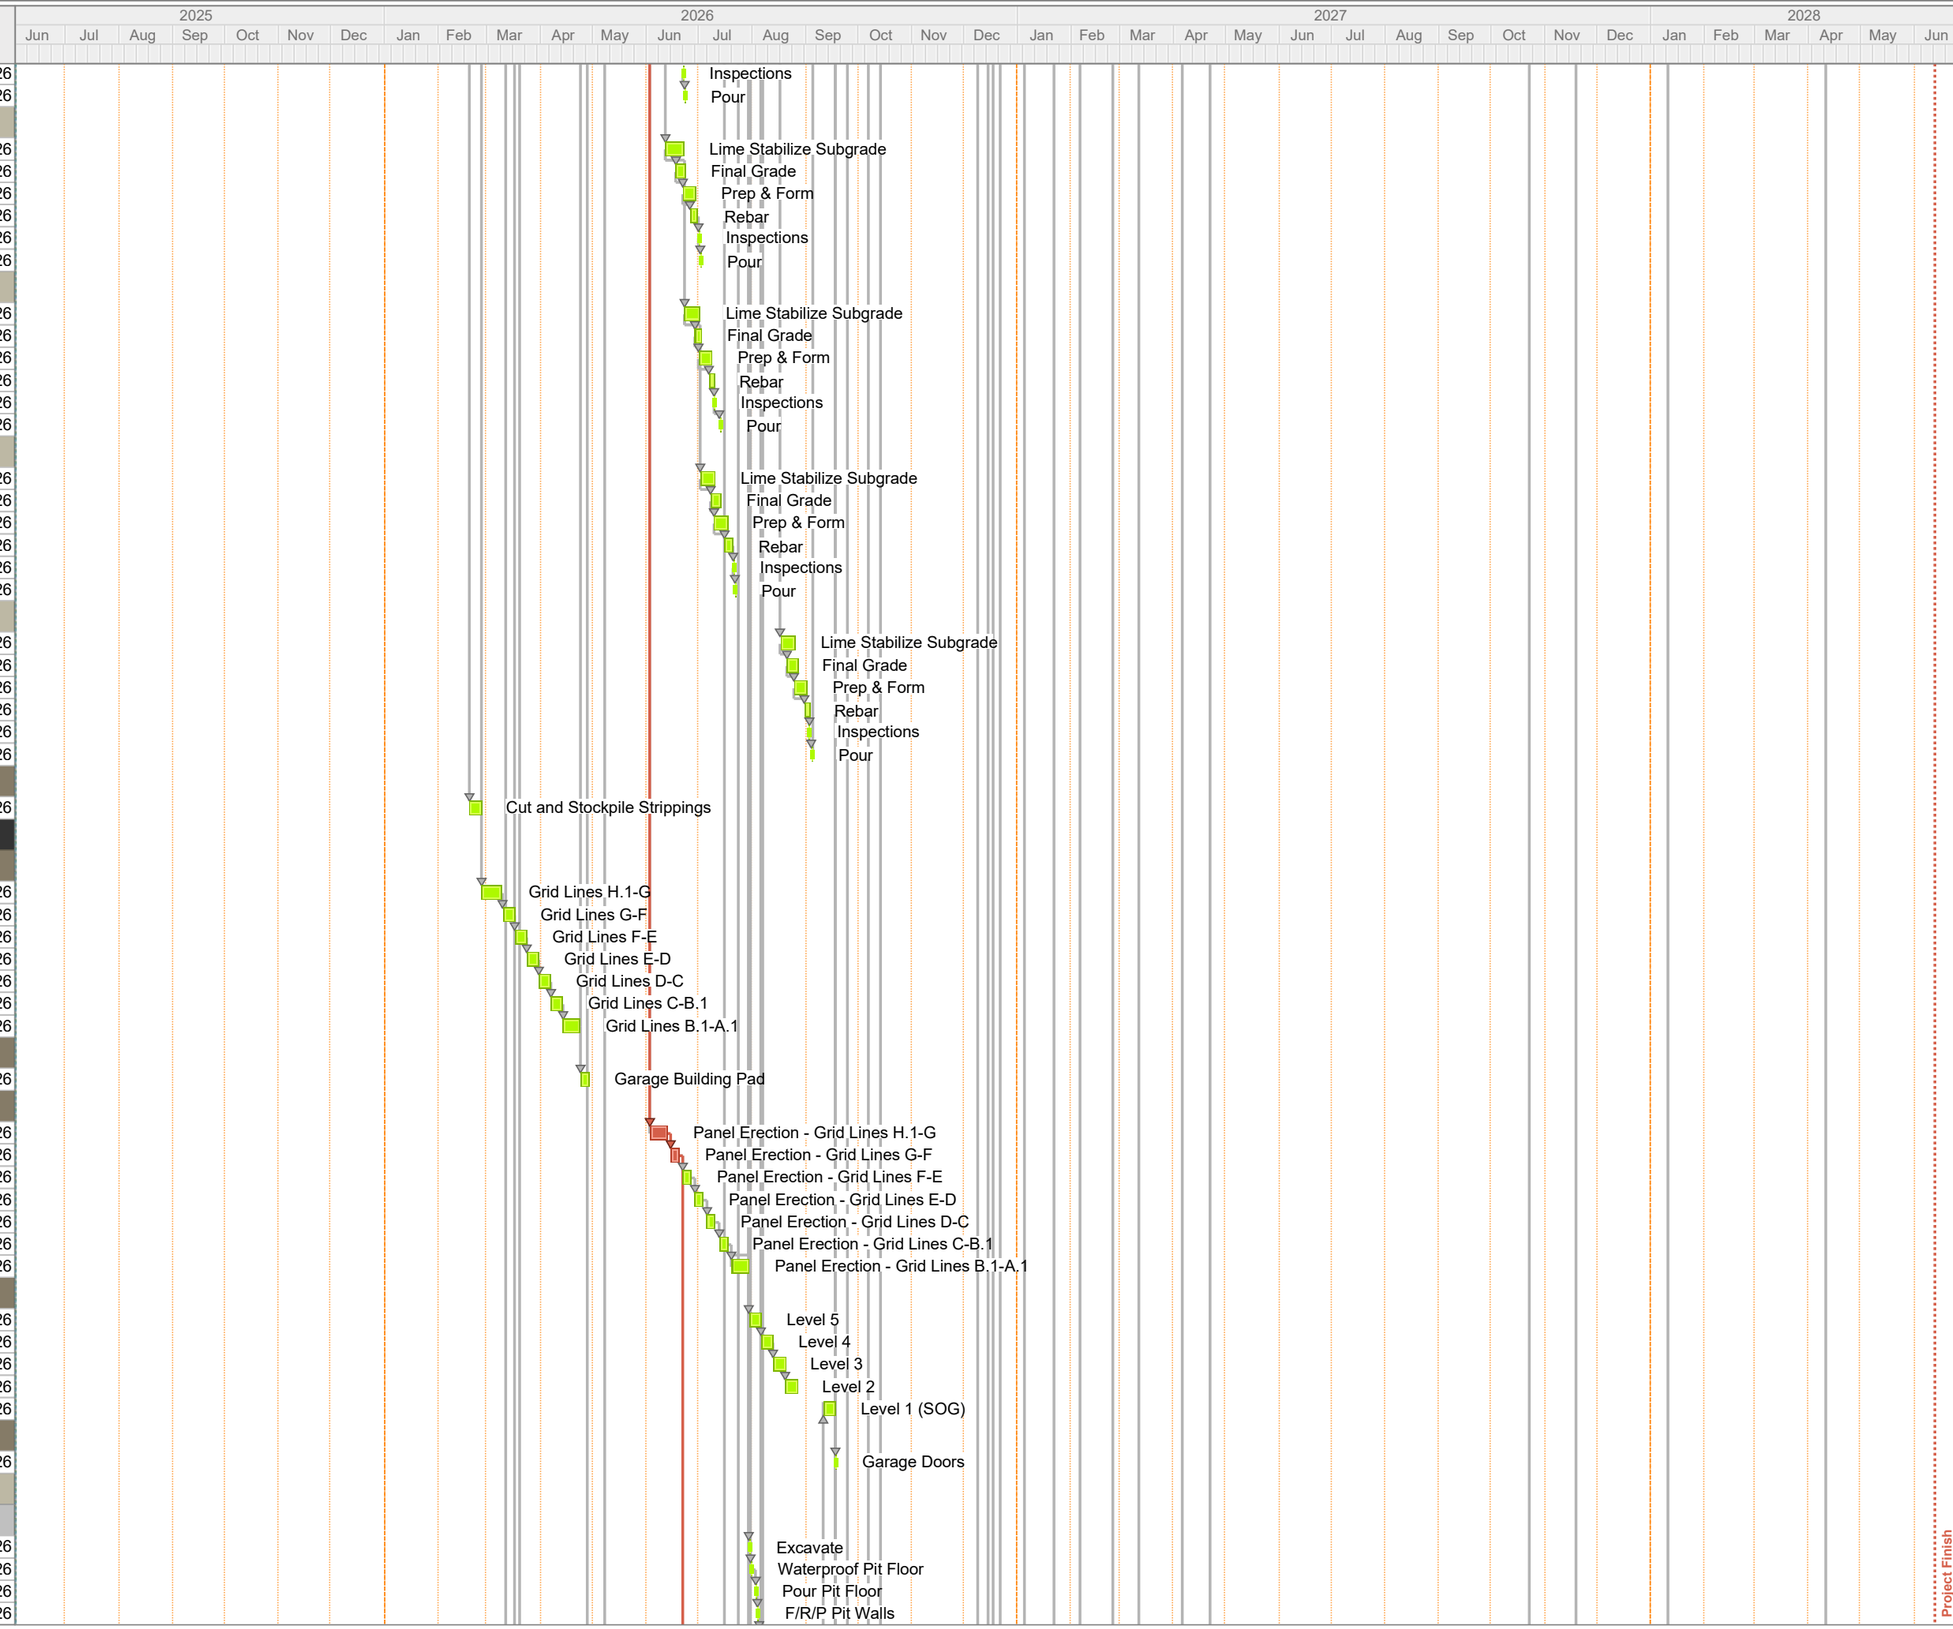

720	Waterproof Pit Walls	1	08/05/26	08/05/26
725	Backfill	1	08/06/26	08/06/26
Buildout				
730	Elevator A&B	30	09/18/26	10/29/26
735	CMU	1	09/18/26	09/18/26
740	Site Readiness Elevator Checklist	1	09/18/26	09/18/26
745	Rail Stack	1	09/21/26	09/21/26
750	Entrance	1	09/22/26	09/22/26
755	Wire Entrance	1	09/23/26	09/23/26
760	Fascia	1	09/24/26	09/24/26
765	Cab Shell	1	09/25/26	09/25/26
770	Wire Cab	1	09/28/26	09/28/26
775	Cab Interior	1	09/29/26	09/29/26
780	Install Complete/Work by Others	1	09/30/26	09/30/26
785	Hoistway Vent Louver & Wire	1	10/01/26	10/01/26
790	Hoistway Electrical R/I	1	10/02/26	10/02/26
795	Sump Pump / Grate & Test	1	10/05/26	10/05/26
800	Elevator Shaft Pre-Inspection	1	10/06/26	10/06/26
805	Adjusting/AHJ Testing	1	10/07/26	10/07/26
810	Turnover	1	10/09/26	10/09/26
Inspections				
815	STATE	1	10/08/26	10/08/26
820	TEMPORARY USE PERMIT	1	10/08/26	10/08/26
Grease Trap				
825	Grease trap	30	07/30/26	09/10/26
830	Set Grease Trap	1	07/29/26	07/29/26
835	Grease Trap Final Connections	3	07/30/26	08/03/26
Fire Pump Room				
850	Equipment Pads (Tank,FP,JP,DP)	3	09/18/26	09/22/26
851	Set Break Tank	3	09/23/26	09/25/26
855	Layout	1	09/28/26	09/28/26
860	CMU	5	09/29/26	10/05/26
865	Mechanical	2	10/06/26	10/07/26
870	Electrical	6	10/08/26	10/15/26
871	Plumbing	6	10/16/26	10/23/26
872	Fire Sprinkler	1	10/26/26	10/26/26
880	Break Tank Final Connections	10	10/27/26	11/09/26
885	Commission Break Tank	1	11/10/26	11/10/26
890	Set Fire & Jockey Pumps	2	11/03/26	11/04/26
895	Fire & Jockey Pump Final Connections	10	11/10/26	11/23/26
900	Set Fire Pump Controller	1	11/05/26	11/05/26
905	Fire Pump Controller Final Connection:	5	11/24/26	12/01/26
910	Jockey & Fire Pump Startup	1	12/02/26	12/02/26
915	Set Domestic Booster Pump	2	11/06/26	11/09/26
920	Domestic Pump Final Connections	5	12/02/26	12/08/26
925	Domestic Water Pump Startup	1	12/09/26	12/09/26
Stair				
A				
840	Stair A	30	09/18/26	10/29/26
B				
845	Stair B	30	09/18/26	10/29/26
Maintanence				
940	Maintanence	30	10/06/26	11/16/26
Trash Room				
945	Trash Room	30	10/16/26	11/27/26
Electrical Room				
950	Electrical Room	30	10/26/26	12/07/26
Pool Equipment Room				
955	Pool Equipment Room	30	11/10/26	12/22/26
Final Inspections				
960	Fire Pump Room Final	2	12/10/26	12/11/26

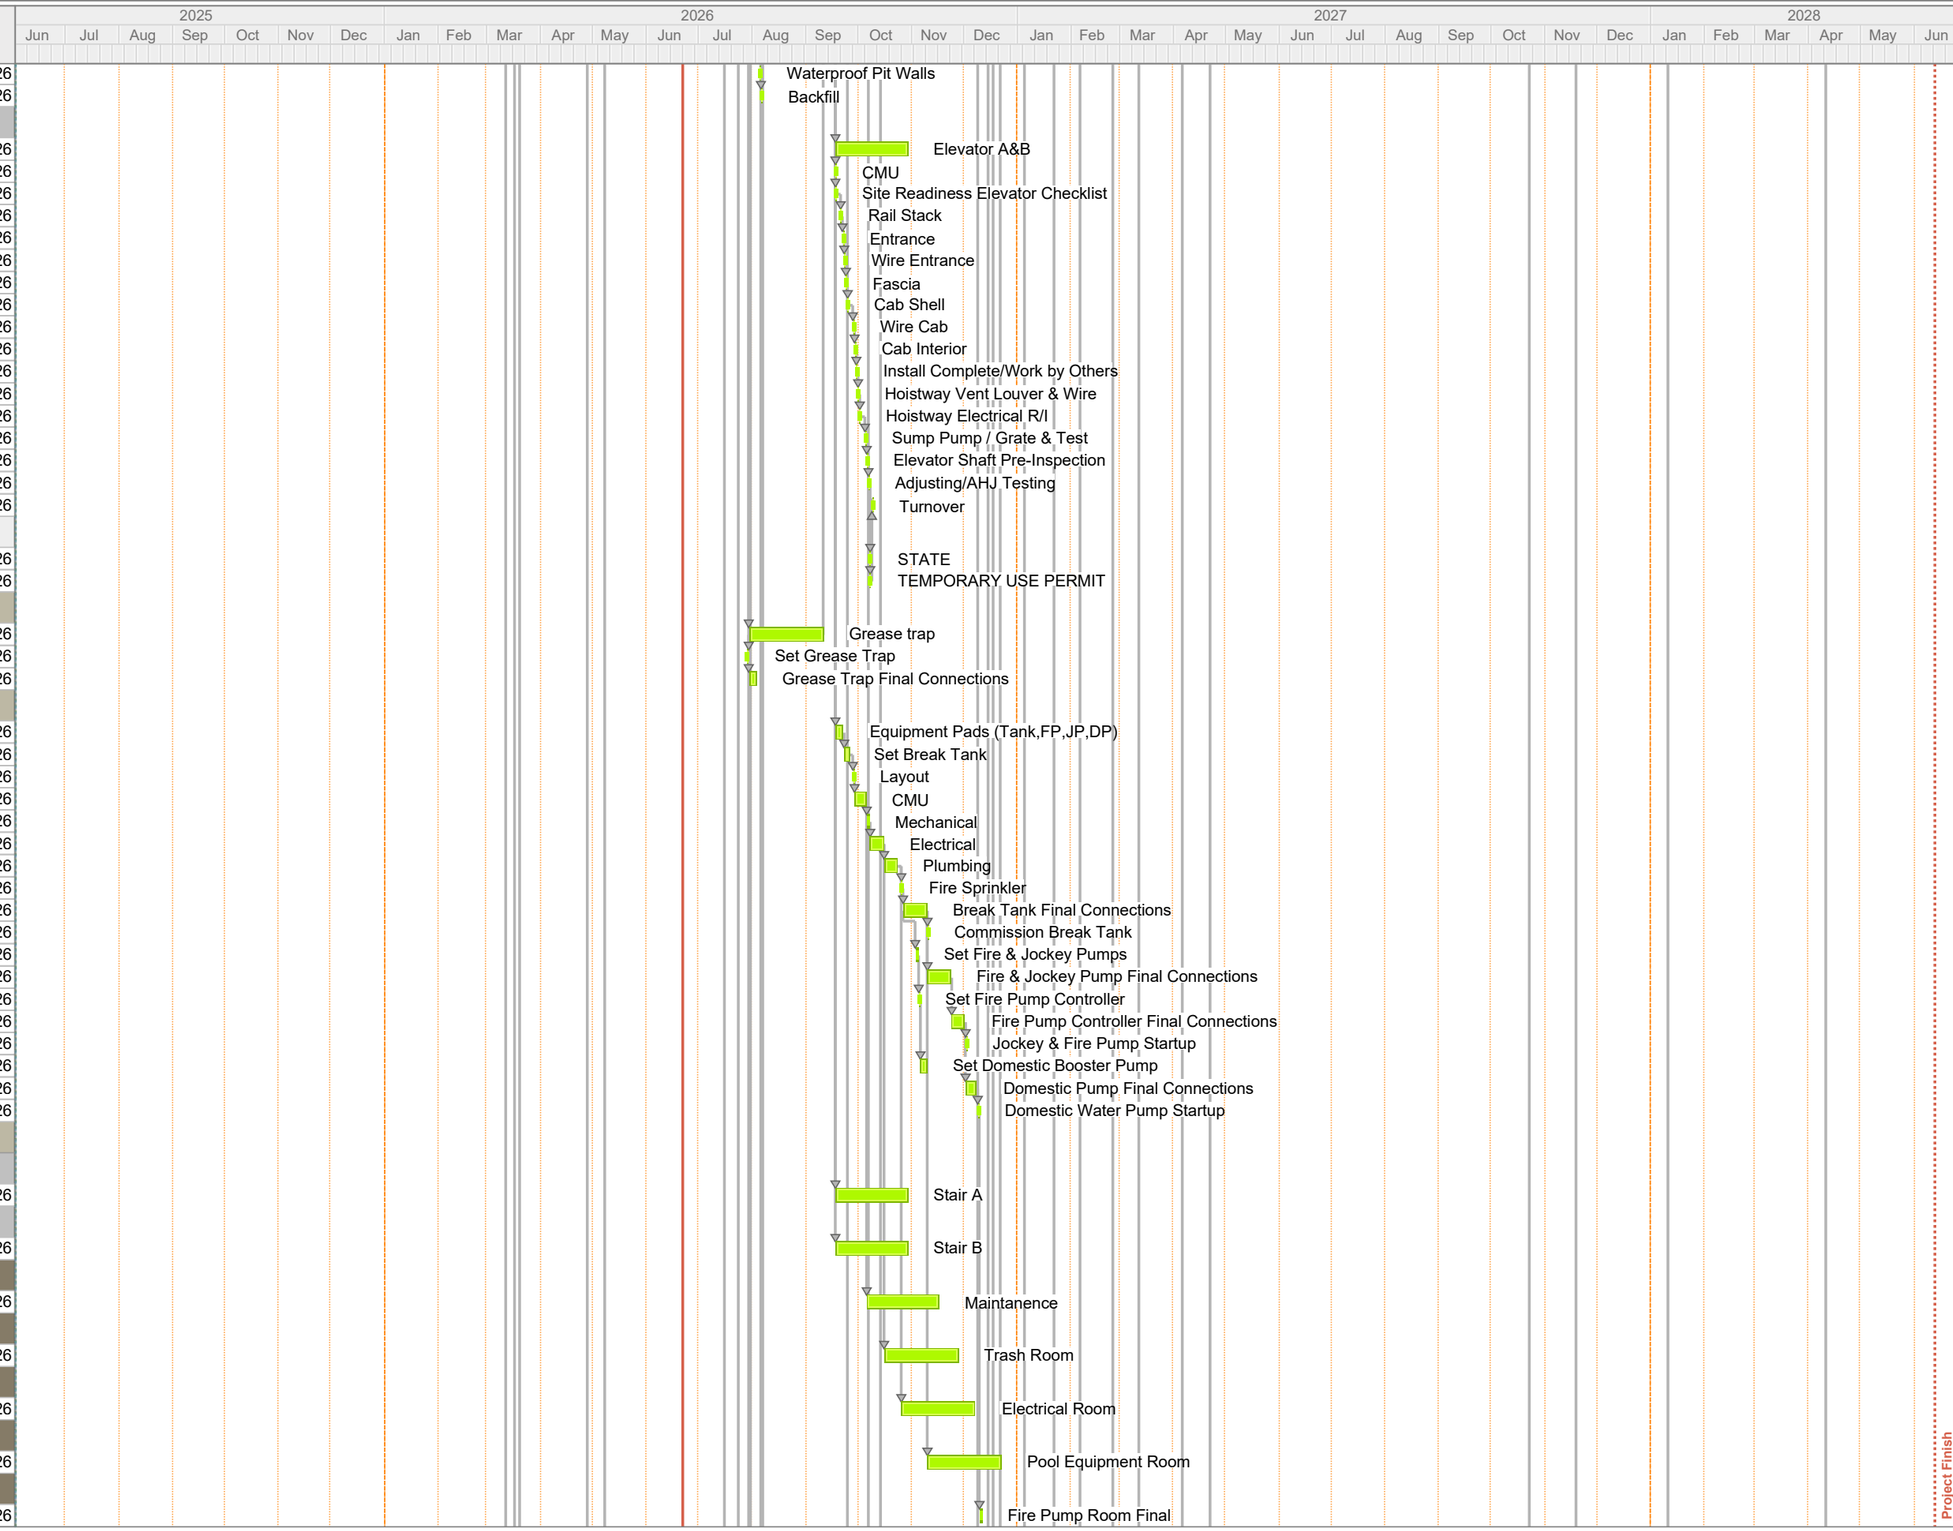

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

Phase 1 (111 Units)				
Slab on Grade				
Pour #05				
Earthwork				
965	Building Pad (Pour #05)	3	03/31/26	04/02/26
Concrete				
970	Batter Boards	1	04/03/26	04/03/26
975	Plumbing Underground	1	04/06/26	04/06/26
980	Backfill Plumbing	1	04/08/26	04/08/26
985	Grade Pad	1	04/09/26	04/09/26
990	Form SOG	1	04/10/26	04/10/26
995	Termite Treatment	1	04/13/26	04/13/26
1000	Vapor Barrier	1	04/13/26	04/13/26
1005	Under Slab Electrical	1	04/14/26	04/14/26
1010	Rebar/PT Cables	1	04/15/26	04/15/26
1015	Hardware/Anchor Bolts	1	04/16/26	04/16/26
1020	Prep For Inspection	1	04/17/26	04/17/26
1025	Pour SOG	1	04/22/26	04/22/26
1030	Remove Forms	1	04/23/26	04/23/26
1035	Breaks, Stress, EOR Approval, Cut & (	5	04/24/26	04/30/26
Inspections				
1040	PLUMBING	1	04/07/26	04/07/26
1045	ELECTRICAL	1	04/14/26	04/14/26
1050	STRUCTURAL	1	04/20/26	04/20/26
1055	3RD PARTY - STRUCTURAL	1	04/21/26	04/21/26
Pour #06				
Earthwork				
1060	Building Pad (Pour #06)	2	04/03/26	04/06/26
Concrete				
1065	Batter Boards	1	04/07/26	04/07/26
1070	Plumbing Underground	1	04/08/26	04/08/26
1075	Backfill Plumbing	1	04/10/26	04/10/26
1080	Grade Pad	1	04/13/26	04/13/26
1085	Form SOG	1	04/14/26	04/14/26
1090	Termite Treatment	1	04/15/26	04/15/26
1095	Vapor Barrier	1	04/15/26	04/15/26
1100	Under Slab Electrical	1	04/16/26	04/16/26
1105	Rebar/PT Cables	1	04/17/26	04/17/26
1110	Hardware/Anchor Bolts	1	04/20/26	04/20/26
1115	Prep For Inspection	1	04/21/26	04/21/26
1120	Pour SOG	1	04/24/26	04/24/26
1125	Remove Forms	1	04/27/26	04/27/26
1130	Breaks, Stress, EOR Approval, Cut & (	5	04/28/26	05/04/26
Inspections				
1135	PLUMBING	1	04/09/26	04/09/26
1140	ELECTRICAL	1	04/16/26	04/16/26
1145	STRUCTURAL	1	04/22/26	04/22/26
1150	3RD PARTY - STRUCTURAL	1	04/23/26	04/23/26
Pour #07				
Earthwork				
1155	Building Pad (Pour #07)	4	06/22/26	06/25/26
Concrete				
1160	Batter Boards	1	06/26/26	06/26/26
1165	Plumbing Underground	1	06/29/26	06/29/26
1170	Backfill Plumbing	1	07/01/26	07/01/26
1175	Grade Pad	1	07/02/26	07/02/26
1180	Form SOG	1	07/03/26	07/03/26
1185	Termite Treatment	1	07/06/26	07/06/26
1190	Vapor Barrier	1	07/06/26	07/06/26
1195	Under Slab Electrical	1	07/07/26	07/07/26
1200	Rebar/PT Cables	1	07/08/26	07/08/26
1205	Hardware/Anchor Bolts	1	07/09/26	07/09/26
1210	Prep For Inspection	1	07/10/26	07/10/26
1215	Pour SOG	1	07/15/26	07/15/26
1220	Remove Forms	1	07/16/26	07/16/26

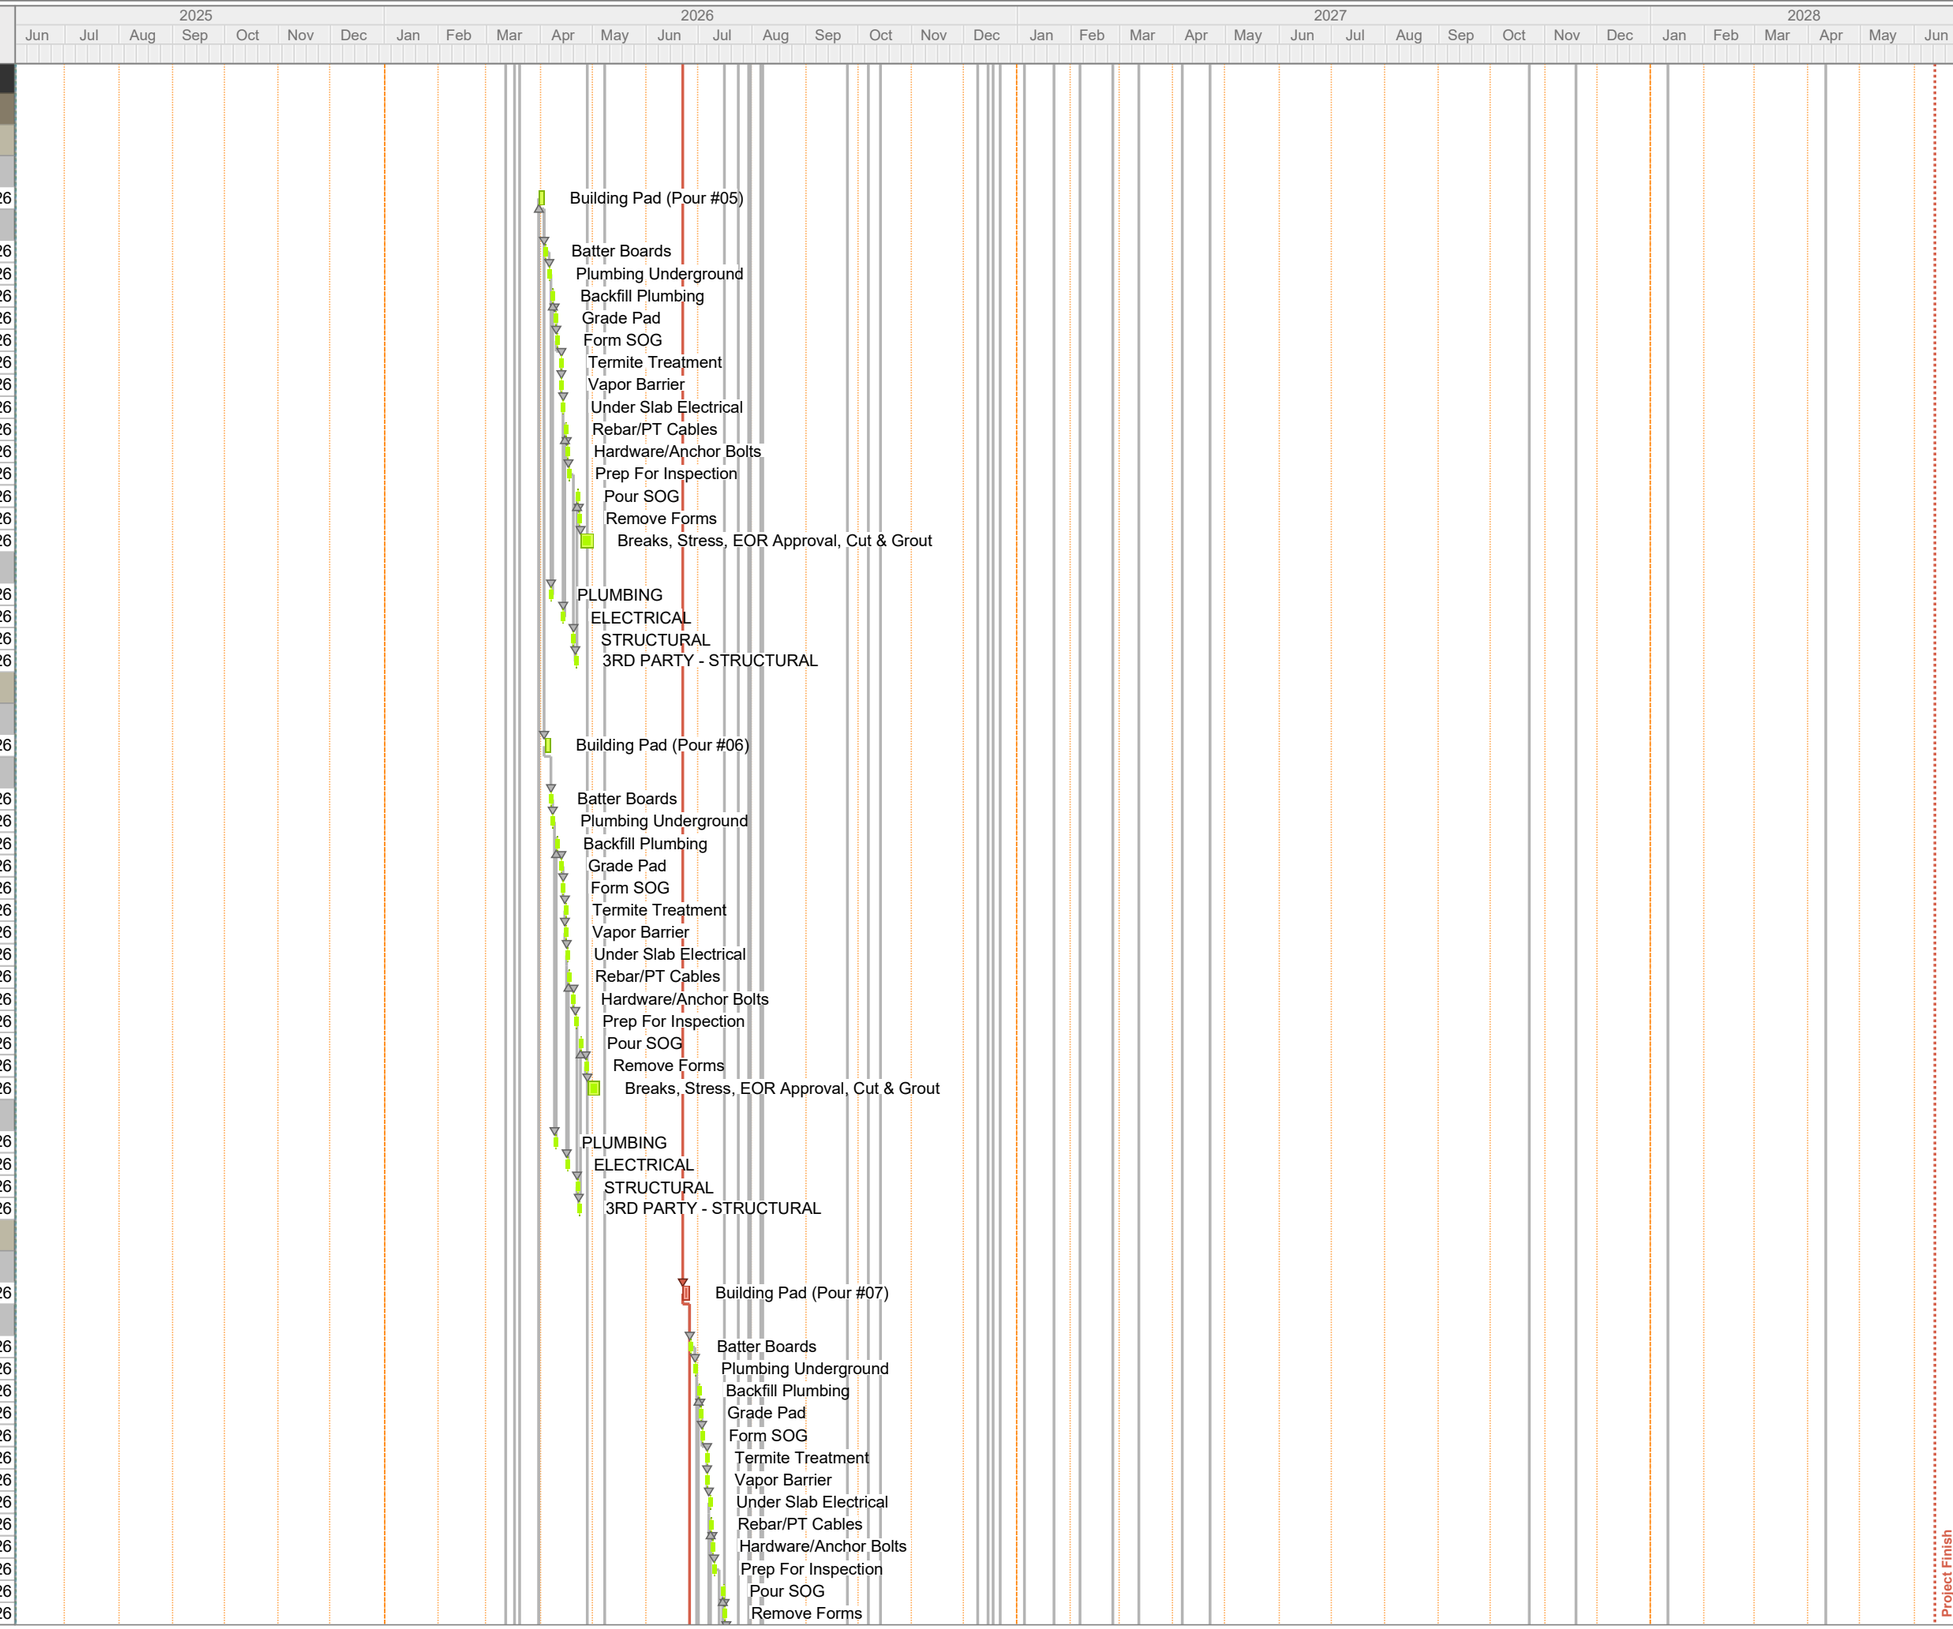

Initials: _____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

1225	Breaks, Stress, EOR Approval, Cut & (	5	07/17/26	07/23/26
Inspections				
1230	PLUMBING	1	06/30/26	06/30/26
1235	ELECTRICAL	1	07/07/26	07/07/26
1240	STRUCTURAL	1	07/13/26	07/13/26
1245	3RD PARTY - STRUCTURAL	1	07/14/26	07/14/26
Pour #08				
Earthwork				
1250	Building Pad (Pour #08)	2	06/26/26	06/29/26
Concrete				
1255	Batter Boards	1	06/30/26	06/30/26
1260	Plumbing Underground	1	07/01/26	07/01/26
1265	Backfill Plumbing	1	07/03/26	07/03/26
1270	Grade Pad	1	07/06/26	07/06/26
1275	Form SOG	1	07/07/26	07/07/26
1280	Termite Treatment	1	07/08/26	07/08/26
1285	Vapor Barrier	1	07/08/26	07/08/26
1290	Under Slab Electrical	1	07/09/26	07/09/26
1295	Rebar/PT Cables	1	07/10/26	07/10/26
1300	Hardware/Anchor Bolts	1	07/13/26	07/13/26
1305	Prep For Inspection	1	07/14/26	07/14/26
1310	Pour SOG	1	07/17/26	07/17/26
1315	Remove Forms	1	07/20/26	07/20/26
1320	Breaks, Stress, EOR Approval, Cut & (	5	07/21/26	07/27/26
Inspections				
1325	PLUMBING	1	07/02/26	07/02/26
1330	ELECTRICAL	1	07/09/26	07/09/26
1335	STRUCTURAL	1	07/15/26	07/15/26
1340	3RD PARTY - STRUCTURAL	1	07/16/26	07/16/26
Lvl. 1				
Wood Framing				
Area A				
1345	Layout	1	05/19/26	05/19/26
1350	Frame Walls	2	05/20/26	05/21/26
1355	Plumb Line Walls	1	05/22/26	05/22/26
1360	Wall Sheathing	2	05/26/26	05/27/26
1365	Floor Joists	2	05/28/26	05/29/26
1370	Floor Decking	2	06/01/26	06/02/26
Inspections				
1375	STRUCTURAL	1	06/03/26	06/03/26
Area B				
1380	Layout	1	07/27/26	07/27/26
1385	Frame Walls	2	07/28/26	07/29/26
1390	Plumb Line Walls	1	07/30/26	07/30/26
1395	Wall Sheathing	2	07/31/26	08/03/26
1400	Floor Joists	2	08/04/26	08/05/26
1405	Floor Decking	2	08/06/26	08/07/26
Inspections				
1410	STRUCTURAL	1	08/10/26	08/10/26
MEPF				
1415	Plumbing R/I	3	10/06/26	10/08/26
1420	Fire Sprinkler	3	10/09/26	10/13/26
1425	Electrical R/I	3	10/14/26	10/16/26
1430	Mechanical R/I	3	10/15/26	10/19/26
1435	Low Votltage RI	3	10/16/26	10/20/26
1440	MEP 1st Trim	3	11/18/26	11/20/26
1445	Hot Punch	2	12/15/26	12/16/26
1450	HVAC Startup	3	12/17/26	12/21/26
1455	MEP 2nd Trim	2	12/17/26	12/18/26
1460	Low Voltage Trim Out	2	12/17/26	12/18/26
Inspections				
1465	PLUMBING	1	10/09/26	10/09/26
1470	PIPE SIZE & HANGER	1	10/14/26	10/14/26
1475	FIRE SPRINKLER HYDRO	1	10/15/26	10/15/26
1480	MECHANICAL	1	10/20/26	10/20/26

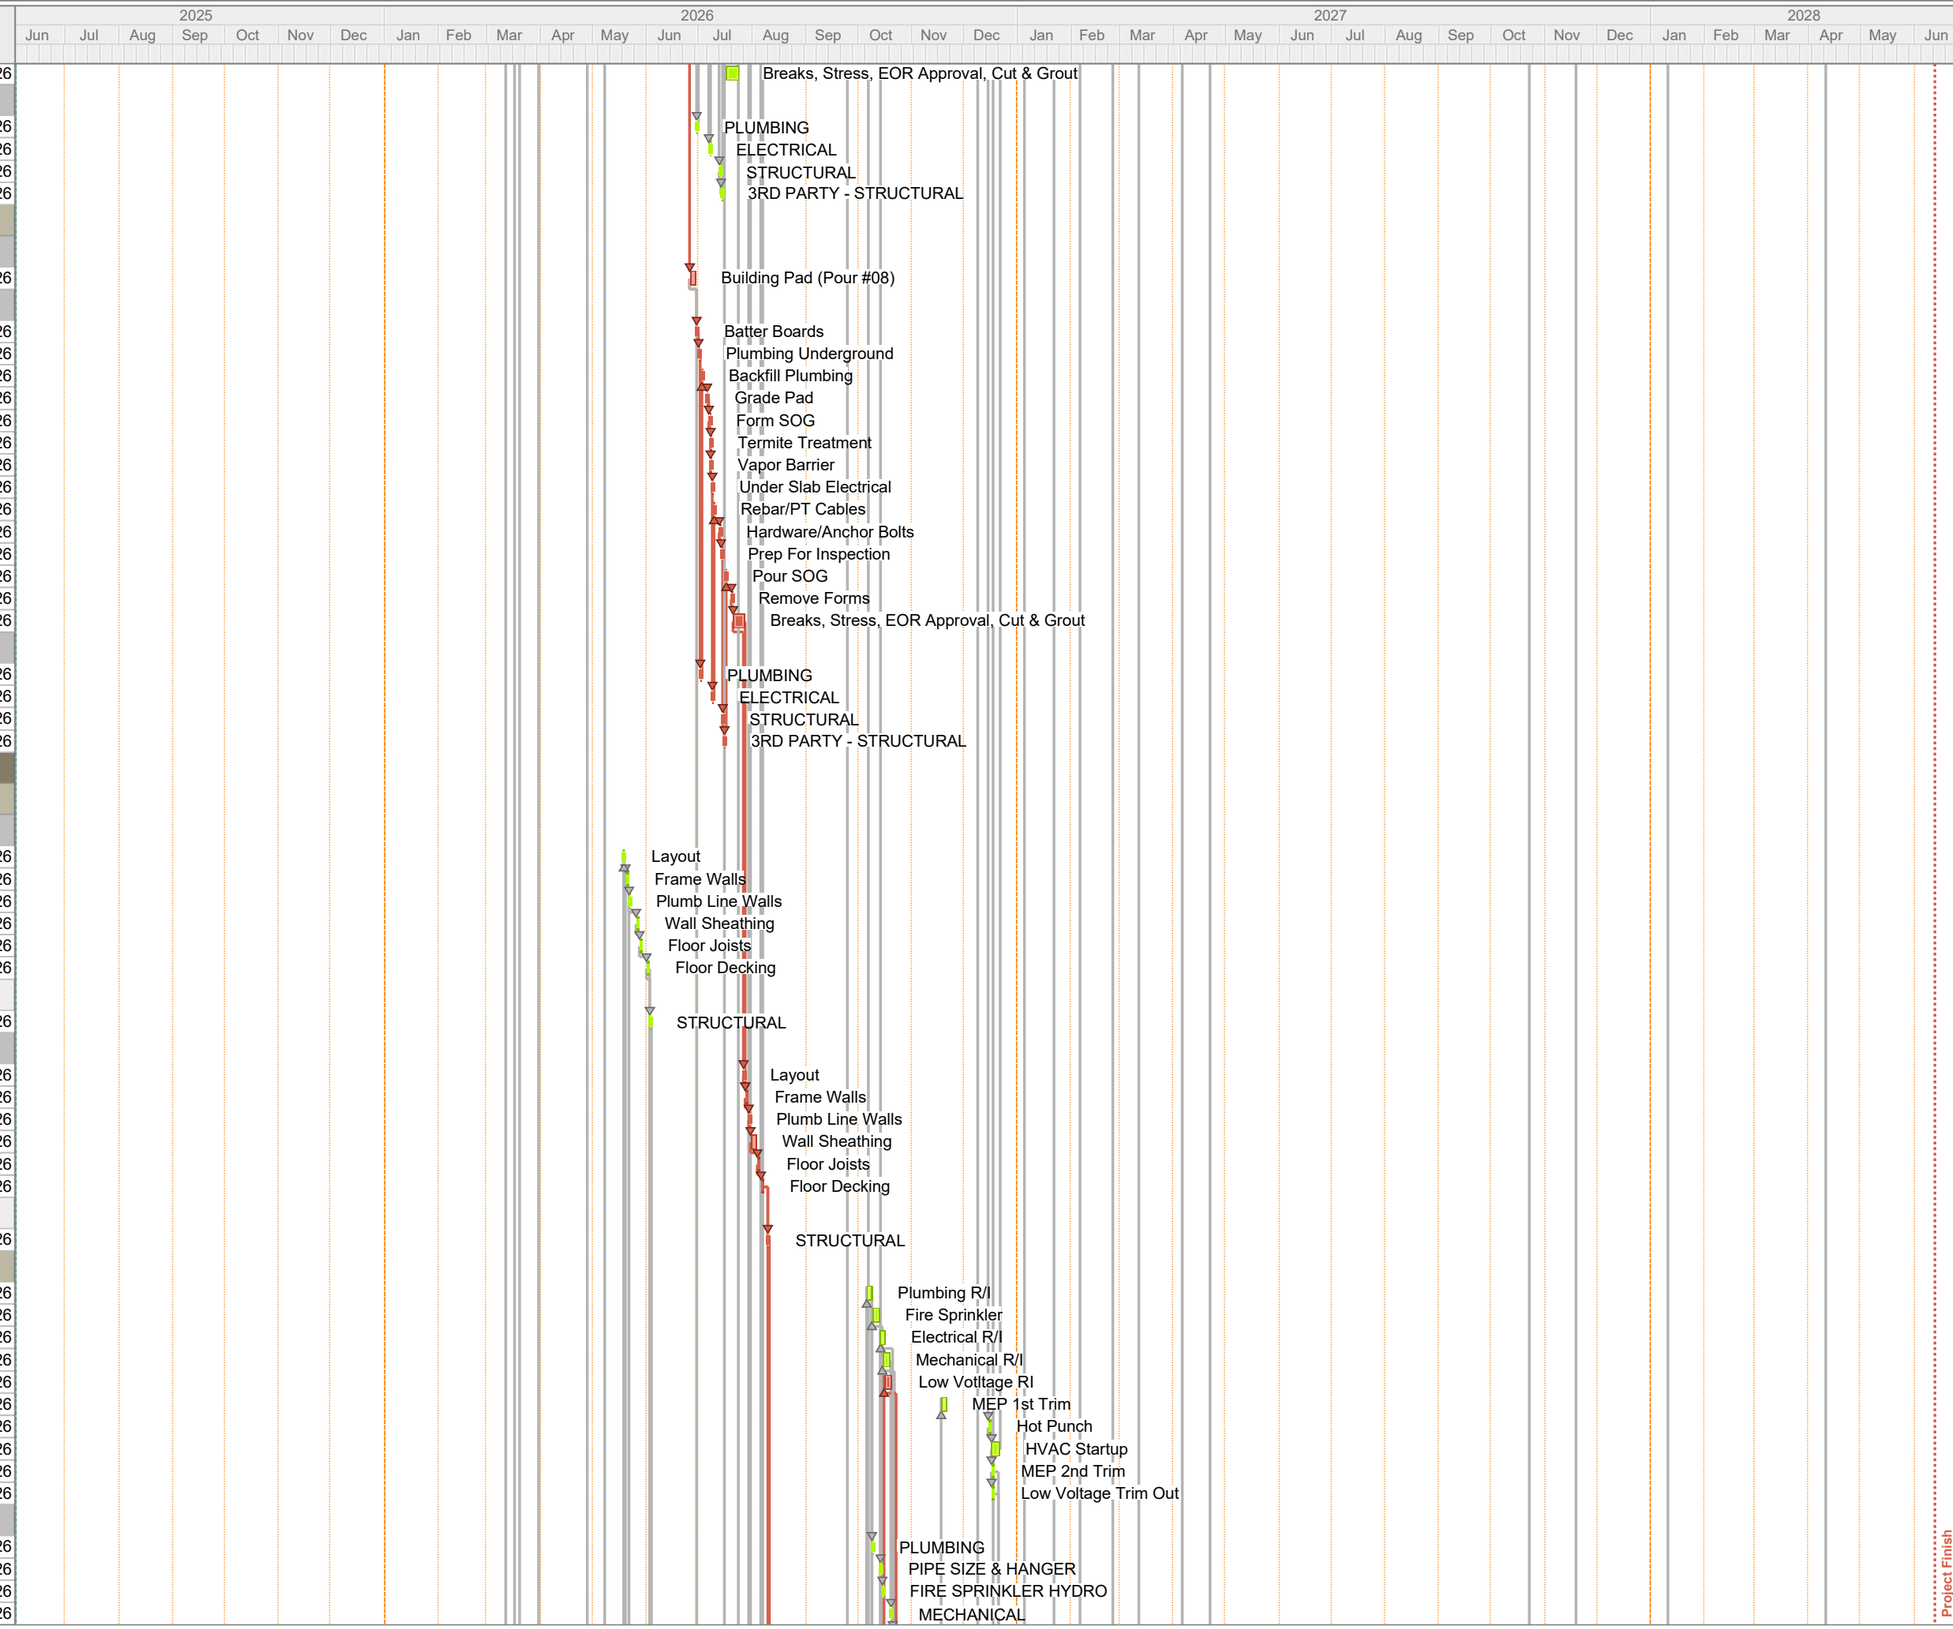

1485	ELECTRICAL	1	10/21/26	10/21/26
Buildout				
1490	Pre-Rock	1	10/23/26	10/23/26
1495	Gypcrete Pre-Pour (Tub & Shower)	1	10/26/26	10/26/26
1500	Insulation	1	10/27/26	10/27/26
1505	Drywall	4	10/29/26	11/03/26
1510	Tub/Shower Pans	1	11/04/26	11/04/26
1515	Gypcrete	1	11/04/26	11/04/26
1520	Tape/Float/Sand Walls & Ceilings	6	11/05/26	11/12/26
1525	Spray Texture	2	11/12/26	11/13/26
1530	Doors & Trim	2	11/13/26	11/16/26
1535	Prime & 1st Coat Paint	1	11/17/26	11/17/26
1540	Tub/Shower Wall Tile	4	11/18/26	11/23/26
1545	Bathroom Floor Tile	4	11/25/26	12/01/26
1550	Shower Doors & Mirrors	2	12/02/26	12/03/26
1555	Toilet Accessories	1	12/04/26	12/04/26
1560	Cabinets	3	11/18/26	11/20/26
1565	Countertops	2	11/23/26	11/24/26
1570	Drywall Touch Up	1	11/25/26	11/25/26
1575	Tile Backsplash	4	12/02/26	12/07/26
1580	LVT	5	12/21/26	12/28/26
1585	Shoe/Scribe Molding	2	12/28/26	12/29/26
1590	Rough Clean	2	12/29/26	12/30/26
1595	Completion List	1	12/31/26	12/31/26
1600	Appliances	1	01/04/27	01/04/27
1605	Blinds	1	01/05/27	01/05/27
1610	Final Paint	1	01/06/27	01/06/27
Inspections				
1615	STRUCTURAL	1	10/22/26	10/22/26
1620	INSULATION	1	10/28/26	10/28/26
Interior Punch List				
1625	Arch-Con Punch List	2	01/07/27	01/08/27
1630	Arch-Con Punch List Corrections	2	01/11/27	01/12/27
1635	Final Clean	1	01/13/27	01/13/27
1640	Owner Punch List	2	01/14/27	01/15/27
1645	Punch List Corrections	2	01/18/27	01/19/27
1650	Powder Puff	1	01/20/27	01/20/27
1655	Owner Acceptance	1	01/21/27	01/21/27
Lvl. 2				
Wood Framing				
Area A				
1660	Layout	1	06/03/26	06/03/26
1665	Frame Walls	2	06/04/26	06/05/26
1670	Plumb Line Walls	1	06/08/26	06/08/26
1675	Wall Sheathing	2	06/09/26	06/10/26
1680	Floor Joists	2	06/11/26	06/12/26
1685	Floor Decking	2	06/15/26	06/16/26
Inspections				
1690	STRUCTURAL	1	06/17/26	06/17/26
Area B				
1695	Layout	1	08/10/26	08/10/26
1700	Frame Walls	2	08/11/26	08/12/26
1705	Plumb Line Walls	1	08/13/26	08/13/26
1710	Wall Sheathing	2	08/14/26	08/17/26
1715	Floor Joists	2	08/18/26	08/19/26
1720	Floor Decking	2	08/20/26	08/21/26
Inspections				
1725	STRUCTURAL	1	08/24/26	08/24/26
MEPF				
1730	Plumbing R/I	4	10/09/26	10/14/26
1735	Fire Sprinkler	4	10/15/26	10/20/26
1740	Electrical R/I	4	10/21/26	10/26/26
1745	Mechanical R/I	4	10/22/26	10/27/26
1750	Low Votltage RI	4	10/23/26	10/28/26
1755	MEP 1st Trim	3	12/03/26	12/07/26
1760	Hot Punch	2	12/08/26	12/09/26

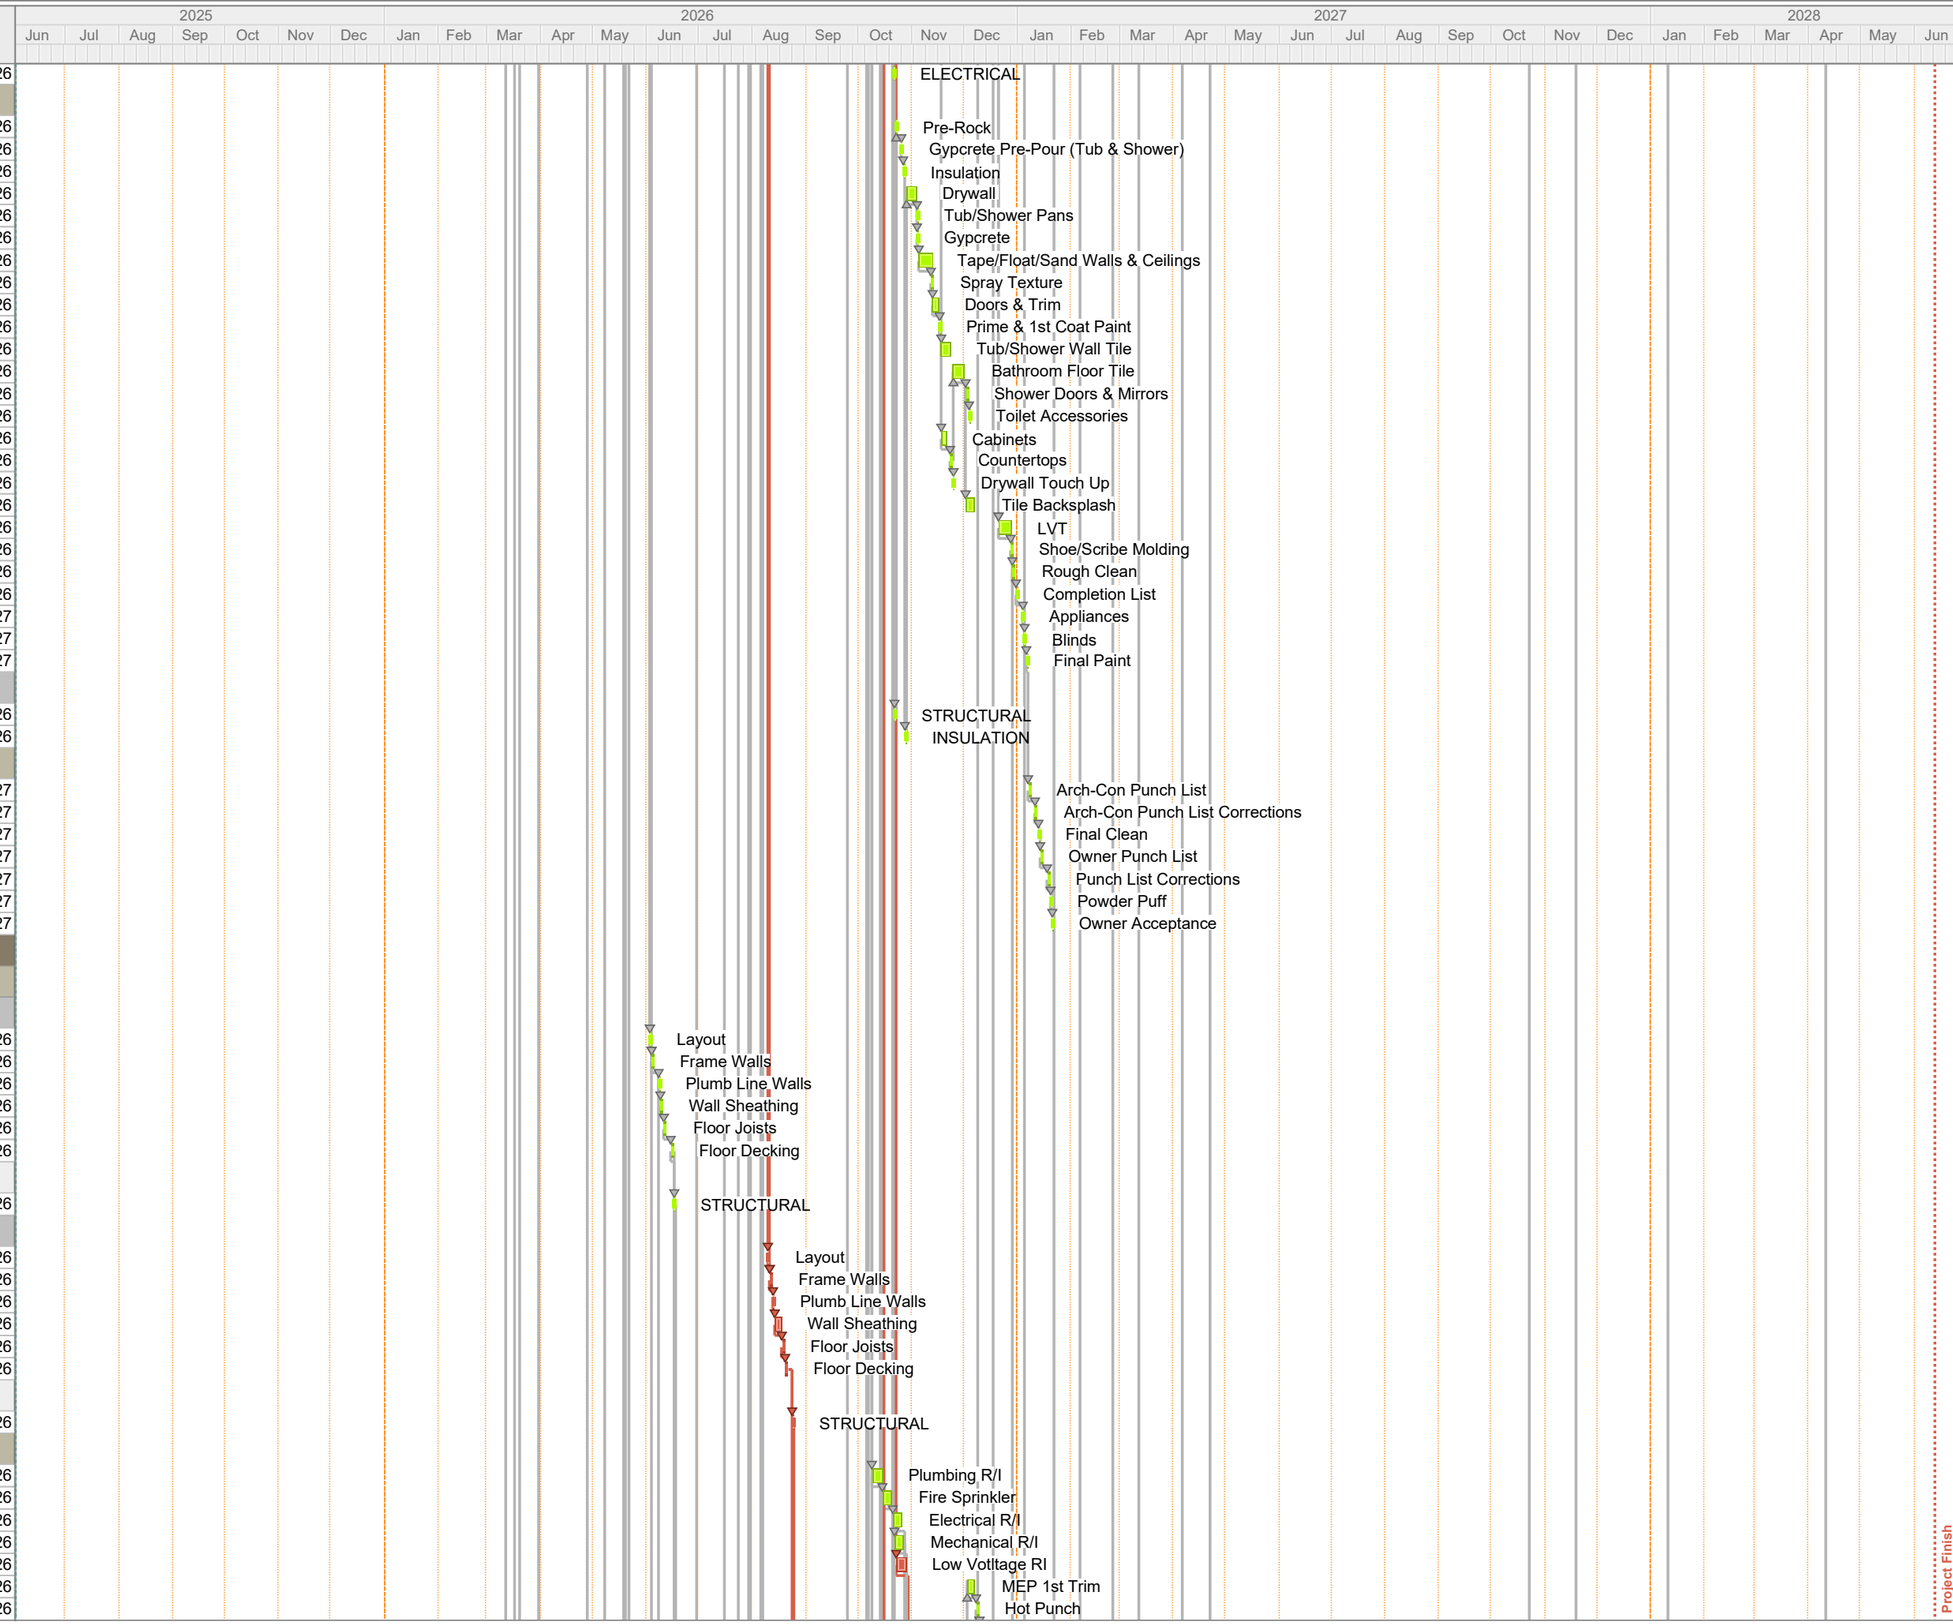

1765	HVAC Startup	3	12/10/26	12/14/26
1770	MEP 2nd Trim	2	12/23/26	12/24/26
1775	Low Voltage Trim Out	2	12/23/26	12/24/26
Inspections				
1780	PLUMBING	1	10/15/26	10/15/26
1785	PIPE SIZE & HANGER	1	10/21/26	10/21/26
1790	FIRE SPRINKLER HYDRO	1	10/22/26	10/22/26
1795	MECHANICAL	1	10/28/26	10/28/26
1800	ELECTRICAL	1	10/29/26	10/29/26
Buildout				
1805	Pre-Rock	1	11/02/26	11/02/26
1810	Gypcrete Pre-Pour (Tub & Shower)	1	11/03/26	11/03/26
1815	Insulation	2	11/04/26	11/05/26
1820	Drywall	5	11/09/26	11/13/26
1825	Tub/Shower Pans	1	11/16/26	11/16/26
1830	Gypcrete	1	11/16/26	11/16/26
1835	Tape/Float/Sand Walls & Ceilings	7	11/17/26	11/25/26
1840	Spray Texture	2	11/25/26	11/27/26
1845	Doors & Trim	3	11/27/26	12/01/26
1850	Prime & 1st Coat Paint	2	12/01/26	12/02/26
1855	Tub/Shower Wall Tile	4	12/03/26	12/08/26
1860	Bathroom Floor Tile	4	12/11/26	12/16/26
1865	Shower Doors & Mirrors	2	12/17/26	12/18/26
1870	Toilet Accessories	1	12/21/26	12/21/26
1875	Cabinets	4	12/03/26	12/08/26
1880	Countertops	2	12/09/26	12/10/26
1885	Drywall Touch Up	1	12/11/26	12/11/26
1890	Tile Backsplash	4	12/17/26	12/22/26
1895	LVT	7	12/29/26	01/07/27
1900	Shoe/Scribe Molding	2	01/07/27	01/08/27
1905	Rough Clean	2	01/08/27	01/11/27
1910	Completion List	1	01/12/27	01/12/27
1915	Appliances	1	01/13/27	01/13/27
1920	Blinds	1	01/14/27	01/14/27
1925	Final Paint	1	01/15/27	01/15/27
Inspections				
1930	STRUCTURAL	1	10/30/26	10/30/26
1935	INSULATION	1	11/06/26	11/06/26
Interior Punch List				
1940	Arch-Con Punch List	3	01/18/27	01/20/27
1945	Arch-Con Punch List Corrections	2	01/20/27	01/21/27
1950	Final Clean	1	01/22/27	01/22/27
1955	Owner Punch List	3	01/25/27	01/27/27
1960	Punch List Corrections	3	01/28/27	02/01/27
1965	Powder Puff	1	02/01/27	02/01/27
1970	Owner Acceptance	2	02/02/27	02/03/27
Lvl. 3				
Wood Framing				
Area A				
1975	Layout	1	06/17/26	06/17/26
1980	Frame Walls	2	06/18/26	06/19/26
1985	Plumb Line Walls	1	06/22/26	06/22/26
1990	Wall Sheathing	2	06/23/26	06/24/26
1995	Floor Joists	2	06/25/26	06/26/26
2000	Floor Decking	2	06/29/26	06/30/26
Inspections				
2005	STRUCTURAL	1	07/01/26	07/01/26
Area B				
2010	Layout	1	08/24/26	08/24/26
2015	Frame Walls	2	08/25/26	08/26/26
2020	Plumb Line Walls	1	08/27/26	08/27/26
2025	Wall Sheathing	2	08/28/26	08/31/26
2030	Floor Joists	2	09/01/26	09/02/26
2035	Floor Decking	2	09/03/26	09/04/26
Inspections				
2040	STRUCTURAL	1	09/08/26	09/08/26

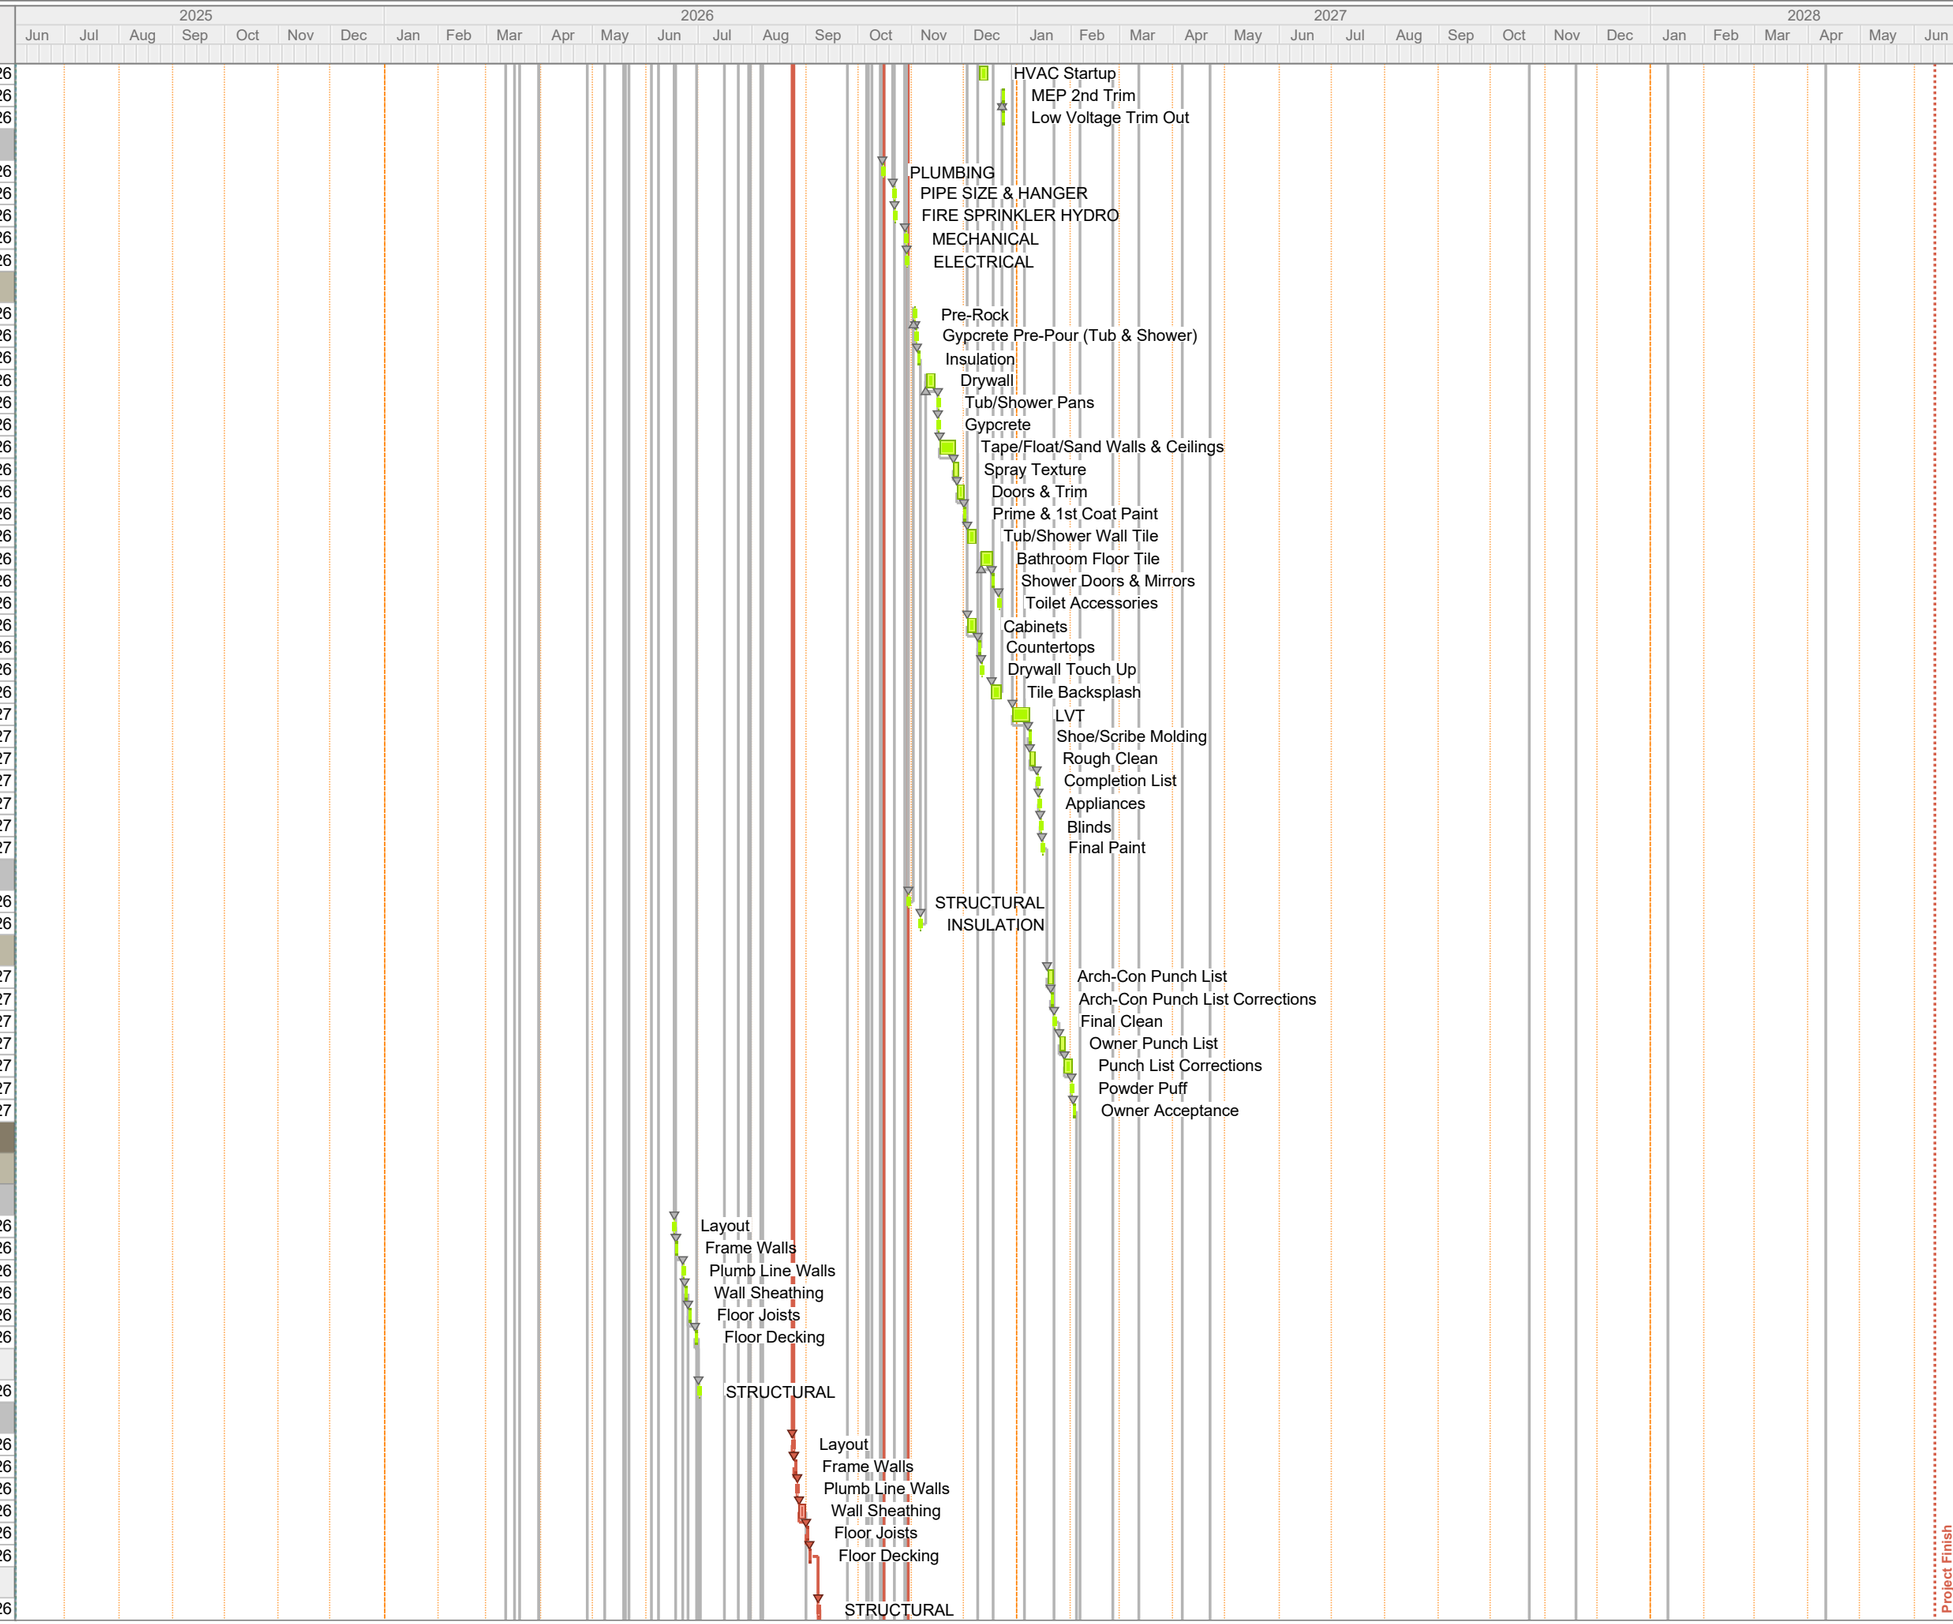

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

MEPF				
2045	Plumbing R/I	5	10/16/26	10/22/26
2050	Fire Sprinkler	5	10/22/26	10/28/26
2055	Electrical R/I	5	10/28/26	11/03/26
2060	Mechanical R/I	5	10/29/26	11/04/26
2065	Low Votltage RI	5	10/30/26	11/05/26
2070	MEP 1st Trim	3	12/15/26	12/17/26
2075	Hot Punch	2	12/18/26	12/21/26
2080	HVAC Startup	3	12/22/26	12/24/26
2085	MEP 2nd Trim	2	01/07/27	01/08/27
2090	Low Voltage Trim Out	2	01/07/27	01/08/27
Inspections				
2095	PLUMBING	1	10/23/26	10/23/26
2100	PIPE SIZE & HANGER	1	10/28/26	10/28/26
2105	FIRE SPRINKLER HYDRO	1	10/29/26	10/29/26
2110	MECHANICAL	1	11/05/26	11/05/26
2115	ELECTRICAL	1	11/06/26	11/06/26
Buildout				
2120	Pre-Rock	1	11/10/26	11/10/26
2125	Gypcrete Pre-Pour (Tub & Shower)	1	11/11/26	11/11/26
2130	Insulation	1	11/12/26	11/12/26
2135	Drywall	6	11/16/26	11/23/26
2140	Tub/Shower Pans	1	11/24/26	11/24/26
2145	Gypcrete	1	11/24/26	11/24/26
2150	Tape/Float/Sand Walls & Ceilings	8	11/25/26	12/07/26
2155	Spray Texture	3	12/07/26	12/09/26
2160	Doors & Trim	3	12/09/26	12/11/26
2165	Prime & 1st Coat Paint	2	12/11/26	12/14/26
2170	Tub/Shower Wall Tile	4	12/15/26	12/18/26
2175	Bathroom Floor Tile	4	12/24/26	12/30/26
2180	Shower Doors & Mirrors	2	12/31/26	01/04/27
2185	Toilet Accessories	1	01/05/27	01/05/27
2190	Cabinets	5	12/15/26	12/21/26
2195	Countertops	2	12/22/26	12/23/26
2200	Drywall Touch Up	1	12/24/26	12/24/26
2205	Tile Backsplash	4	12/31/26	01/06/27
2210	LVT	8	01/08/27	01/19/27
2215	Shoe/Scribe Molding	2	01/19/27	01/20/27
2220	Rough Clean	2	01/20/27	01/21/27
2225	Completion List	1	01/22/27	01/22/27
2230	Appliances	1	01/25/27	01/25/27
2235	Blinds	1	01/26/27	01/26/27
2240	Final Paint	1	01/27/27	01/27/27
Inspections				
2245	STRUCTURAL	1	11/09/26	11/09/26
2250	INSULATION	1	11/13/26	11/13/26
Interior Punch List				
2255	Arch-Con Punch List	3	01/27/27	01/29/27
2260	Arch-Con Punch List Corrections	2	01/29/27	02/01/27
2265	Final Clean	1	02/02/27	02/02/27
2270	Owner Punch List	3	02/04/27	02/08/27
2275	Punch List Corrections	3	02/09/27	02/11/27
2280	Powder Puff	2	02/11/27	02/12/27
2285	Owner Acceptance	3	02/12/27	02/16/27
Lvl. 4				
Wood Framing				
Area A				
2290	Layout	1	07/01/26	07/01/26
2295	Frame Walls	2	07/02/26	07/03/26
2300	Plumb Line Walls	1	07/06/26	07/06/26
2305	Wall Sheathing	2	07/07/26	07/08/26
2310	Floor Joists	2	07/09/26	07/10/26
2315	Floor Decking	2	07/13/26	07/14/26
Inspections				
2320	STRUCTURAL	1	07/15/26	07/15/26

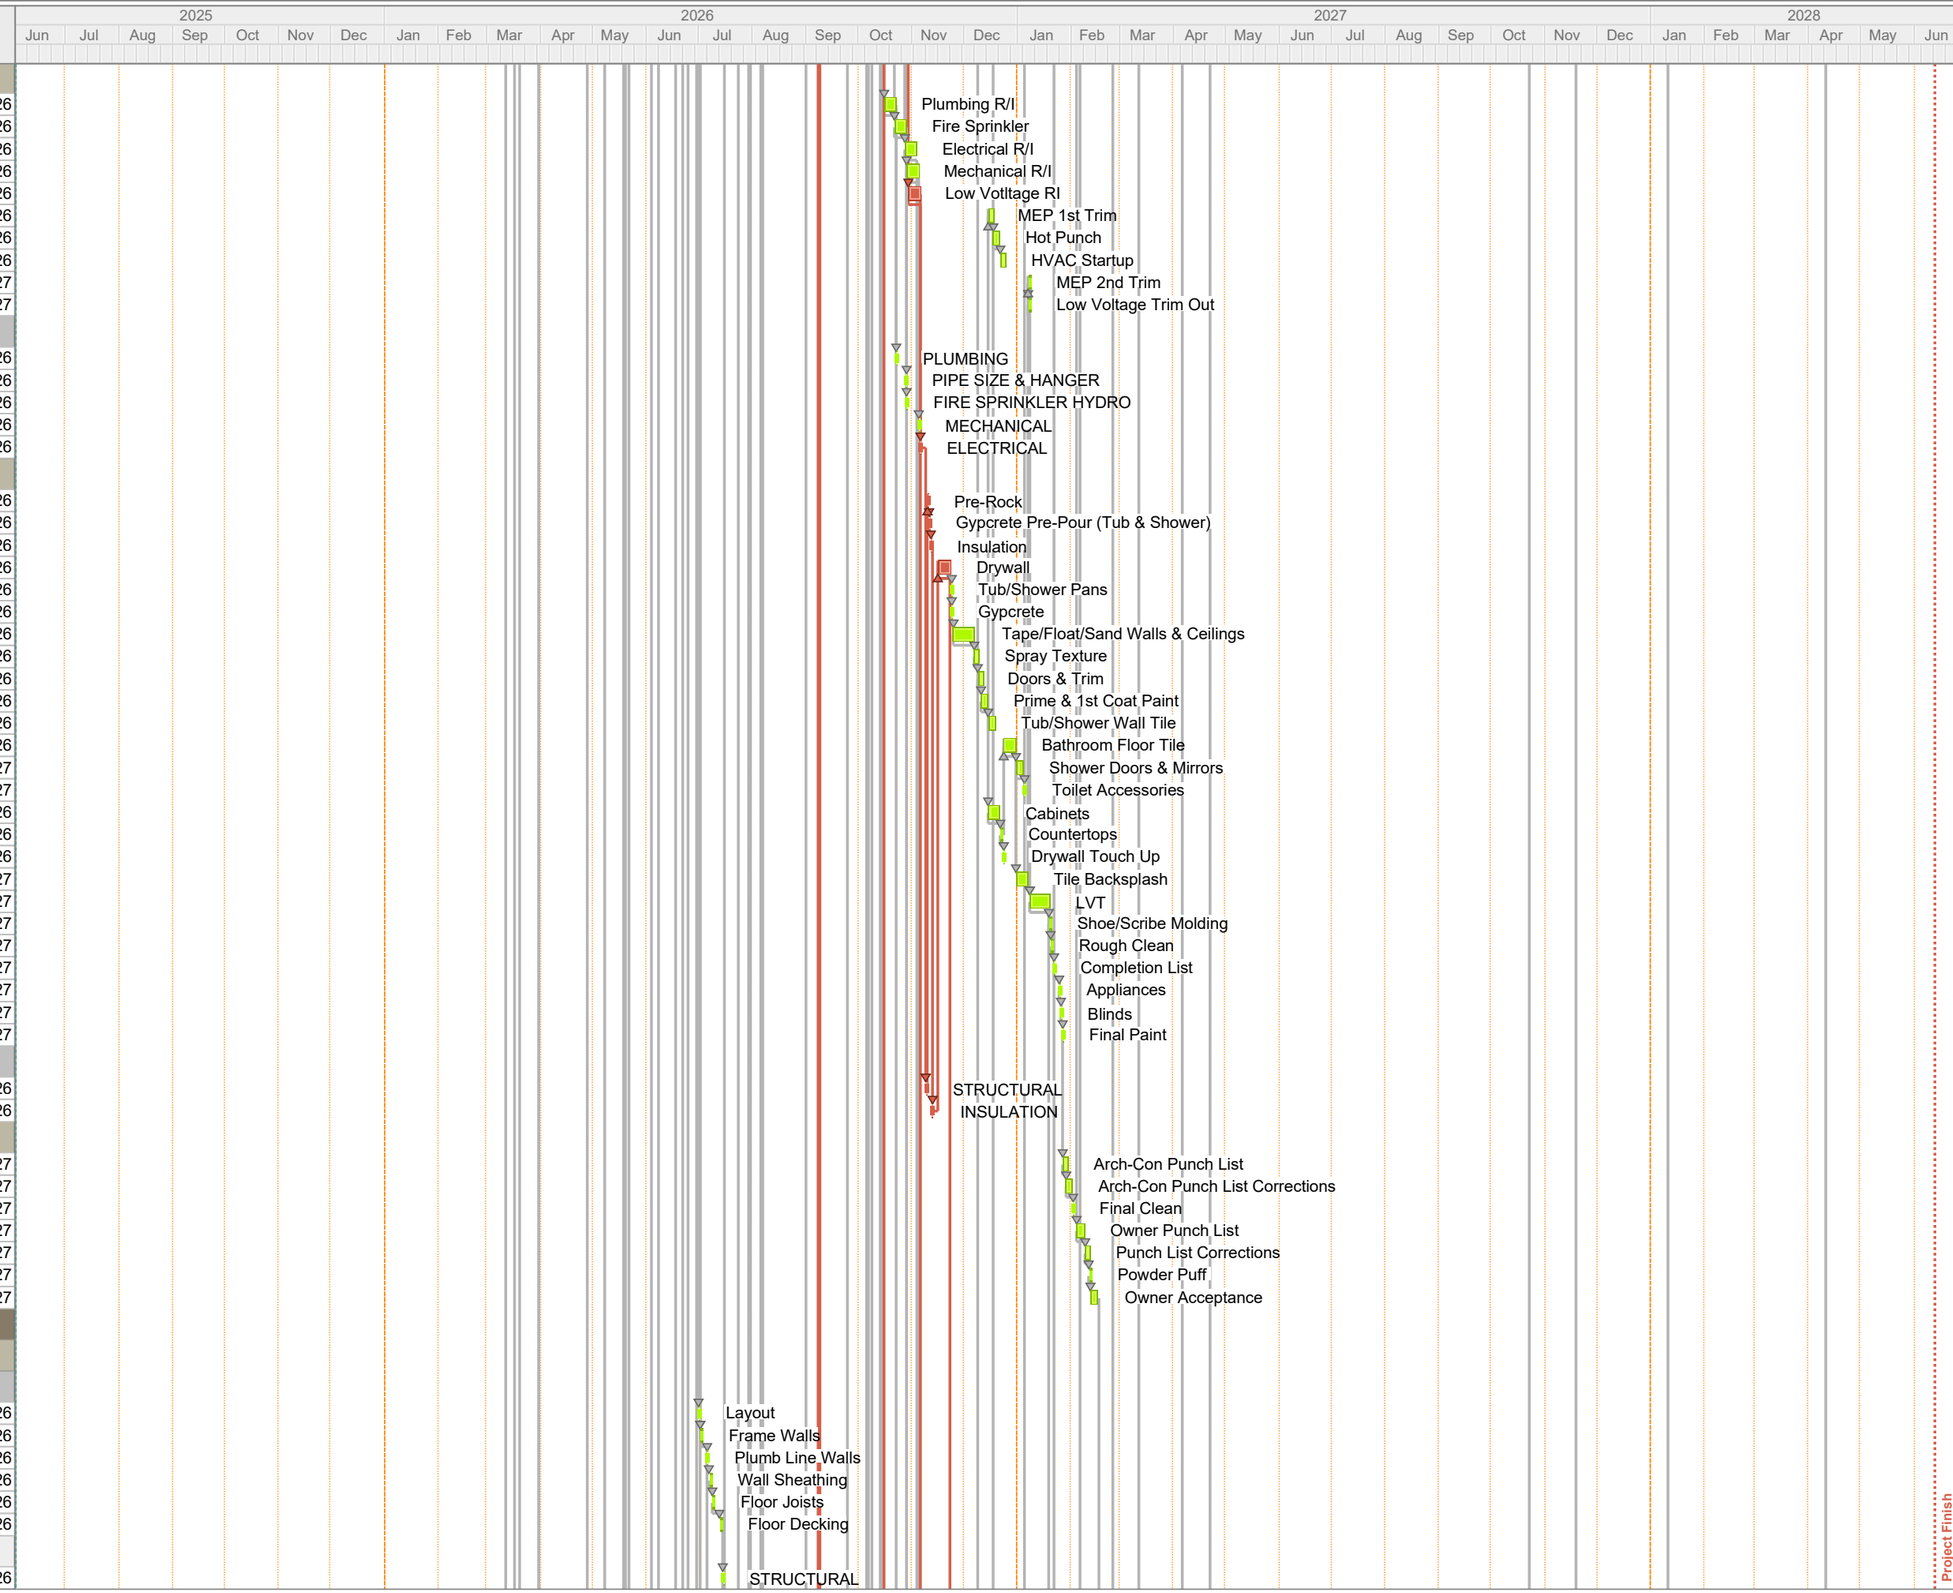

Initials: _____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

Area B				
2325	Layout	1	09/08/26	09/08/26
2330	Frame Walls	2	09/09/26	09/10/26
2335	Plumb Line Walls	1	09/11/26	09/11/26
2340	Wall Sheathing	2	09/14/26	09/15/26
2345	Floor Joists	2	09/16/26	09/17/26
2350	Floor Decking	2	09/18/26	09/21/26
Inspections				
2355	STRUCTURAL	1	09/22/26	09/22/26
MEPF				
2360	Plumbing R/I	5	10/23/26	10/29/26
2365	Fire Sprinkler	5	10/29/26	11/04/26
2370	Electrical R/I	5	11/04/26	11/10/26
2375	Mechanical R/I	5	11/05/26	11/11/26
2380	Low Votltage RI	5	11/06/26	11/12/26
2385	MEP 1st Trim	3	12/21/26	12/23/26
2390	Hot Punch	2	12/24/26	12/28/26
2395	HVAC Startup	3	12/29/26	12/31/26
2400	MEP 2nd Trim	2	01/13/27	01/14/27
2405	Low Voltage Trim Out	2	01/13/27	01/14/27
Inspections				
2410	PLUMBING	1	10/30/26	10/30/26
2415	PIPE SIZE & HANGER	1	11/04/26	11/04/26
2420	FIRE SPRINKLER HYDRO	1	11/05/26	11/05/26
2425	MECHANICAL	1	11/12/26	11/12/26
2430	ELECTRICAL	1	11/13/26	11/13/26
Buildout				
2435	Pre-Rock	1	11/17/26	11/17/26
2440	Gypcrete Pre-Pour (Tub & Shower)	1	11/18/26	11/18/26
2445	Insulation	1	11/19/26	11/19/26
2450	Drywall	6	11/23/26	12/01/26
2455	Tub/Shower Pans	1	12/02/26	12/02/26
2460	Gypcrete	1	12/02/26	12/02/26
2465	Tape/Float/Sand Walls & Ceilings	8	12/03/26	12/14/26
2470	Spray Texture	3	12/14/26	12/16/26
2475	Doors & Trim	3	12/15/26	12/17/26
2480	Prime & 1st Coat Paint	2	12/17/26	12/18/26
2485	Tub/Shower Wall Tile	4	12/21/26	12/24/26
2490	Bathroom Floor Tile	4	12/31/26	01/06/27
2495	Shower Doors & Mirrors	2	01/07/27	01/08/27
2500	Toilet Accessories	1	01/11/27	01/11/27
2505	Cabinets	5	12/21/26	12/28/26
2510	Countertops	2	12/29/26	12/30/26
2515	Drywall Touch Up	1	12/31/26	12/31/26
2520	Tile Backsplash	4	01/07/27	01/12/27
2525	LVT	8	01/19/27	01/28/27
2530	Shoe/Scribe Molding	2	01/28/27	01/29/27
2535	Rough Clean	1	02/01/27	02/01/27
2540	Completion List	1	02/02/27	02/02/27
2545	Appliances	1	02/03/27	02/03/27
2550	Blinds	1	02/04/27	02/04/27
2555	Final Paint	1	02/05/27	02/05/27
Inspections				
2560	STRUCTURAL	1	11/16/26	11/16/26
2565	INSULATION	1	11/20/26	11/20/26
Interior Punch List				
2570	Arch-Con Punch List	3	02/08/27	02/10/27
2575	Arch-Con Punch List Corrections	2	02/10/27	02/11/27
2580	Final Clean	1	02/12/27	02/12/27
2585	Owner Punch List	3	02/17/27	02/19/27
2590	Punch List Corrections	3	02/19/27	02/23/27
2595	Powder Puff	2	02/24/27	02/25/27
2600	Owner Acceptance	3	02/25/27	03/01/27

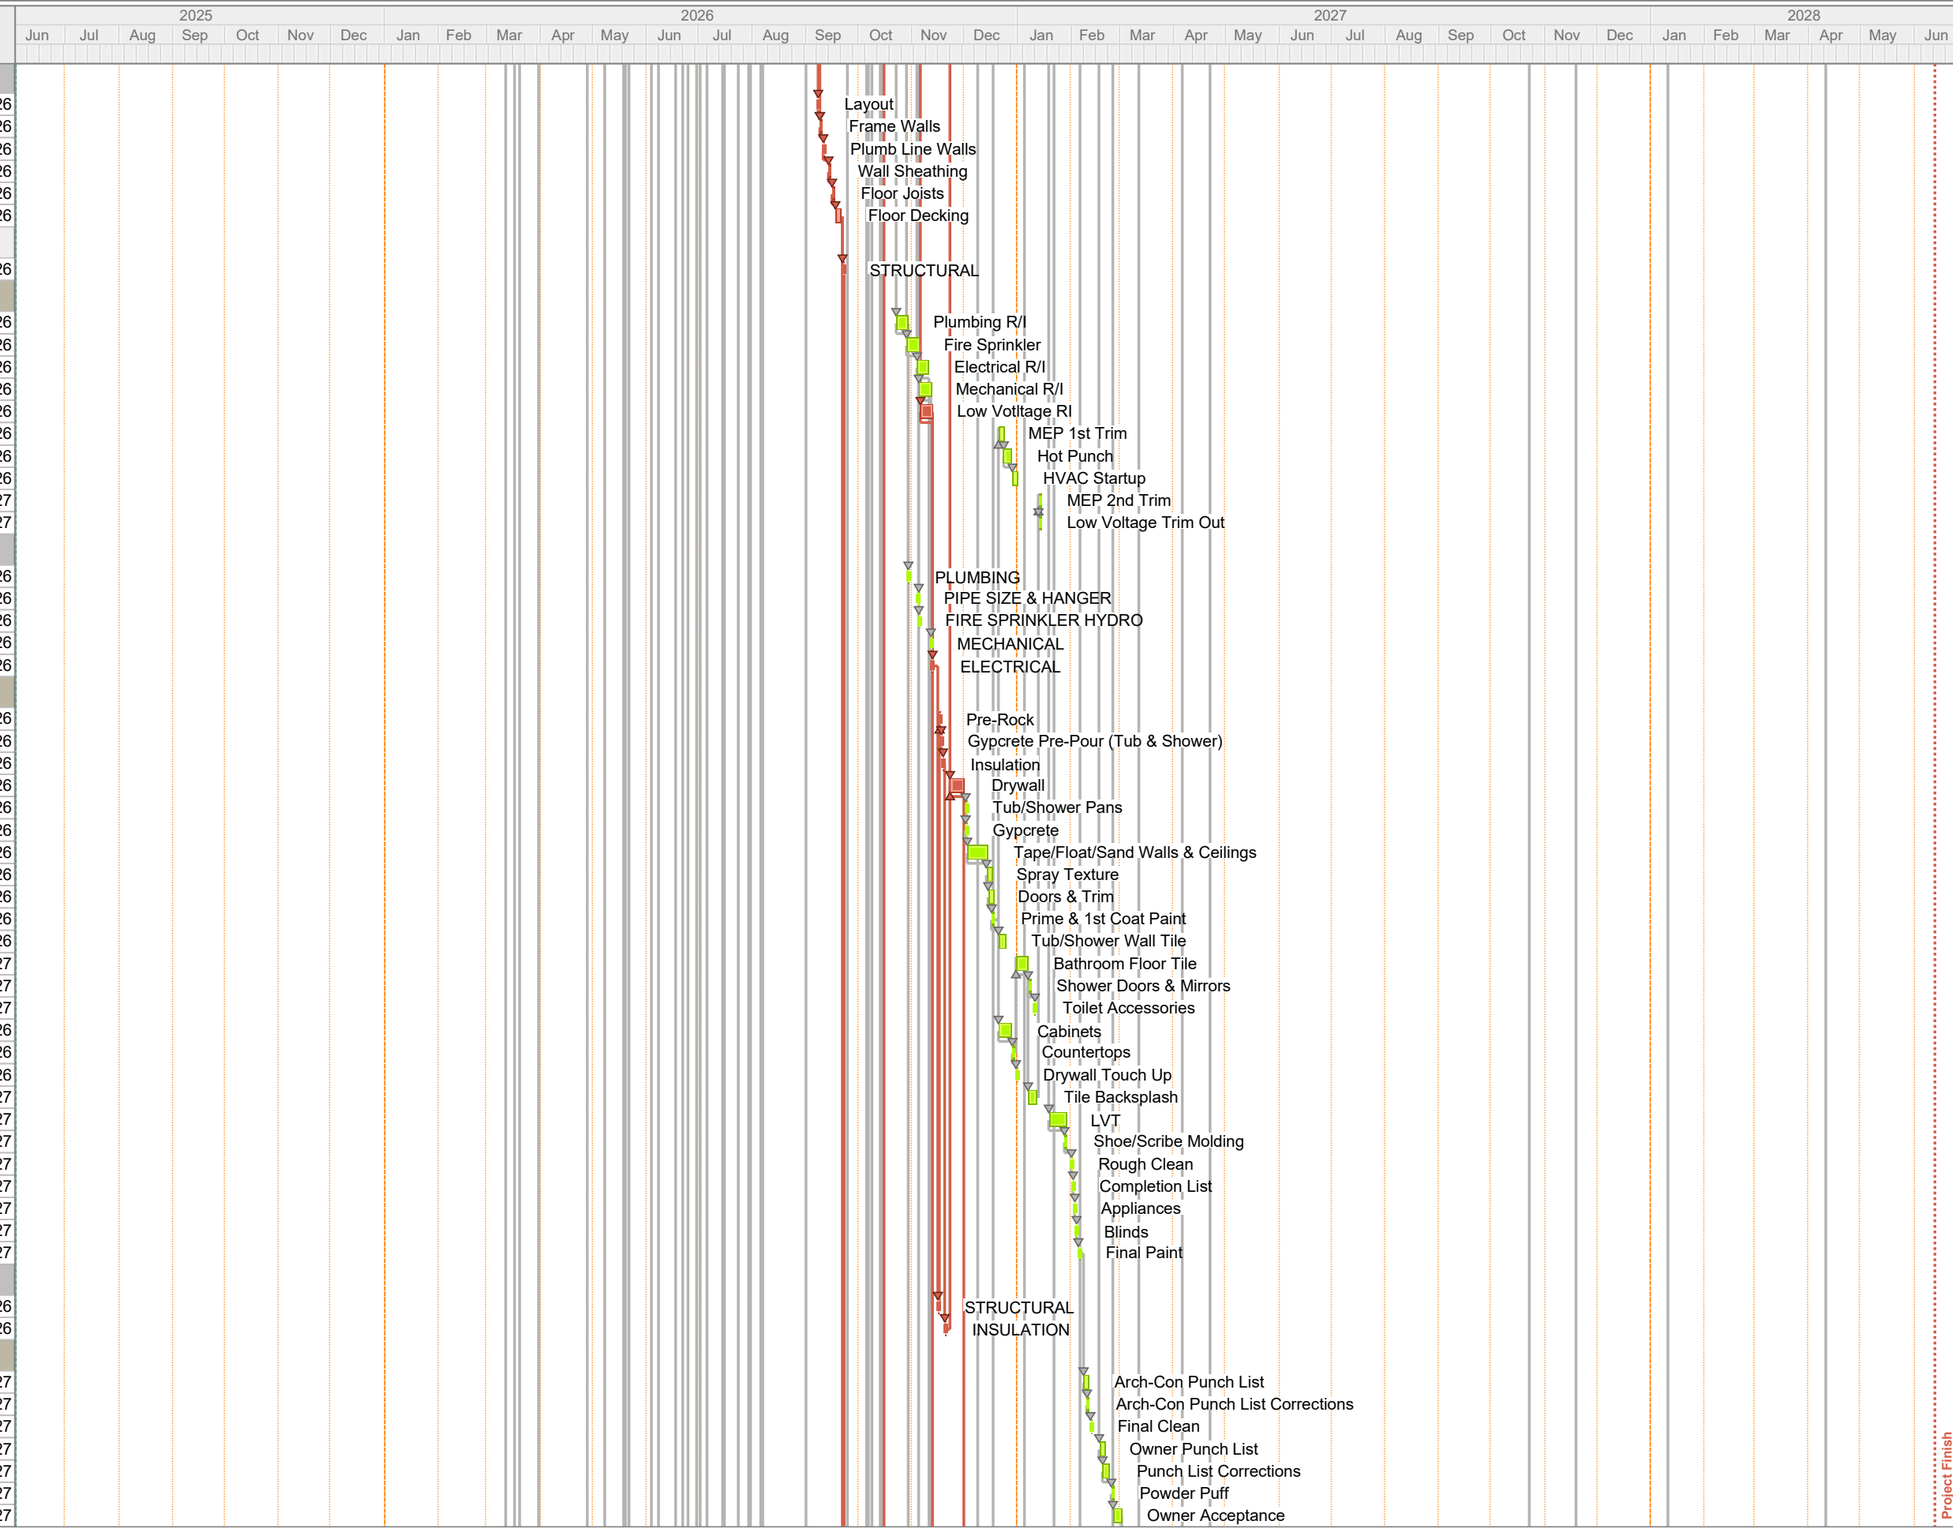

Initials: _____

Lvl. 5

Wood Framing				
Area A				
2605	Layout	1	07/15/26	07/15/26
2610	Frame Walls	2	07/17/26	07/20/26
2615	Plumb Line Walls	1	07/21/26	07/21/26
2620	Wall Sheathing	2	07/22/26	07/23/26
2625	Roof Joists	2	07/24/26	07/27/26
2630	Roof Decking	2	07/28/26	07/29/26
Inspections				
2635	STRUCTURAL	1	07/30/26	07/30/26
Area B				
2640	Layout	1	09/22/26	09/22/26
2645	Frame Walls	2	09/23/26	09/24/26
2650	Plumb Line Walls	1	09/25/26	09/25/26
2655	Wall Sheathing	2	09/28/26	09/29/26
2660	Roof Joists	2	09/30/26	10/01/26
2665	Roof Decking	2	10/02/26	10/05/26
Inspections				
2670	STRUCTURAL	1	10/06/26	10/06/26
MEPF				
2675	Plumbing R/I	5	10/30/26	11/05/26
2680	Fire Sprinkler	5	11/05/26	11/11/26
2685	Electrical R/I	5	11/11/26	11/17/26
2690	Mechanical R/I	5	11/12/26	11/18/26
2695	Low Votltage RI	5	11/13/26	11/19/26
2700	MEP 1st Trim	3	12/31/26	01/05/27
2705	Hot Punch	2	01/06/27	01/07/27
2710	HVAC Startup	3	01/08/27	01/12/27
2715	MEP 2nd Trim	3	01/25/27	01/27/27
2720	Low Voltage Trim Out	3	01/28/27	02/01/27
Inspections				
2725	PLUMBING	1	11/06/26	11/06/26
2730	PIPE SIZE & HANGER	1	11/11/26	11/11/26
2735	FIRE SPRINKLER HYDRO	1	11/12/26	11/12/26
2740	MECHANICAL	1	11/19/26	11/19/26
2745	ELECTRICAL	1	11/20/26	11/20/26
Buildout				
2750	Pre-Rock	1	11/24/26	11/24/26
2755	Gypcrete Pre-Pour (Tub & Shower)	1	11/25/26	11/25/26
2760	Insulation	1	11/27/26	11/27/26
2765	Drywall	6	12/01/26	12/08/26
2770	Tub/Shower Pans	1	12/09/26	12/09/26
2775	Gypcrete	1	12/09/26	12/09/26
2780	Tape/Float/Sand Walls & Ceilings	8	12/10/26	12/21/26
2785	Spray Texture	3	12/21/26	12/23/26
2790	Doors & Trim	3	12/23/26	12/28/26
2795	Prime & 1st Coat Paint	2	12/29/26	12/30/26
2800	Tub/Shower Wall Tile	4	12/31/26	01/06/27
2805	Bathroom Floor Tile	4	01/13/27	01/18/27
2810	Shower Doors & Mirrors	2	01/19/27	01/20/27
2815	Toilet Accessories	1	01/21/27	01/21/27
2820	Cabinets	5	12/31/26	01/07/27
2825	Countertops	2	01/08/27	01/11/27
2830	Drywall Touch Up	1	01/12/27	01/12/27
2835	Tile Backsplash	4	01/19/27	01/22/27
2840	LVT	8	02/02/27	02/11/27
2845	Shoe/Scribe Molding	2	02/11/27	02/12/27
2850	Rough Clean	1	02/15/27	02/15/27
2855	Completion List	1	02/16/27	02/16/27
2860	Appliances	1	02/17/27	02/17/27
2865	Blinds	1	02/18/27	02/18/27
2870	Final Paint	1	02/19/27	02/19/27
Inspections				
2875	STRUCTURAL	1	11/23/26	11/23/26
2880	INSULATION	1	11/30/26	11/30/26

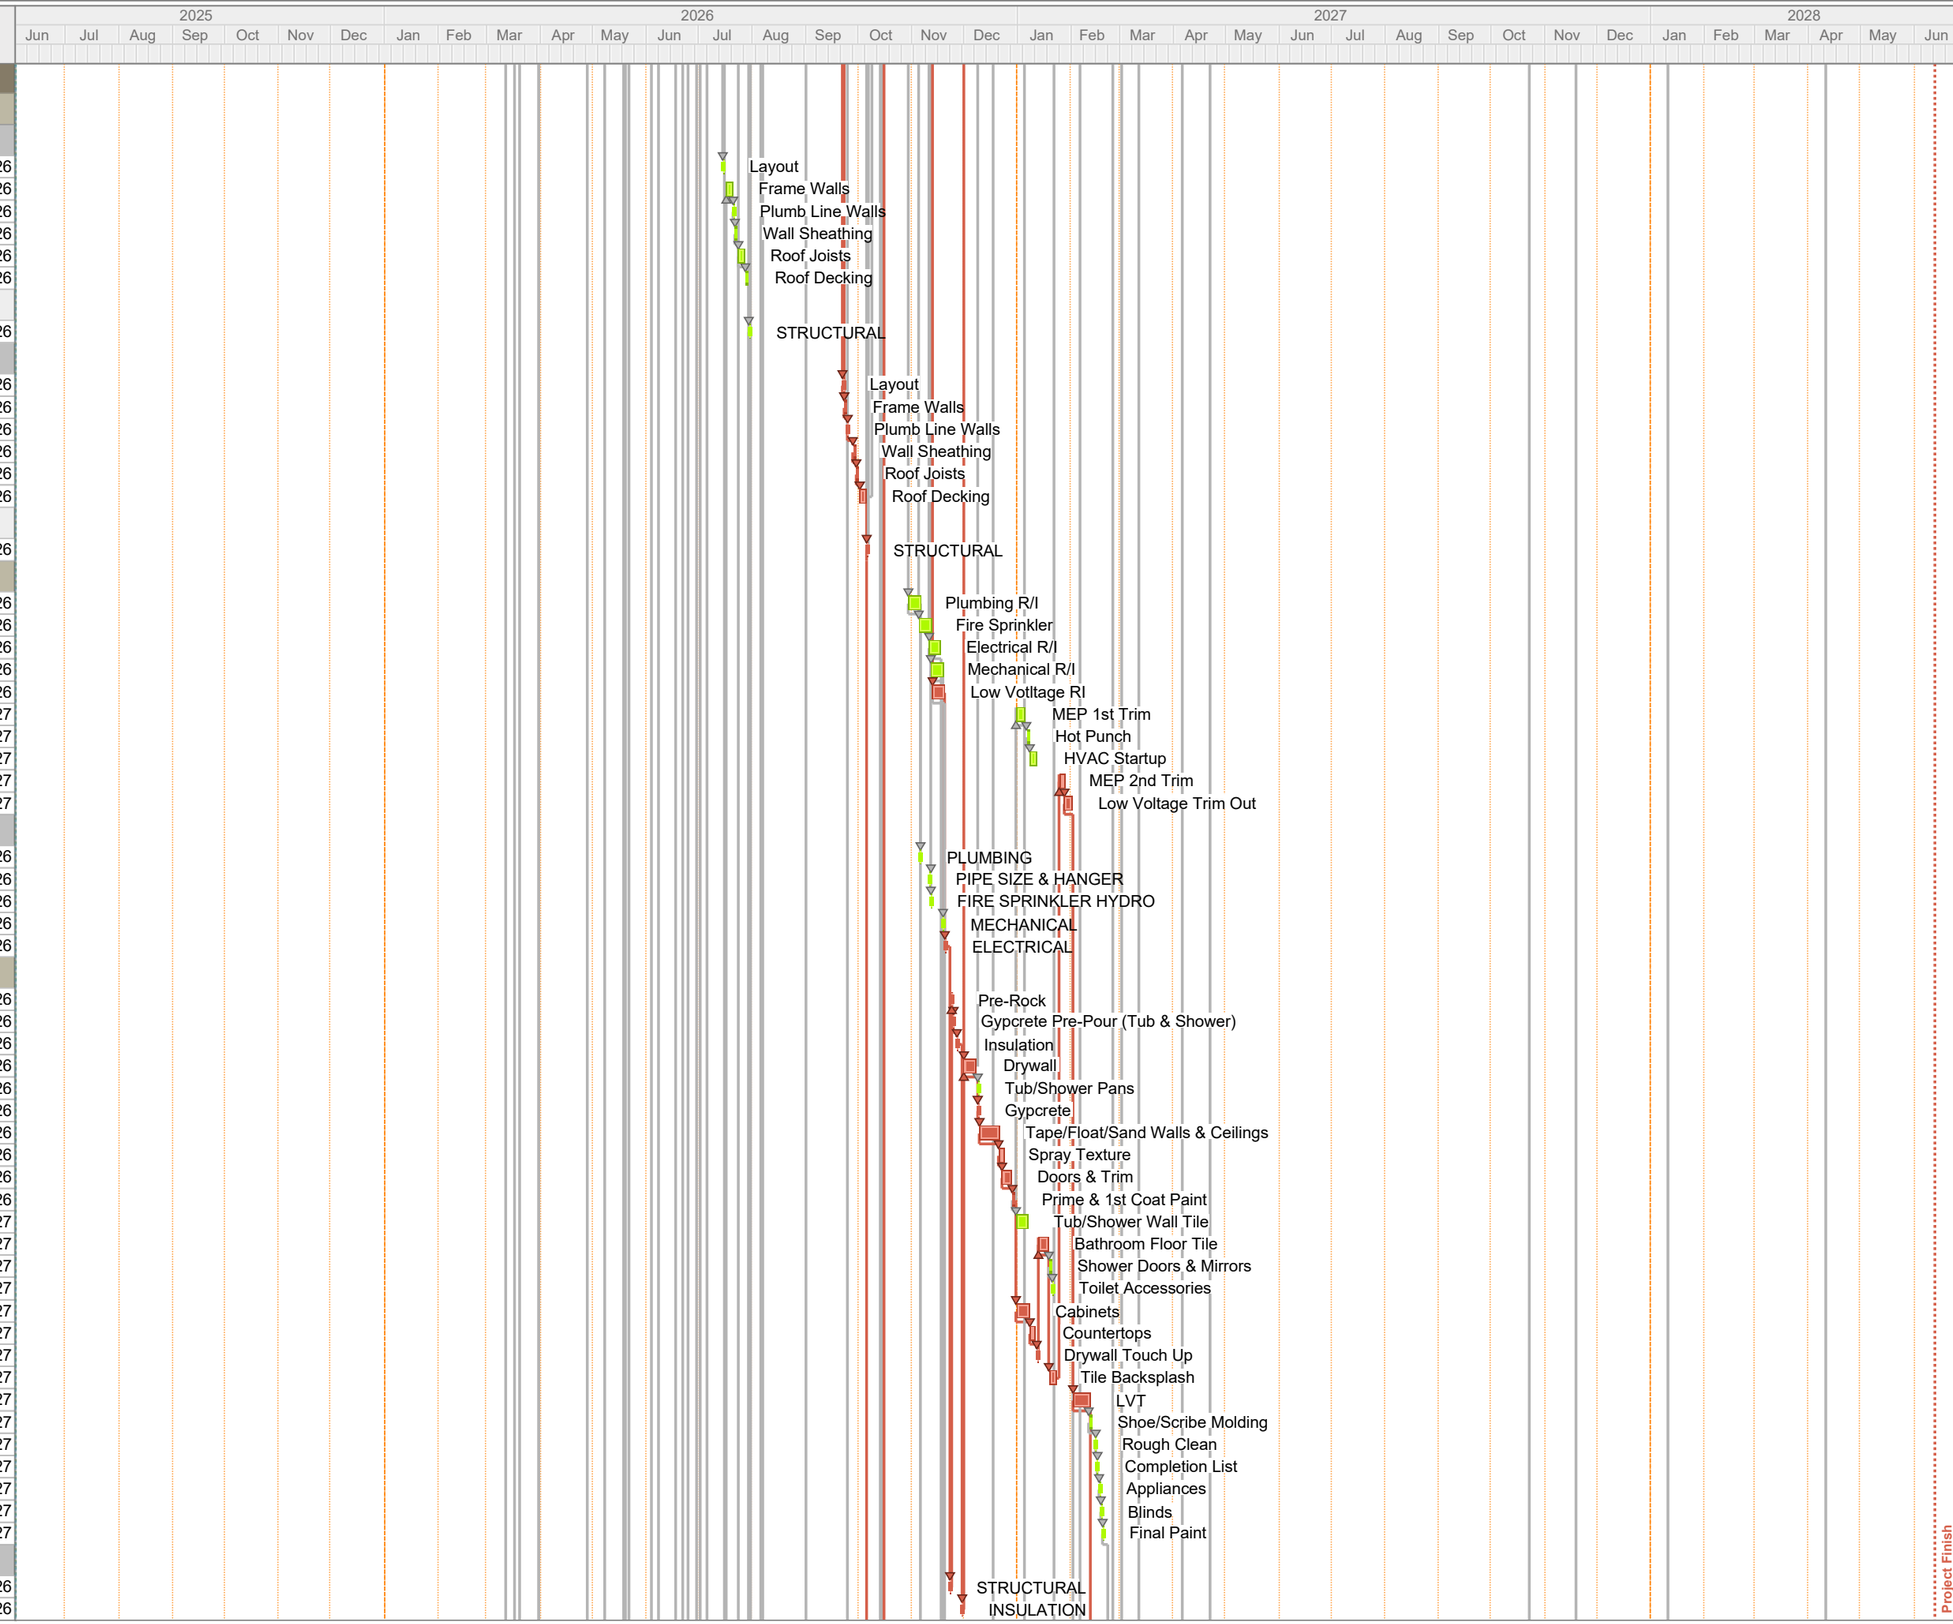

Initials: _____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

Interior Punch List				
2885	Arch-Con Punch List	3	02/22/27	02/24/27
2890	Arch-Con Punch List Corrections	2	02/24/27	02/25/27
2895	Final Clean	1	02/26/27	02/26/27
2900	Owner Punch List	3	03/02/27	03/04/27
2905	Punch List Corrections	3	03/04/27	03/08/27
2910	Powder Puff	2	03/09/27	03/10/27
2915	Owner Acceptance	3	03/10/27	03/12/27
Building Exterior				
Roof				
Area A				
2920	TPO Roofing	6	07/30/26	08/06/26
Area B				
2925	TPO Roofing	6	10/06/26	10/13/26
North Elevation				
2930	Windows	10	06/25/26	07/08/26
2935	Waterproofing	10	06/30/26	07/13/26
2940	Exterior Storefront	10	07/07/26	07/20/26
2945	Storefront Glass	10	07/07/26	07/20/26
2950	Masonry/Brick	10	07/17/26	07/30/26
2955	Hardi & Trim	10	07/29/26	08/11/26
2960	Paint Prep (Caulk, Prime, 1st Coat)	10	08/10/26	08/21/26
2965	Final Paint	10	08/20/26	09/02/26
East Elevation (Left)				
2970	Windows	10	07/03/26	07/16/26
2975	Waterproofing	10	07/08/26	07/21/26
2980	Exterior Storefront	10	07/15/26	07/28/26
2985	Storefront Glass	10	07/15/26	07/28/26
2990	Masonry/Brick	10	07/27/26	08/07/26
2995	Hardi & Trim	10	08/06/26	08/19/26
3000	Paint Prep (Caulk, Prime, 1st Coat)	10	08/18/26	08/31/26
3005	Final Paint	10	08/28/26	09/11/26
West Elevation				
3010	Windows	10	09/01/26	09/15/26
3015	Waterproofing	10	09/04/26	09/18/26
3020	Exterior Storefront	10	09/14/26	09/25/26
3025	Storefront Glass	10	09/14/26	09/25/26
3030	Masonry/Brick	10	09/24/26	10/07/26
3035	Hardi & Trim	10	10/06/26	10/19/26
3040	Paint Prep (Caulk, Prime, 1st Coat)	10	10/16/26	10/29/26
3045	Final Paint	10	10/28/26	11/10/26
Entry Courtyard North Elevation				
3050	Windows	10	09/10/26	09/23/26
3055	Waterproofing	10	09/15/26	09/28/26
3060	Exterior Storefront	10	09/22/26	10/05/26
3065	Storefront Glass	10	09/22/26	10/05/26
3070	Masonry/Brick	10	10/02/26	10/15/26
3075	Hardi & Trim	10	10/14/26	10/27/26
3080	Paint Prep (Caulk, Prime, 1st Coat)	10	10/26/26	11/06/26
3085	Final Paint	10	11/05/26	11/18/26
Entry Courtyard South Elevation				
3090	Windows	10	09/18/26	10/01/26
3095	Waterproofing	10	09/23/26	10/06/26
3100	Exterior Storefront	10	09/30/26	10/13/26
3105	Storefront Glass	10	09/30/26	10/13/26
3110	Masonry/Brick	10	10/12/26	10/23/26
3115	Hardi & Trim	10	10/22/26	11/04/26
3120	Paint Prep (Caulk, Prime, 1st Coat)	10	11/03/26	11/16/26
3125	Final Paint	10	11/13/26	11/27/26
Entry Courtyard West Elevation				
3130	Windows	10	09/28/26	10/09/26
3135	Waterproofing	10	10/01/26	10/14/26
3140	Exterior Storefront	10	10/08/26	10/21/26
3145	Storefront Glass	10	10/08/26	10/21/26
3150	Masonry/Brick	10	10/20/26	11/02/26
3155	Hardi & Trim	10	10/30/26	11/12/26

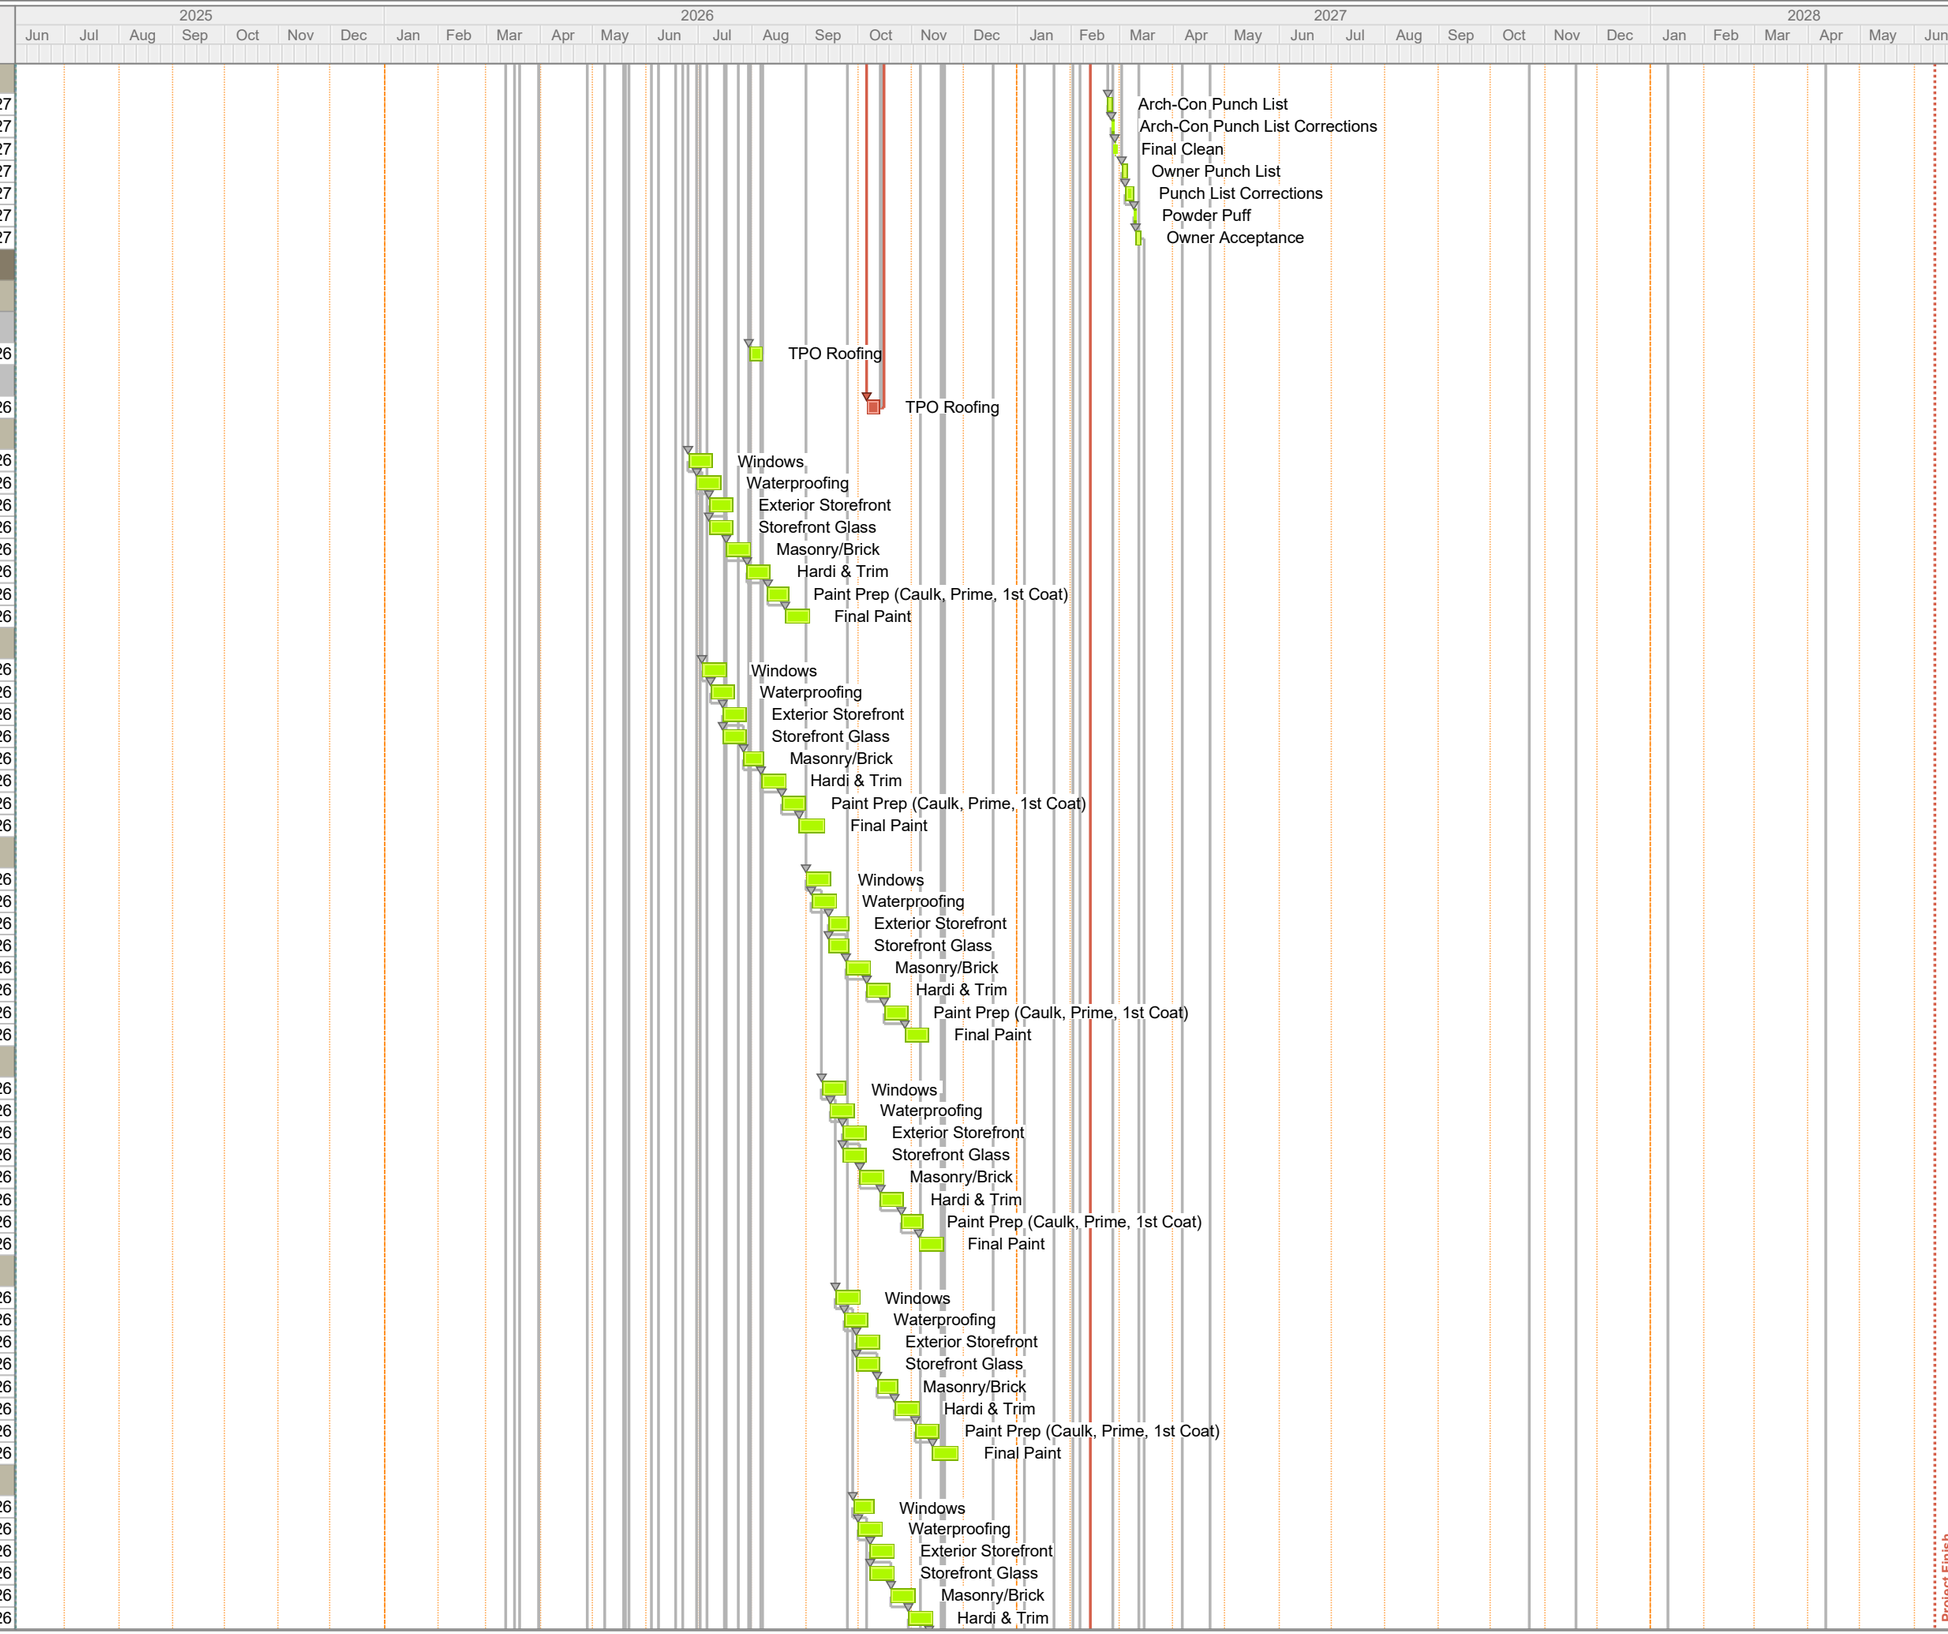

Initials: _____

3160	Paint Prep (Caulk, Prime, 1st Coat)	10	11/11/26	11/24/26
3165	Final Paint	10	11/23/26	12/07/26
Courtyard #1 North Elevation				
3170	Windows	10	10/06/26	10/19/26
3175	Waterproofing	10	10/09/26	10/22/26
3180	Exterior Storefront	10	10/16/26	10/29/26
3185	Storefront Glass	10	10/16/26	10/29/26
3190	Masonry/Brick	10	10/28/26	11/10/26
3195	Hardi & Trim	10	11/09/26	11/20/26
3200	Paint Prep (Caulk, Prime, 1st Coat)	10	11/19/26	12/03/26
3205	Final Paint	10	12/02/26	12/15/26
Pool Courtyard North Elevation				
3210	Windows	10	10/14/26	10/27/26
3215	Waterproofing	10	10/19/26	10/30/26
3220	Exterior Storefront	10	10/26/26	11/06/26
3225	Storefront Glass	10	10/26/26	11/06/26
3230	Masonry/Brick	10	11/05/26	11/18/26
3235	Hardi & Trim	10	11/17/26	12/01/26
3240	Paint Prep (Caulk, Prime, 1st Coat)	10	11/30/26	12/11/26
3245	Final Paint	10	12/10/26	12/23/26
Pool Courtyard East Elevation				
3250	Windows	10	10/22/26	11/04/26
3255	Waterproofing	10	10/27/26	11/09/26
3260	Exterior Storefront	10	11/03/26	11/16/26
3265	Storefront Glass	10	11/03/26	11/16/26
3270	Masonry/Brick	10	11/13/26	11/27/26
3275	Hardi & Trim	10	11/25/26	12/09/26
3280	Paint Prep (Caulk, Prime, 1st Coat)	10	12/08/26	12/21/26
3285	Final Paint	10	12/18/26	01/04/27
Exterior Punch List				
3290	Arch-Con Punch List	1	01/05/27	01/05/27
3295	Arch-Con Punch List Corrections	2	01/06/27	01/07/27
3300	Final Clean	1	01/08/27	01/08/27
3305	Owner Punch List	1	01/11/27	01/11/27
3310	Punch List Corrections	1	01/12/27	01/12/27
3315	Owner Acceptance	1	01/13/27	01/13/27
Stair				
C				
3450	Stair C	30	07/31/26	09/11/26
3455	Fire Sprinkler Standpipe	5	07/31/26	08/06/26
F				
3460	Stair F	30	07/31/26	09/11/26
3465	Fire Sprinkler Standpipe	5	07/31/26	08/06/26
Elevator				
C				
Pit				
3320	Excavate	1	03/31/26	03/31/26
3325	Waterproof Pit Floor	1	04/01/26	04/01/26
3330	Pour Pit Floor	1	04/02/26	04/02/26
3335	F/R/P Pit Walls	1	04/03/26	04/03/26
3340	Waterproof Pit Walls	1	04/06/26	04/06/26
3345	Backfill	1	04/07/26	04/07/26
Buildout				
3350	CMU	15	04/28/26	05/18/26
3355	Hang	1	08/07/26	08/07/26
3360	Site Readiness Elevator Checklist	1	08/10/26	08/10/26
3365	Rail Stack	1	08/11/26	08/11/26
3370	Entrance	1	08/12/26	08/12/26
3375	Wire Entrance	1	08/13/26	08/13/26
3380	Fascia	1	08/14/26	08/14/26
3385	Cab Shell	1	08/17/26	08/17/26
3390	Wire Cab	1	08/18/26	08/18/26
3395	Cab Interior	1	08/19/26	08/19/26
3400	Install Complete/Work by Others	1	08/20/26	08/20/26
3405	Hoistway Vent Louver & Wire	1	08/21/26	08/21/26
3410	Hoistway Electrical R/I	1	08/24/26	08/24/26

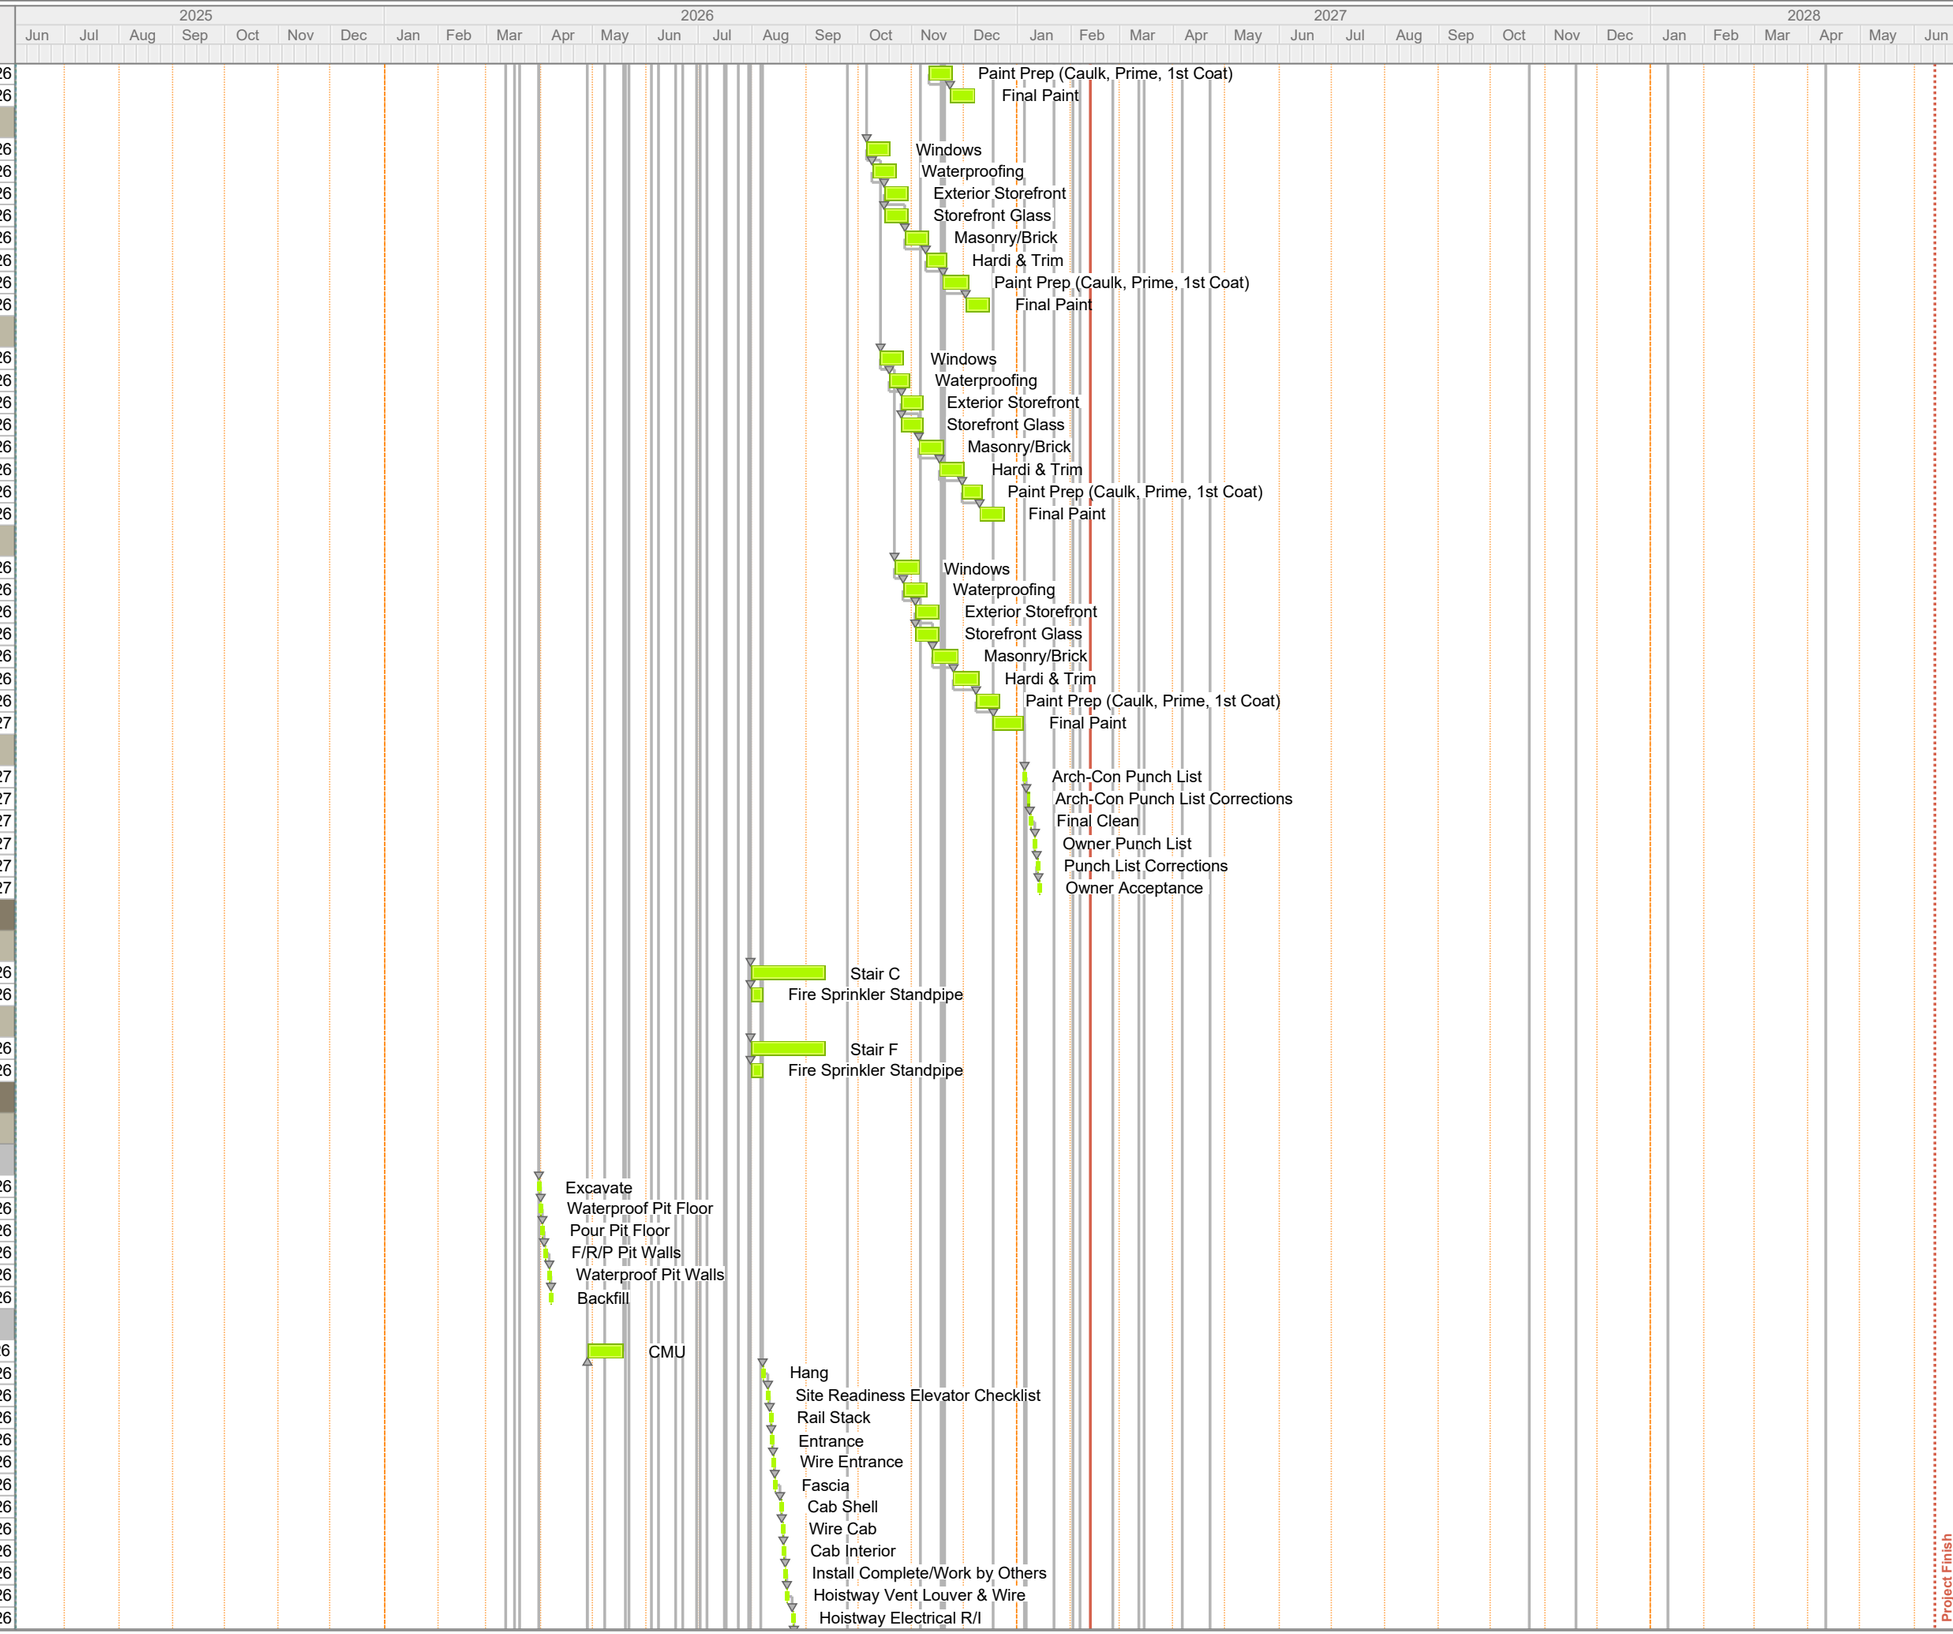

Initials: _____

3415	Sump Pump / Grate & Test	1	08/25/26	08/25/26
3420	Elevator Shaft Pre-Inspection	1	08/26/26	08/26/26
3425	Adjusting/AHJ Testing	1	08/27/26	08/27/26
3430	Turnover	1	09/03/26	09/03/26
Inspections				
3435	STATE	1	08/28/26	08/28/26
3440	COH ELEVATOR SHAFT & RECALL	2	08/31/26	09/01/26
3445	TEMPORARY USE PERMIT	1	09/02/26	09/02/26
Interior Amenities				
Leasing				
3470	Leasing	30	07/02/26	08/12/26
Clubhouse				
3475	Clubhouse	30	07/23/26	09/02/26
Fitness				
3480	Fitness	30	08/13/26	09/24/26
Business Lounge				
3485	Business Lounge	30	09/03/26	10/15/26
Cafe				
3490	Cafe	30	09/25/26	11/05/26
Mail/Package Room				
3495	Mail & Package Room	30	10/16/26	11/27/26
Lounge				
3500	Lounge	30	11/06/26	12/18/26
Final Inspections				
3505	Knox Boxes	10	01/06/27	01/19/27
3510	MECHANICAL	15	02/02/27	02/22/27
3515	ELECTRICAL	15	02/23/27	03/15/27
3520	PLUMBING	15	03/16/27	04/05/27
3525	STRUCTURAL	15	04/06/27	04/26/27
3530	FIRE SPRINKLER & FIRE ALARM	15	04/27/27	05/17/27
3535	EGRESS	15	05/18/27	06/07/27
Systems Verification				
3540	Systems Verification	65	06/08/27	09/07/27
Weather				
3545	Weather Impacts Days	33	09/08/27	10/22/27
Substatial Completion				
3550	Substantial Completion	0		10/22/27
Phase 2 (52 Units)				
Slab on Grade				
Pour #03				
Earthwork				
3555	Building Pad (Pour #03)	3	03/20/26	03/24/26
Concrete				
3560	Batter Boards	1	03/25/26	03/25/26
3565	Plumbing Underground	1	03/26/26	03/26/26
3570	Backfill Plumbing	1	03/30/26	03/30/26
3575	Grade Pad	1	03/31/26	03/31/26
3580	Form SOG	1	04/01/26	04/01/26
3585	Termite Treatment	1	04/02/26	04/02/26
3590	Vapor Barrier	1	04/02/26	04/02/26
3595	Under Slab Electrical	1	04/03/26	04/03/26
3600	Rebar/PT Cables	1	04/06/26	04/06/26
3605	Hardware/Anchor Bolts	1	04/07/26	04/07/26
3610	Prep For Inspection	1	04/08/26	04/08/26
3615	Pour SOG	1	04/13/26	04/13/26
3620	Remove Forms	1	04/14/26	04/14/26
3625	Breaks, Stress, EOR Approval, Cut & (	5	04/15/26	04/21/26
Inspections				
3630	PLUMBING	1	03/27/26	03/27/26
3635	ELECTRICAL	1	04/03/26	04/03/26
3640	SOG	1	04/09/26	04/09/26
3645	3RD PARTY - STRUCTURAL	1	04/10/26	04/10/26

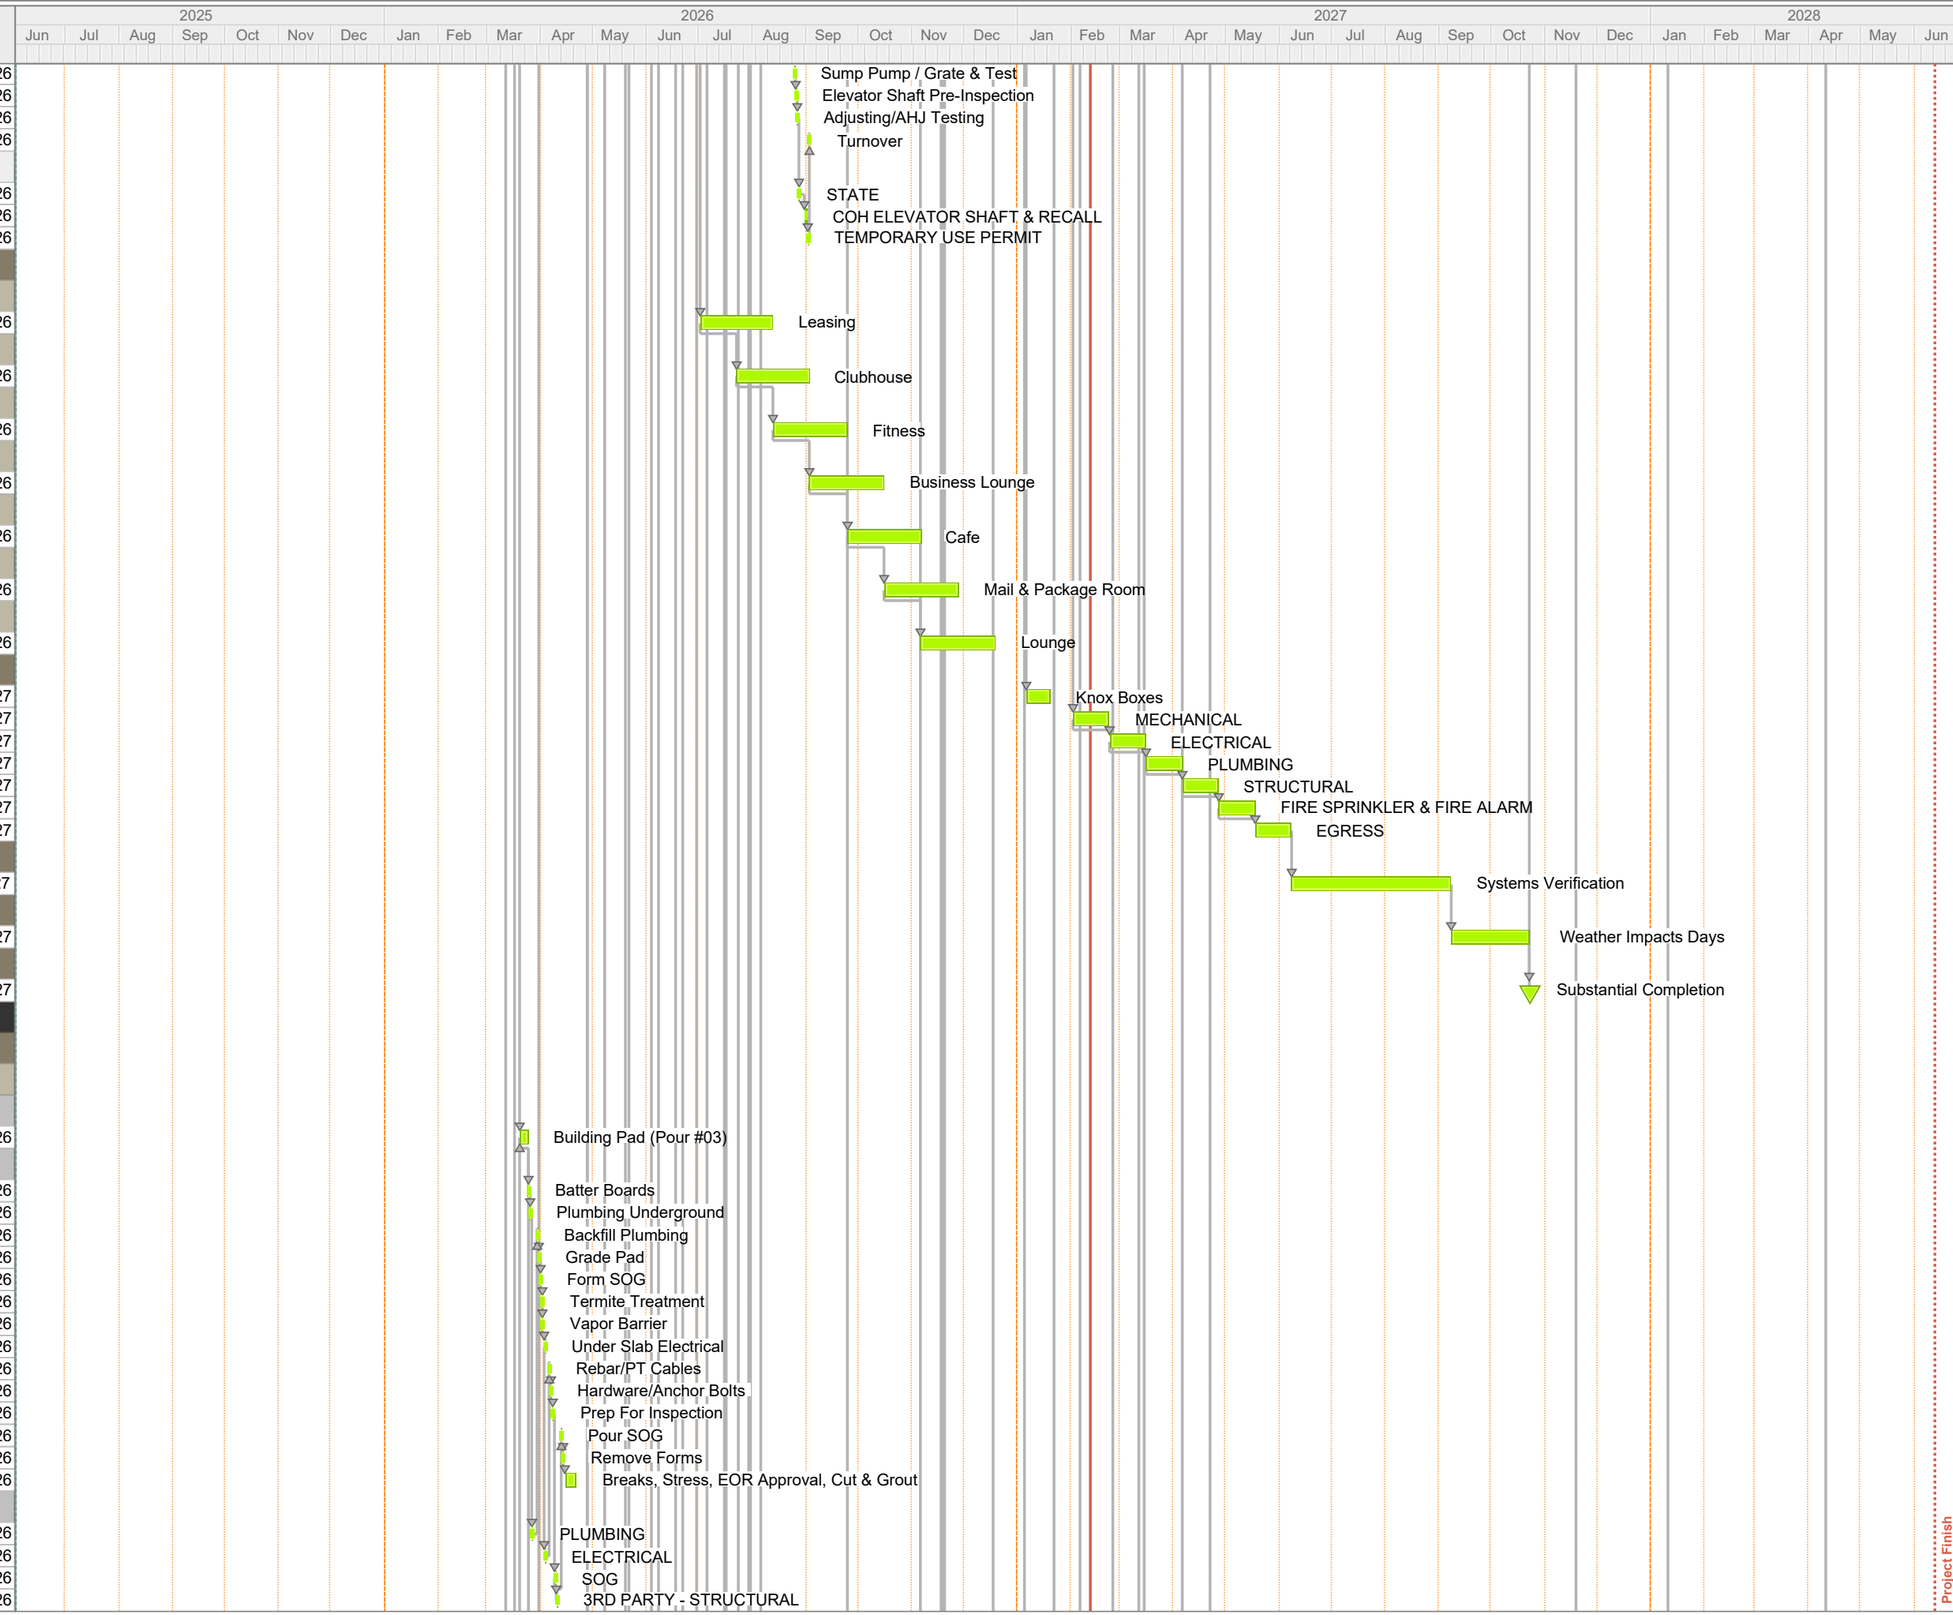

Initials: _____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

Pour #04				
Earthwork				
3650	Building Pad (Pour #04)	4	03/25/26	03/30/26
Concrete				
3655	Batter Boards	1	03/31/26	03/31/26
3660	Plumbing Underground	1	04/01/26	04/01/26
3665	Backfill Plumbing	1	04/03/26	04/03/26
3670	Grade Pad	1	04/06/26	04/06/26
3675	Form SOG	1	04/07/26	04/07/26
3680	Termite Treatment	1	04/08/26	04/08/26
3685	Vapor Barrier	1	04/08/26	04/08/26
3690	Under Slab Electrical	1	04/09/26	04/09/26
3695	Rebar/PT Cables	1	04/10/26	04/10/26
3700	Hardware/Anchor Bolts	1	04/13/26	04/13/26
3705	Prep For Inspection	1	04/14/26	04/14/26
3710	Pour SOG	1	04/17/26	04/17/26
3715	Remove Forms	1	04/20/26	04/20/26
3720	Breaks, Stress, EOR Approval, Cut & (	5	04/21/26	04/27/26
Inspections				
3725	PLUMBING	1	04/02/26	04/02/26
3730	ELECTRICAL	1	04/09/26	04/09/26
3735	STRUCTURAL	1	04/15/26	04/15/26
3740	3RD PARTY - STRUCTURAL	1	04/16/26	04/16/26
Lvl. 1				
Wood Framing				
3745	Layout	1	05/08/26	05/08/26
3750	Frame Walls	2	05/12/26	05/13/26
3755	Plumb Line Walls	1	05/14/26	05/14/26
3760	Wall Sheathing	1	05/15/26	05/15/26
3765	Floor Joists	2	05/18/26	05/19/26
3770	Floor Decking	1	05/20/26	05/20/26
Inspections				
3775	STRUCTURAL	1	05/21/26	05/21/26
MEPF				
3780	Plumbing R/I	3	11/06/26	11/10/26
3785	Fire Sprinkler	3	11/11/26	11/13/26
3790	Electrical R/I	3	11/18/26	11/20/26
3795	Mechanical R/I	3	11/19/26	11/23/26
3800	Low Votltage RI	3	11/20/26	11/24/26
3805	MEP 1st Trim	3	01/05/27	01/07/27
3810	Hot Punch	2	01/08/27	01/11/27
3815	HVAC Startup	3	01/11/27	01/13/27
3820	MEP 2nd Trim	2	01/19/27	01/20/27
3825	Low Voltage Trim Out	2	01/19/27	01/20/27
Inspections				
3830	PLUMBING	1	11/11/26	11/11/26
3835	PIPE SIZE & HANGER	1	11/16/26	11/16/26
3840	FIRE SPRINKLER HYDRO	1	11/17/26	11/17/26
3845	MECHANICAL	1	11/24/26	11/24/26
3850	ELECTRICAL	1	11/25/26	11/25/26
Buildout				
3855	Pre-Rock	1	11/30/26	11/30/26
3860	Gypcrete Pre-Pour (Tub & Shower)	1	12/01/26	12/01/26
3865	Insulation	1	12/02/26	12/02/26
3870	Drywall	4	12/14/26	12/17/26
3875	Tub/Shower Pans	1	12/18/26	12/18/26
3880	Gypcrete	1	12/18/26	12/18/26
3885	Tape/Float/Sand Walls & Ceilings	6	12/21/26	12/29/26
3890	Spray Texture	2	12/29/26	12/30/26
3895	Doors & Trim	2	12/30/26	12/31/26
3900	Prime & 1st Coat Paint	1	01/04/27	01/04/27
3905	Tub/Shower Wall Tile	4	01/05/27	01/08/27
3910	Bathroom Floor Tile	4	01/12/27	01/15/27
3915	Shower Doors & Mirrors	2	01/18/27	01/19/27
3920	Toilet Accessories	1	01/20/27	01/20/27
3925	Cabinets	3	01/05/27	01/07/27

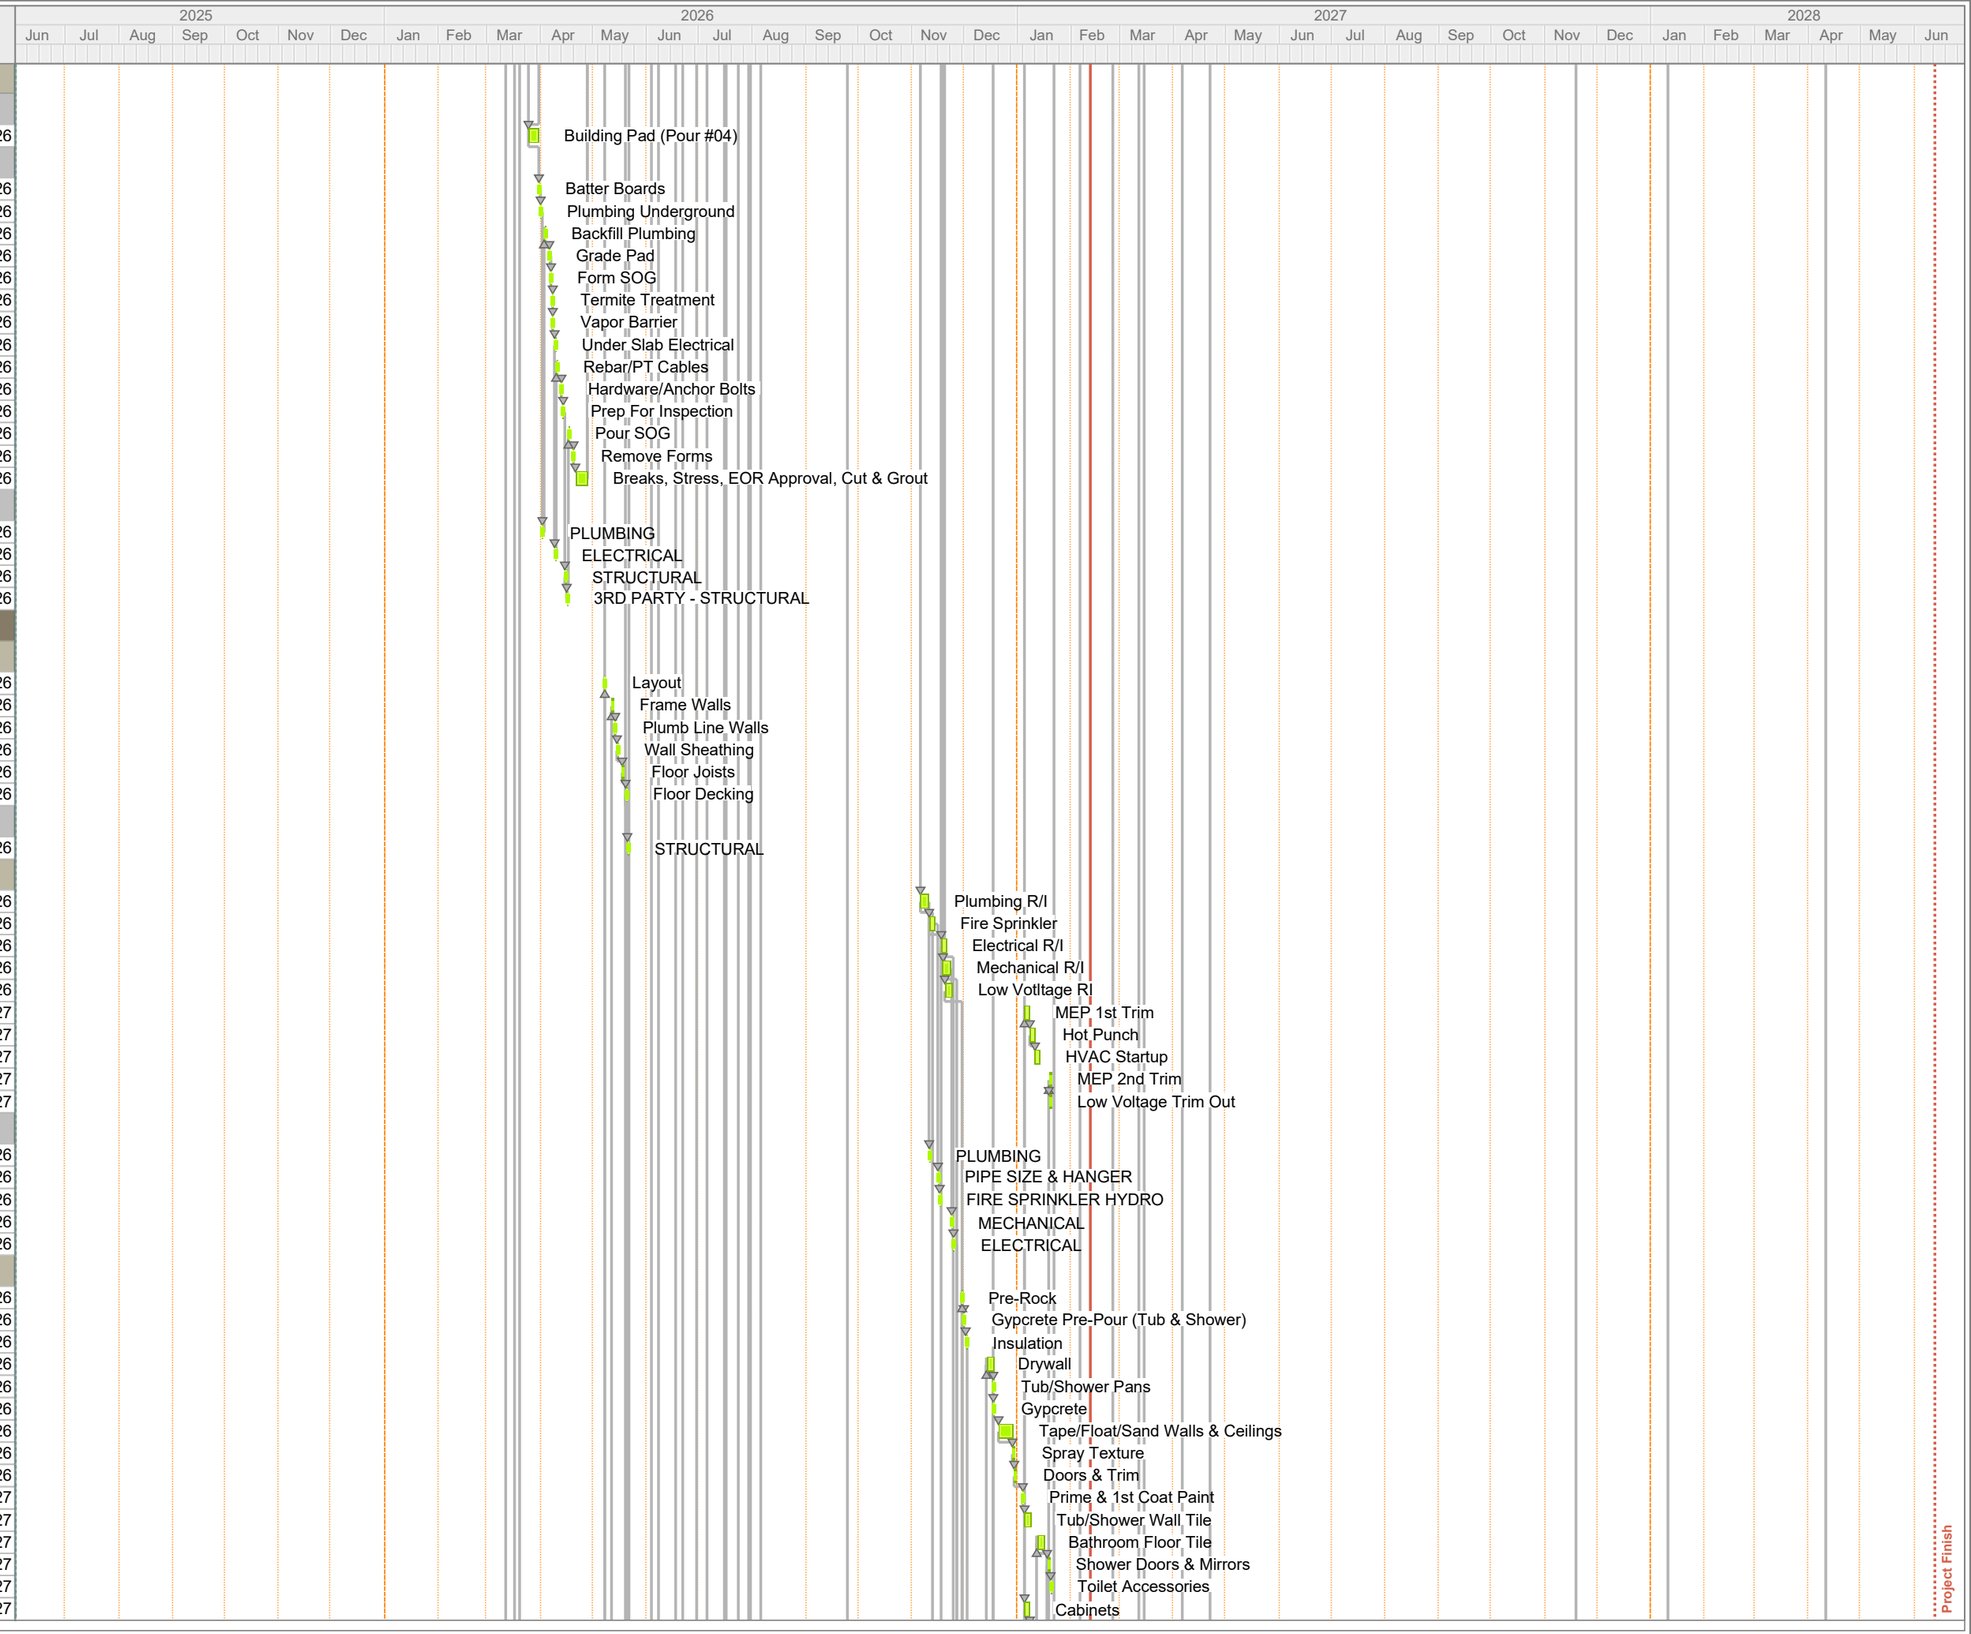

Initials: _____

3930	Countertops	2	01/08/27	01/11/27
3935	Drywall Touch Up	1	01/12/27	01/12/27
3940	Tile Backsplash	3	01/18/27	01/20/27
3945	LVT	5	02/12/27	02/18/27
3950	Shoe/Scribe Molding	2	02/19/27	02/22/27
3955	Rough Clean	2	02/22/27	02/23/27
3960	Completion List	1	02/24/27	02/24/27
3965	Appliances	1	02/25/27	02/25/27
3970	Blinds	1	02/26/27	02/26/27
3975	Final Paint	1	03/01/27	03/01/27
Inspections				
3980	STRUCTURAL	1	11/27/26	11/27/26
3985	INSULATION	1	12/03/26	12/03/26
Interior Punch List				
3990	Arch-Con Punch List	2	03/02/27	03/03/27
3995	Arch-Con Punch List Corrections	2	03/04/27	03/05/27
4000	Final Clean	1	03/08/27	03/08/27
4005	Owner Punch List	2	03/15/27	03/16/27
4010	Punch List Corrections	2	03/16/27	03/17/27
4015	Powder Puff	1	03/18/27	03/18/27
4020	Owner Acceptance	1	03/19/27	03/19/27
Lvl. 2				
Wood Framing				
4025	Layout	1	05/21/26	05/21/26
4030	Frame Walls	2	05/27/26	05/28/26
4035	Plumb Line Walls	1	05/29/26	05/29/26
4040	Wall Sheathing	1	06/01/26	06/01/26
4045	Floor Joists	2	06/02/26	06/03/26
4050	Floor Decking	1	06/04/26	06/04/26
Inspections				
4055	STRUCTURAL	1	06/05/26	06/05/26
MEPF				
4060	Plumbing R/I	3	11/13/26	11/17/26
4065	Fire Sprinkler	3	11/18/26	11/20/26
4070	Electrical R/I	3	11/25/26	11/30/26
4075	Mechanical R/I	3	11/27/26	12/01/26
4080	Low Votltage RI	3	11/30/26	12/02/26
4085	MEP 1st Trim	3	01/11/27	01/13/27
4090	Hot Punch	2	01/14/27	01/15/27
4095	HVAC Startup	3	01/18/27	01/20/27
4100	MEP 2nd Trim	2	01/26/27	01/27/27
4105	Low Voltage Trim Out	2	01/26/27	01/27/27
Inspections				
4110	PLUMBING	1	11/18/26	11/18/26
4115	PIPE SIZE & HANGER	1	11/23/26	11/23/26
4120	FIRE SPRINKLER HYDRO	1	11/24/26	11/24/26
4125	MECHANICAL	1	12/02/26	12/02/26
4130	ELECTRICAL	1	12/03/26	12/03/26
Buildout				
4135	Pre-Rock	1	12/07/26	12/07/26
4140	Gypcrete Pre-Pour (Tub & Shower)	1	12/08/26	12/08/26
4145	Insulation	1	12/09/26	12/09/26
4150	Drywall	4	12/18/26	12/23/26
4155	Tub/Shower Pans	1	12/24/26	12/24/26
4160	Gypcrete	1	12/24/26	12/24/26
4165	Tape/Float/Sand Walls & Ceilings	6	12/28/26	01/05/27
4170	Spray Texture	2	01/05/27	01/06/27
4175	Doors & Trim	2	01/06/27	01/07/27
4180	Prime & 1st Coat Paint	1	01/08/27	01/08/27
4185	Tub/Shower Wall Tile	4	01/11/27	01/14/27
4190	Bathroom Floor Tile	4	01/18/27	01/21/27
4195	Shower Doors & Mirrors	2	01/22/27	01/25/27
4200	Toilet Accessories	1	01/26/27	01/26/27
4205	Cabinets	3	01/11/27	01/13/27
4210	Countertops	2	01/14/27	01/15/27
4215	Drywall Touch Up	1	01/18/27	01/18/27
4220	Tile Backsplash	4	01/22/27	01/27/27

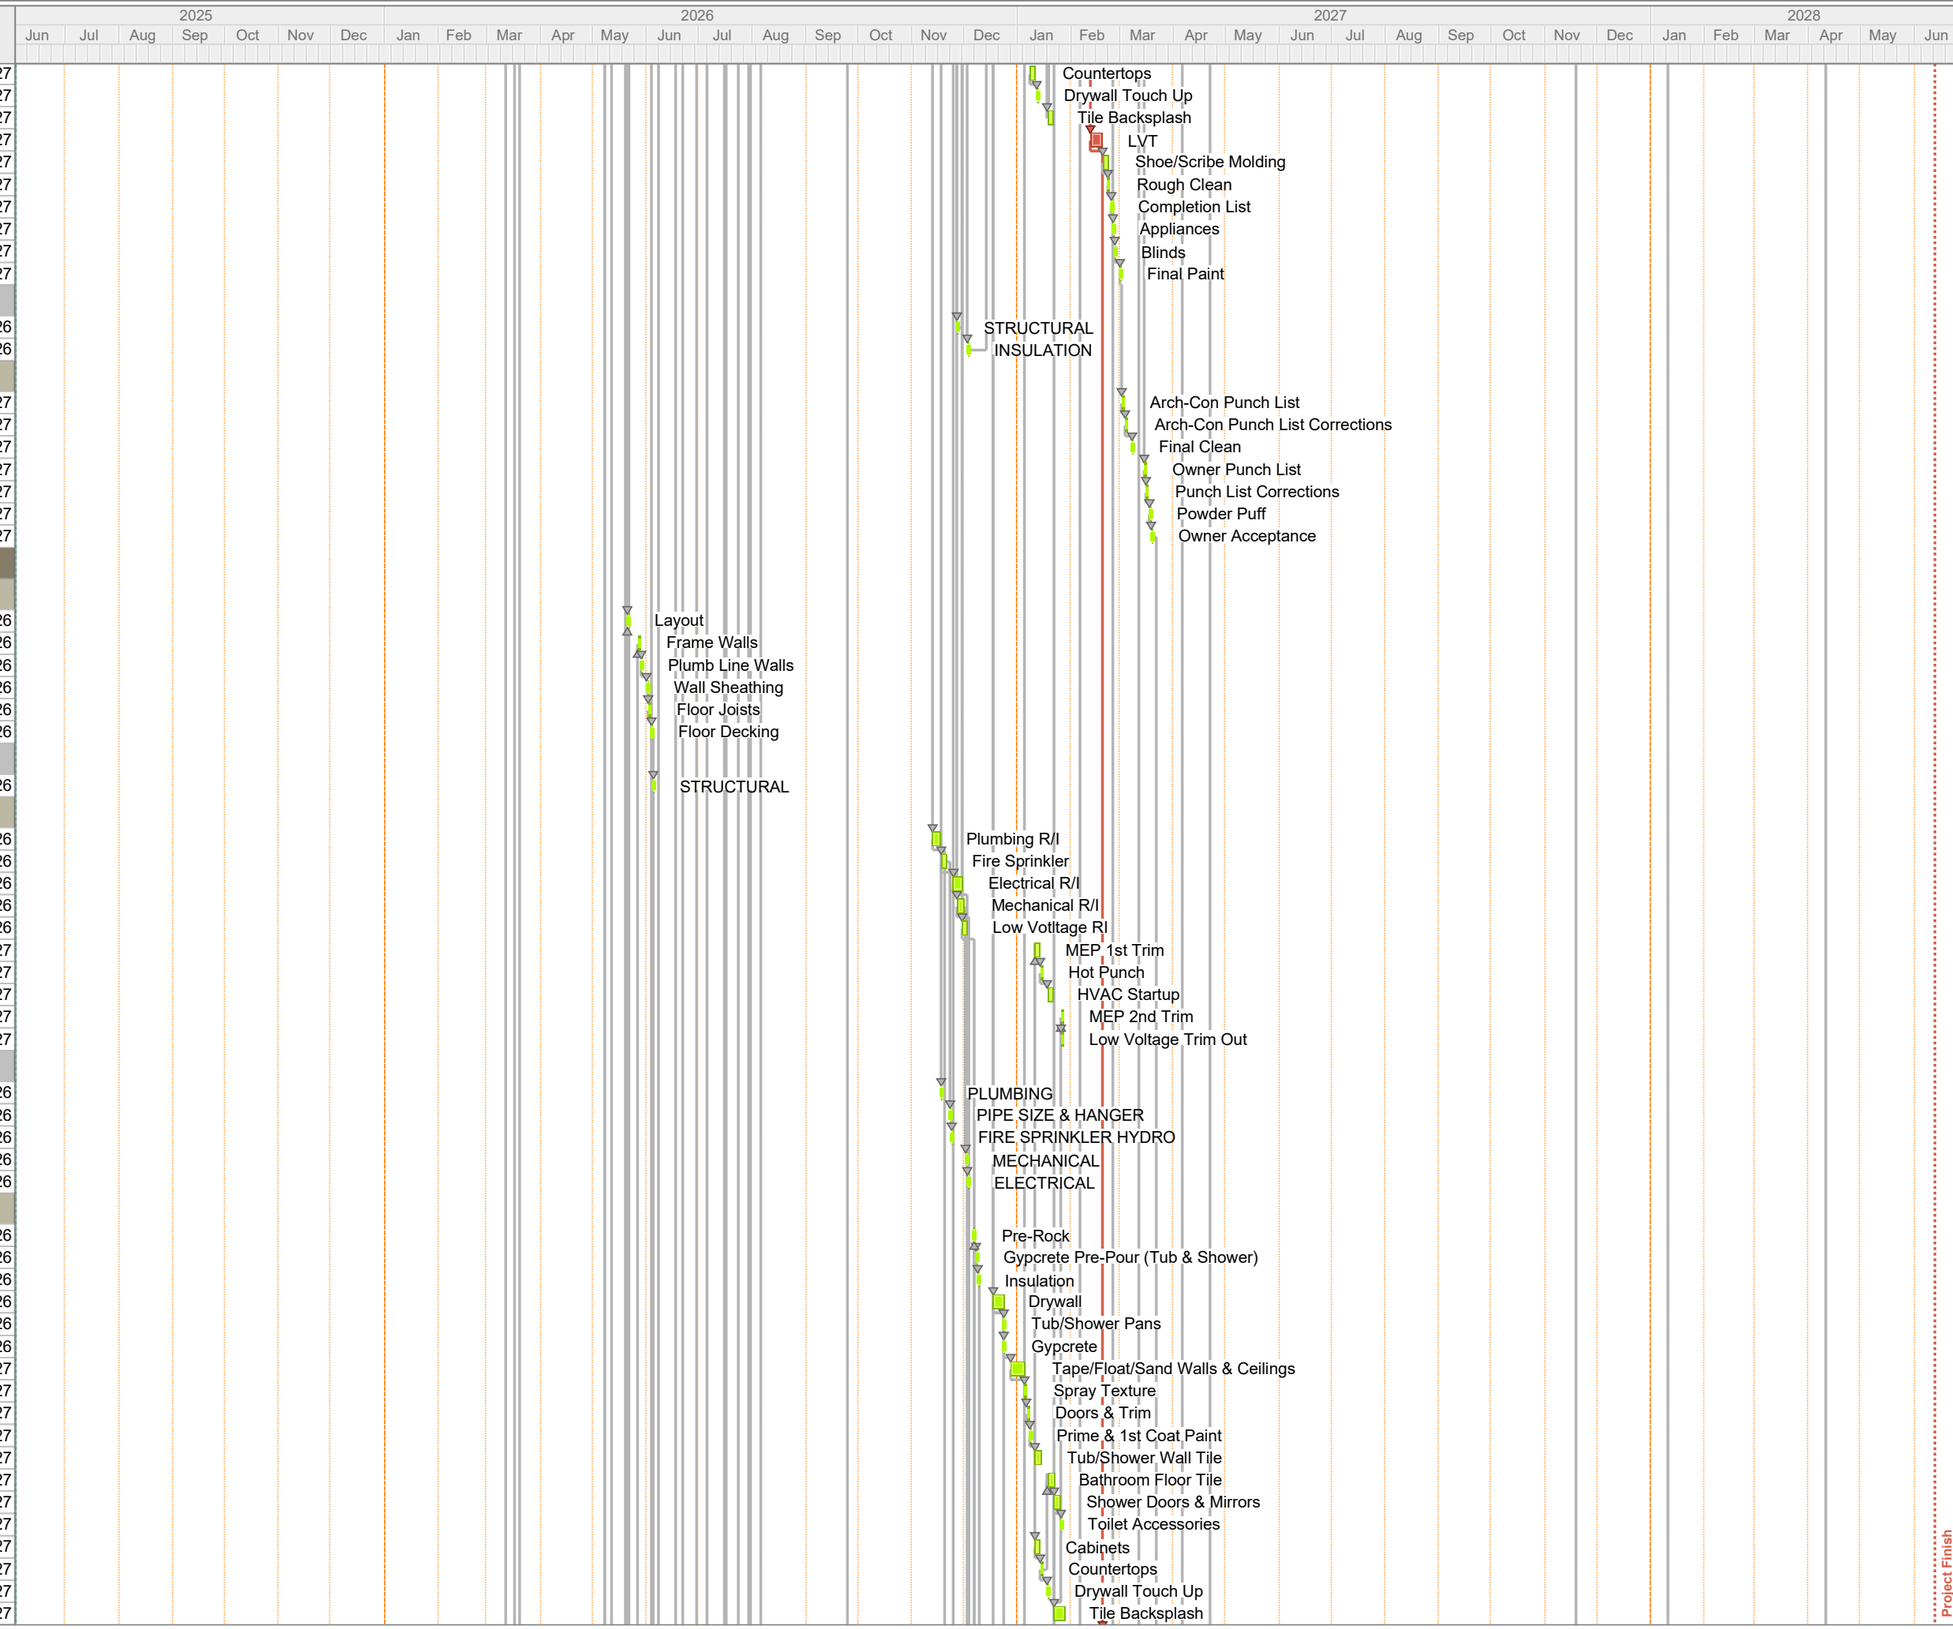

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

4225	LVT	5	02/19/27	02/25/27
4230	Shoe/Scribe Molding	2	02/26/27	03/01/27
4235	Rough Clean	2	03/01/27	03/02/27
4240	Completion List	1	03/03/27	03/03/27
4245	Appliances	1	03/04/27	03/04/27
4250	Blinds	1	03/05/27	03/05/27
4255	Final Paint	1	03/08/27	03/08/27
Inspections				
4260	STRUCTURAL	1	12/04/26	12/04/26
4265	INSULATION	1	12/10/26	12/10/26
Interior Punch List				
4270	Arch-Con Punch List	2	03/09/27	03/10/27
4275	Arch-Con Punch List Corrections	2	03/11/27	03/12/27
4280	Final Clean	1	03/15/27	03/15/27
4285	Owner Punch List	2	03/22/27	03/23/27
4290	Punch List Corrections	2	03/23/27	03/24/27
4295	Powder Puff	1	03/25/27	03/25/27
4300	Owner Acceptance	1	03/26/27	03/26/27
Lvl. 3				
Wood Framing				
4305	Layout	1	06/05/26	06/05/26
4310	Frame Walls	2	06/10/26	06/11/26
4315	Plumb Line Walls	1	06/12/26	06/12/26
4320	Wall Sheathing	1	06/15/26	06/15/26
4325	Floor Joists	2	06/16/26	06/17/26
4330	Floor Decking	1	06/18/26	06/18/26
Inspections				
4335	STRUCTURAL	1	06/19/26	06/19/26
MEPF				
4340	Plumbing R/I	3	11/20/26	11/24/26
4345	Fire Sprinkler	3	11/25/26	11/30/26
4350	Electrical R/I	3	12/03/26	12/07/26
4355	Mechanical R/I	3	12/04/26	12/08/26
4360	Low Votltage RI	3	12/07/26	12/09/26
4365	MEP 1st Trim	3	01/15/27	01/19/27
4370	Hot Punch	2	01/20/27	01/21/27
4375	HVAC Startup	3	01/21/27	01/25/27
4380	MEP 2nd Trim	2	01/29/27	02/01/27
4385	Low Voltage Trim Out	2	01/29/27	02/01/27
Inspections				
4390	PLUMBING	1	11/25/26	11/25/26
4395	PIPE SIZE & HANGER	1	11/30/26	11/30/26
4400	FIRE SPRINKLER HYDRO	1	12/01/26	12/01/26
4405	MECHANICAL	1	12/09/26	12/09/26
4410	ELECTRICAL	1	12/10/26	12/10/26
Buildout				
4415	Pre-Rock	1	12/14/26	12/14/26
4420	Gypcrete Pre-Pour (Tub & Shower)	1	12/15/26	12/15/26
4425	Insulation	1	12/16/26	12/16/26
4430	Drywall	4	12/24/26	12/30/26
4435	Tub/Shower Pans	1	12/31/26	12/31/26
4440	Gypcrete	1	12/31/26	12/31/26
4445	Tape/Float/Sand Walls & Ceilings	6	01/04/27	01/11/27
4450	Spray Texture	2	01/11/27	01/12/27
4455	Doors & Trim	2	01/12/27	01/13/27
4460	Prime & 1st Coat Paint	1	01/14/27	01/14/27
4465	Tub/Shower Wall Tile	4	01/15/27	01/20/27
4470	Bathroom Floor Tile	4	01/22/27	01/27/27
4475	Shower Doors & Mirrors	2	01/28/27	01/29/27
4480	Toilet Accessories	1	02/01/27	02/01/27
4485	Cabinets	3	01/15/27	01/19/27
4490	Countertops	2	01/20/27	01/21/27
4495	Drywall Touch Up	1	01/22/27	01/22/27
4500	Tile Backsplash	4	01/28/27	02/02/27
4505	LVT	5	02/26/27	03/04/27
4510	Shoe/Scribe Molding	2	03/05/27	03/08/27
4515	Rough Clean	2	03/08/27	03/09/27

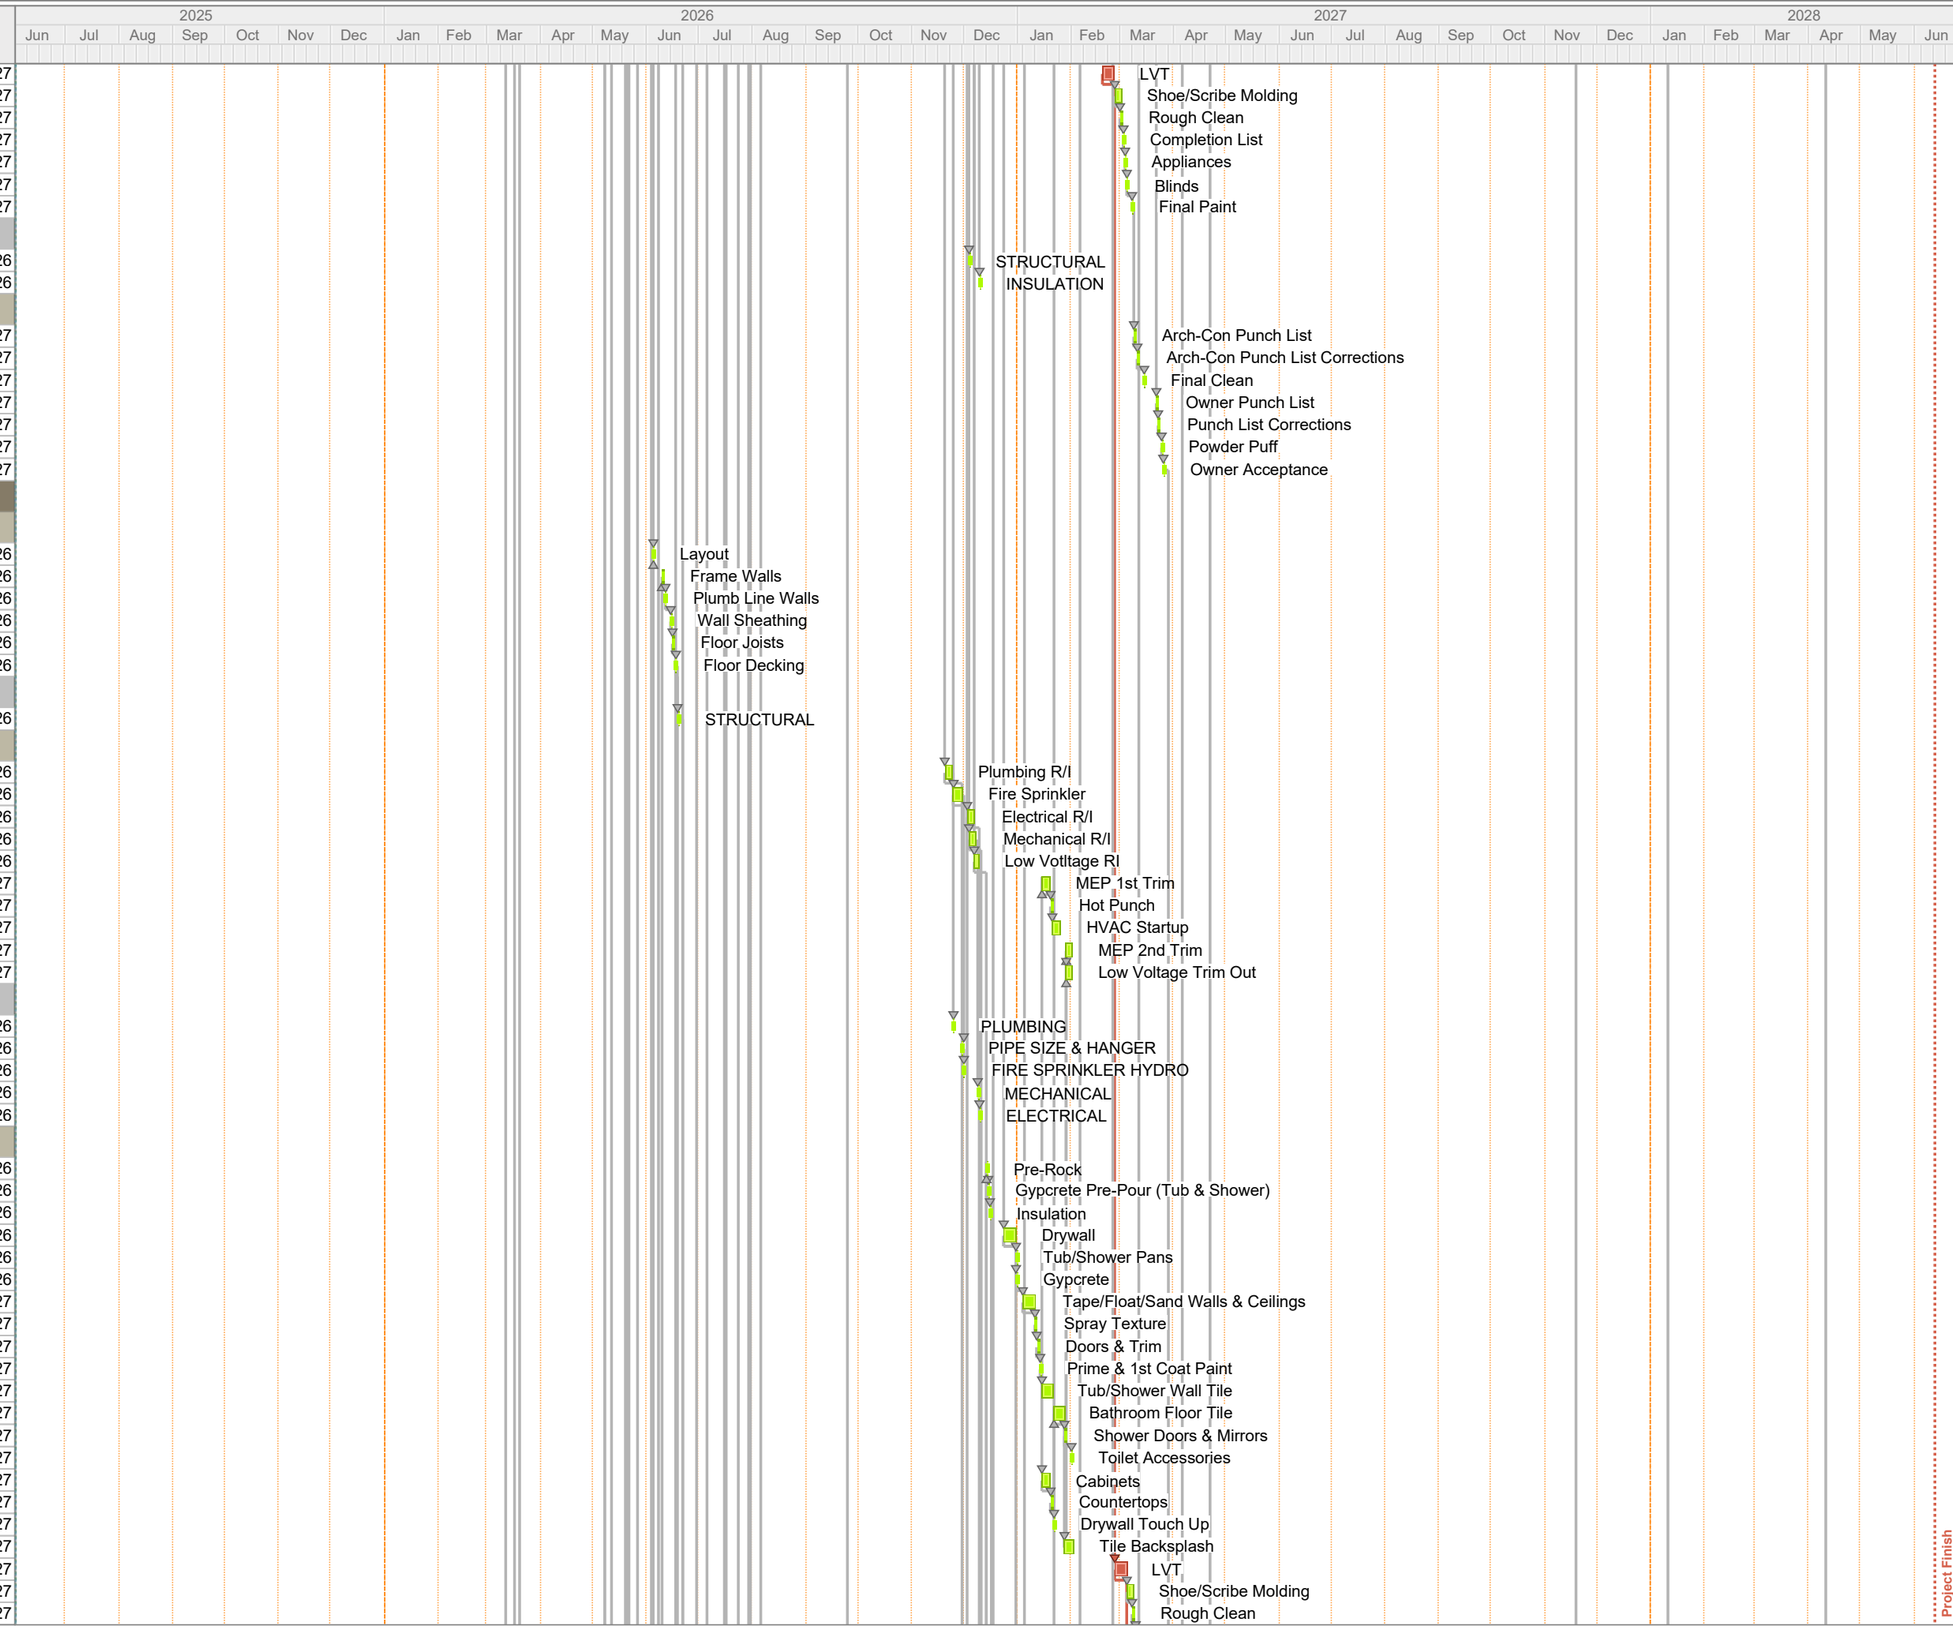

Initials: _____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

4520	Completion List	1	03/10/27	03/10/27
4525	Appliances	1	03/11/27	03/11/27
4530	Blinds	1	03/12/27	03/12/27
4535	Final Paint	1	03/15/27	03/15/27
Inspections				
4540	STRUCTURAL	1	12/11/26	12/11/26
4545	INSULATION	1	12/17/26	12/17/26
Interior Punch List				
4550	Arch-Con Punch List	2	03/16/27	03/17/27
4555	Arch-Con Punch List Corrections	2	03/18/27	03/19/27
4560	Final Clean	1	03/22/27	03/22/27
4565	Owner Punch List	2	03/29/27	03/30/27
4570	Punch List Corrections	2	03/30/27	03/31/27
4575	Powder Puff	1	04/01/27	04/01/27
4580	Owner Acceptance	1	04/02/27	04/02/27
Lvl. 4				
Wood Framing				
4585	Layout	1	06/19/26	06/19/26
4590	Frame Walls	2	06/24/26	06/25/26
4595	Plumb Line Walls	1	06/26/26	06/26/26
4600	Wall Sheathing	1	06/29/26	06/29/26
4605	Floor Joists	2	06/30/26	07/01/26
4610	Floor Decking	1	07/02/26	07/02/26
Inspections				
4615	STRUCTURAL	1	07/03/26	07/03/26
MEPF				
4620	Plumbing R/I	3	11/30/26	12/02/26
4625	Fire Sprinkler	3	12/03/26	12/07/26
4630	Electrical R/I	3	12/10/26	12/14/26
4635	Mechanical R/I	3	12/11/26	12/15/26
4640	Low Votltage RI	3	12/14/26	12/16/26
4645	MEP 1st Trim	3	01/21/27	01/25/27
4650	Hot Punch	2	01/26/27	01/27/27
4655	HVAC Startup	3	01/27/27	01/29/27
4660	MEP 2nd Trim	2	02/04/27	02/05/27
4665	Low Voltage Trim Out	2	02/04/27	02/05/27
Inspections				
4670	PLUMBING	1	12/03/26	12/03/26
4675	PIPE SIZE & HANGER	1	12/07/26	12/07/26
4680	FIRE SPRINKLER HYDRO	1	12/08/26	12/08/26
4685	MECHANICAL	1	12/16/26	12/16/26
4690	ELECTRICAL	1	12/17/26	12/17/26
Buildout				
4695	Pre-Rock	1	12/21/26	12/21/26
4700	Gypcrete Pre-Pour (Tub & Shower)	1	12/22/26	12/22/26
4705	Insulation	1	12/23/26	12/23/26
4710	Drywall	4	12/31/26	01/06/27
4715	Tub/Shower Pans	1	01/07/27	01/07/27
4720	Gypcrete	1	01/07/27	01/07/27
4725	Tape/Float/Sand Walls & Ceilings	6	01/08/27	01/15/27
4730	Spray Texture	2	01/15/27	01/18/27
4735	Doors & Trim	2	01/18/27	01/19/27
4740	Prime & 1st Coat Paint	1	01/20/27	01/20/27
4745	Tub/Shower Wall Tile	4	01/21/27	01/26/27
4750	Bathroom Floor Tile	4	01/28/27	02/02/27
4755	Shower Doors & Mirrors	2	02/02/27	02/03/27
4760	Toilet Accessories	1	02/04/27	02/04/27
4765	Cabinets	3	01/21/27	01/25/27
4770	Countertops	2	01/26/27	01/27/27
4775	Drywall Touch Up	1	01/28/27	01/28/27
4780	Tile Backsplash	4	02/03/27	02/08/27
4785	LVT	5	03/05/27	03/11/27
4790	Shoe/Scribe Molding	2	03/12/27	03/15/27
4795	Rough Clean	2	03/15/27	03/16/27
4800	Completion List	1	03/17/27	03/17/27
4805	Appliances	1	03/18/27	03/18/27
4810	Blinds	1	03/19/27	03/19/27

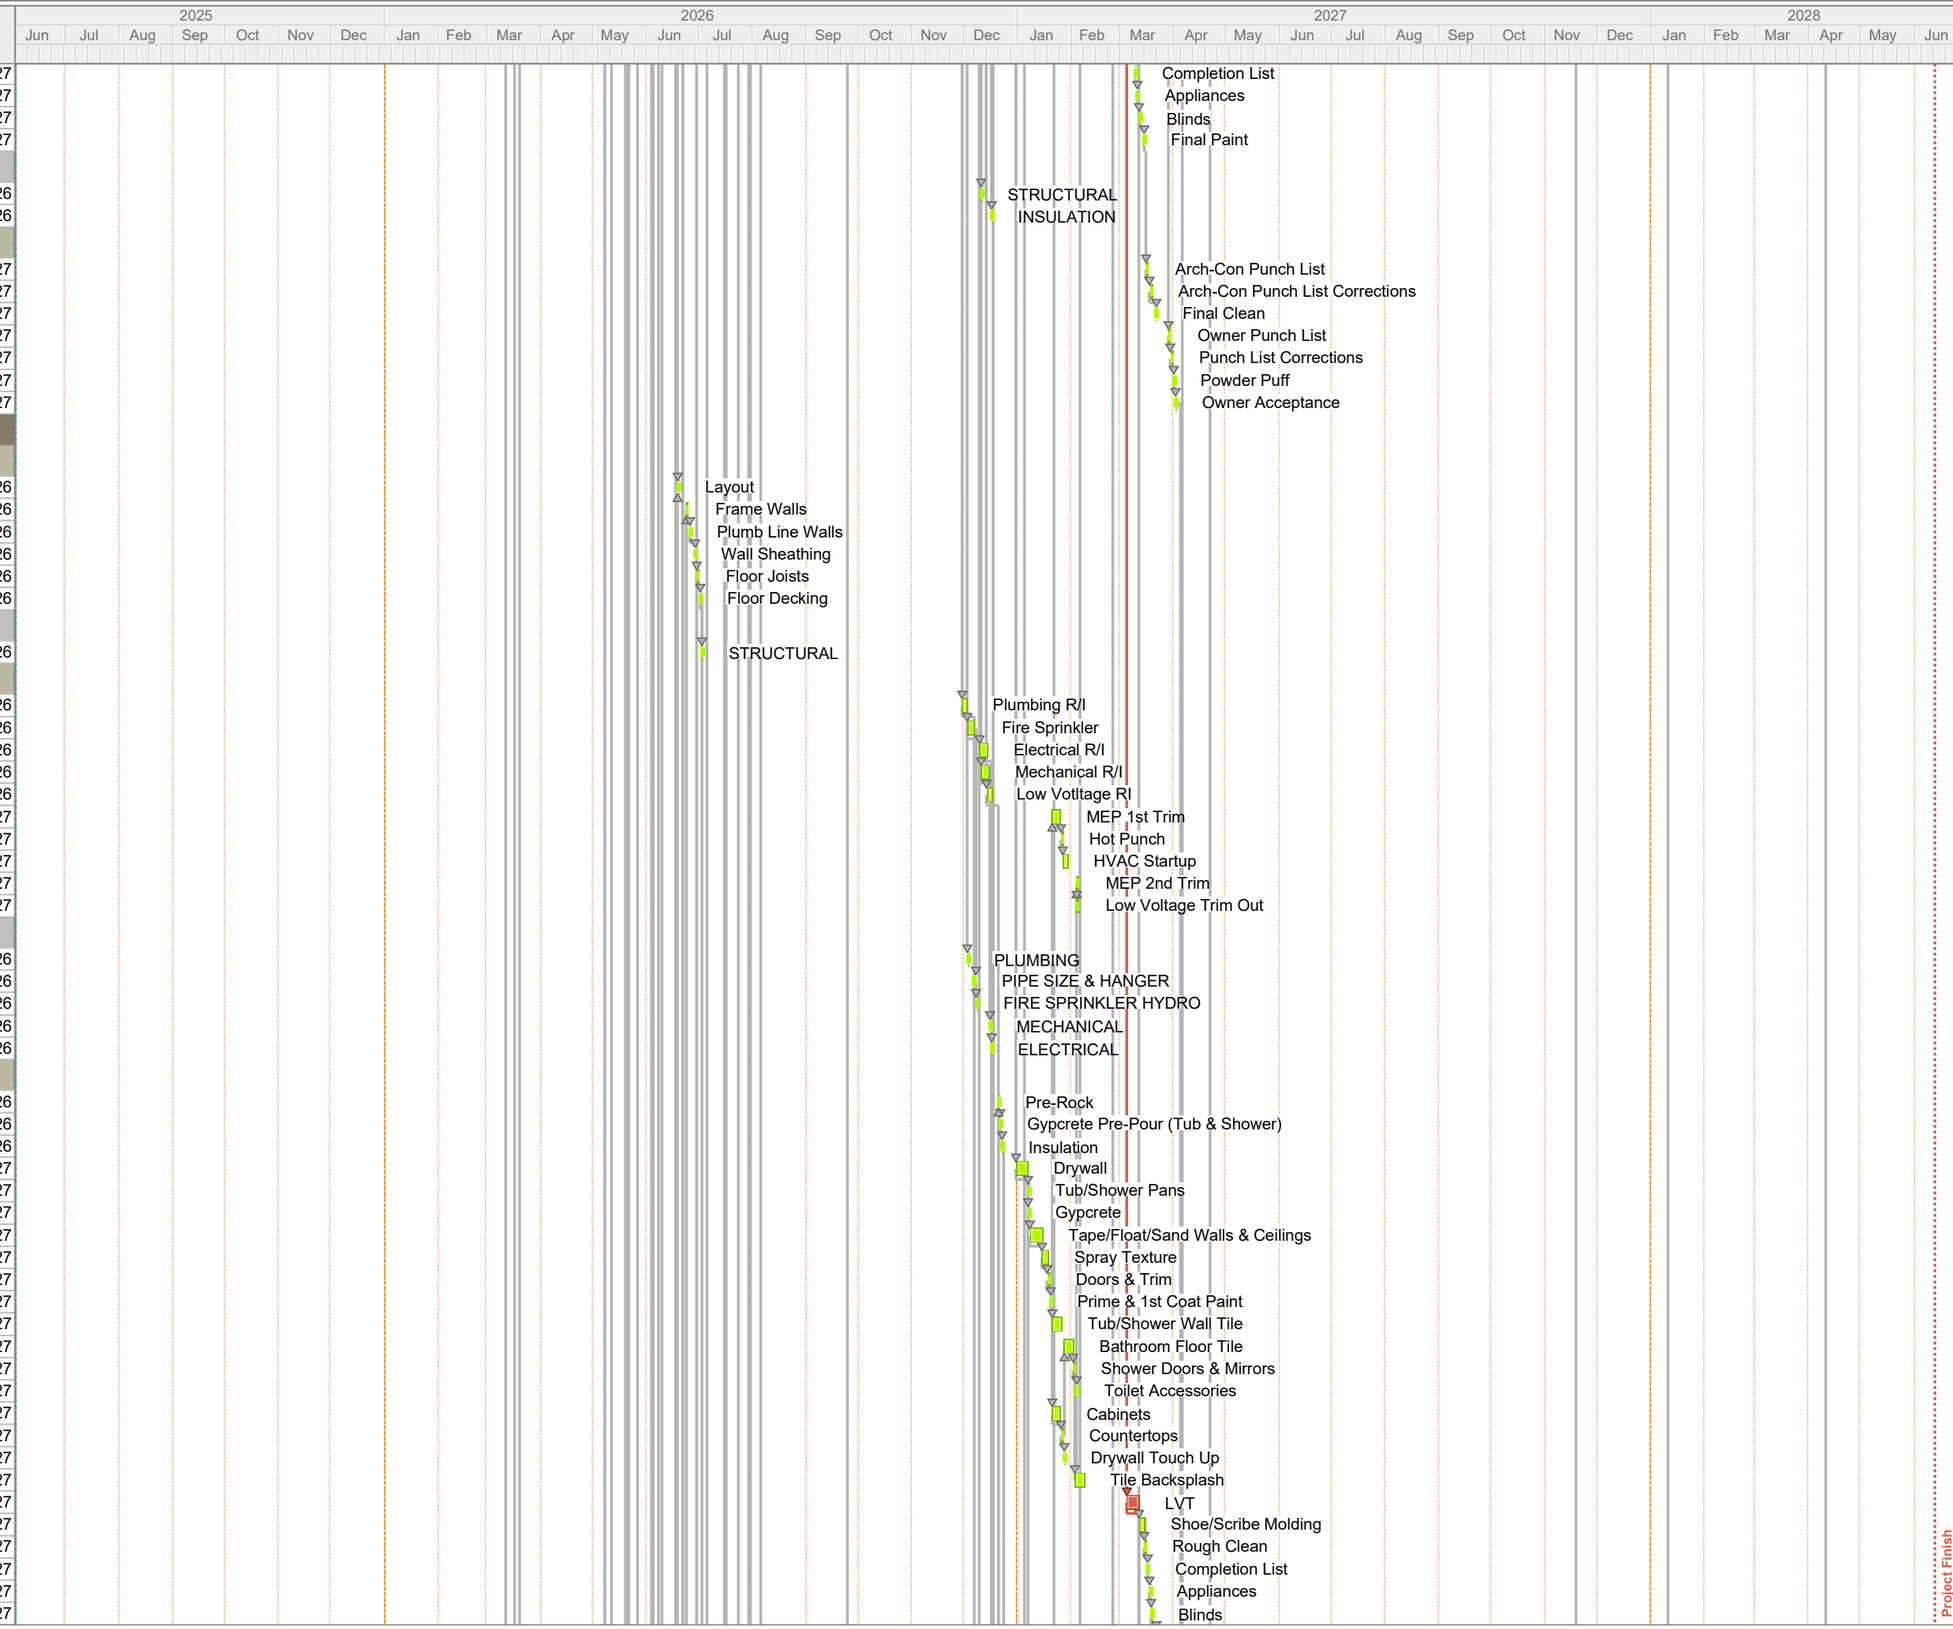

Initials: _____

4815	Final Paint	1	03/22/27	03/22/27
Inspections				
4820	STRUCTURAL	1	12/18/26	12/18/26
4825	INSULATION	1	12/24/26	12/24/26
Interior Punch List				
4830	Arch-Con Punch List	2	03/23/27	03/24/27
4835	Arch-Con Punch List Corrections	2	03/25/27	03/26/27
4840	Final Clean	1	03/29/27	03/29/27
4845	Owner Punch List	2	04/05/27	04/06/27
4850	Punch List Corrections	2	04/06/27	04/07/27
4855	Powder Puff	1	04/08/27	04/08/27
4860	Owner Acceptance	1	04/09/27	04/09/27
Lvl. 5				
Wood Framing				
4865	Layout	1	07/03/26	07/03/26
4870	Frame Walls	2	07/15/26	07/16/26
4875	Plumb Line Walls	1	07/17/26	07/17/26
4880	Roof Joists	2	07/20/26	07/21/26
4885	Roof Decking	1	07/22/26	07/22/26
Inspections				
4890	STRUCTURAL	1	07/23/26	07/23/26
MEPF				
4895	Plumbing R/I	3	12/07/26	12/09/26
4900	Fire Sprinkler	3	12/10/26	12/14/26
4905	Electrical R/I	3	12/17/26	12/21/26
4910	Mechanical R/I	3	12/18/26	12/22/26
4915	Low Votltage RI	3	12/21/26	12/23/26
4920	MEP 1st Trim	3	01/27/27	01/29/27
4925	Hot Punch	2	02/01/27	02/02/27
4930	HVAC Startup	3	02/03/27	02/05/27
4935	MEP 2nd Trim	2	02/10/27	02/11/27
4940	Low Voltage Trim Out	2	02/12/27	02/15/27
Inspections				
4945	PLUMBING	1	12/10/26	12/10/26
4950	PIPE SIZE & HANGER	1	12/14/26	12/14/26
4955	FIRE SPRINKLER HYDRO	1	12/15/26	12/15/26
4960	MECHANICAL	1	12/23/26	12/23/26
4965	ELECTRICAL	1	12/24/26	12/24/26
Buildout				
4970	Pre-Rock	1	12/29/26	12/29/26
4975	Gypcrete Pre-Pour (Tub & Shower)	1	12/30/26	12/30/26
4980	Insulation	1	12/31/26	12/31/26
4985	Drywall	4	01/07/27	01/12/27
4990	Tub/Shower Pans	1	01/13/27	01/13/27
4995	Gypcrete	1	01/13/27	01/13/27
5000	Tape/Float/Sand Walls & Ceilings	6	01/14/27	01/21/27
5005	Spray Texture	2	01/21/27	01/22/27
5010	Doors & Trim	2	01/22/27	01/25/27
5015	Prime & 1st Coat Paint	1	01/26/27	01/26/27
5020	Tub/Shower Wall Tile	4	01/27/27	02/01/27
5025	Bathroom Floor Tile	4	02/03/27	02/08/27
5030	Shower Doors & Mirrors	2	02/08/27	02/09/27
5035	Toilet Accessories	1	02/10/27	02/10/27
5040	Cabinets	3	01/27/27	01/29/27
5045	Countertops	2	02/01/27	02/02/27
5050	Drywall Touch Up	1	02/03/27	02/03/27
5055	Tile Backsplash	4	02/09/27	02/12/27
5060	LVT	5	03/12/27	03/18/27
5065	Shoe/Scribe Molding	2	03/19/27	03/22/27
5070	Rough Clean	2	03/22/27	03/23/27
5075	Completion List	1	03/24/27	03/24/27
5080	Appliances	1	03/25/27	03/25/27
5085	Blinds	1	03/26/27	03/26/27
5090	Final Paint	1	03/29/27	03/29/27
Inspections				
5095	STRUCTURAL	1	12/28/26	12/28/26

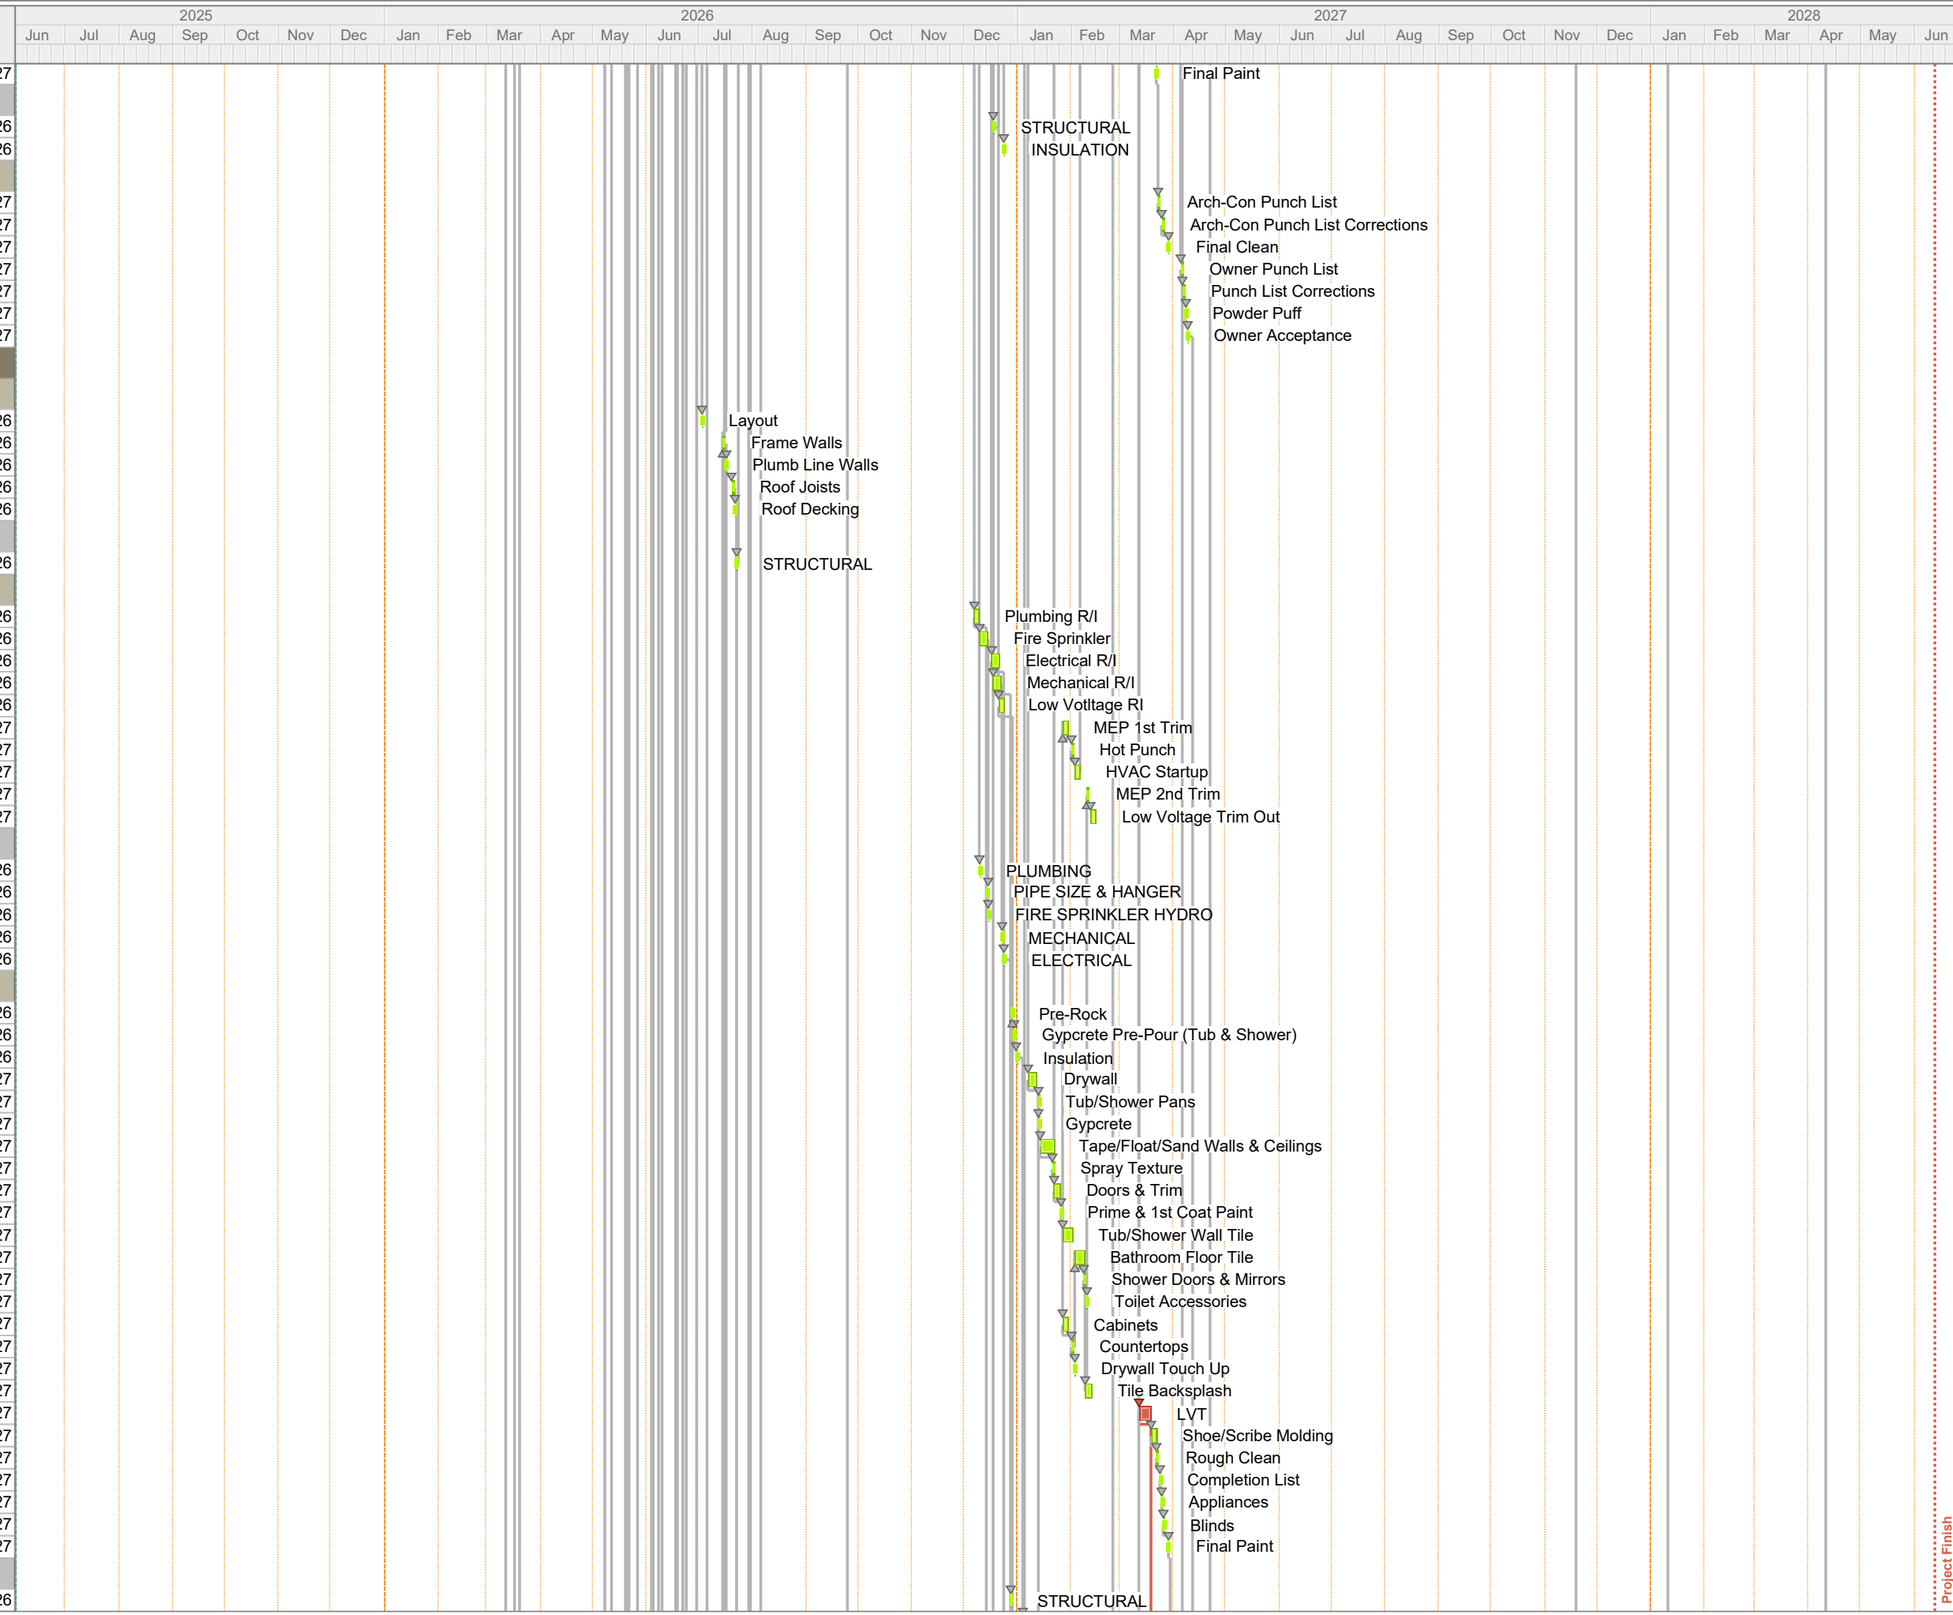

Initials: _____

5100	INSULATION	1	01/04/27	01/04/27
Interior Punch List				
5105	Arch-Con Punch List	2	03/30/27	03/31/27
5110	Arch-Con Punch List Corrections	2	04/01/27	04/02/27
5115	Final Clean	1	04/05/27	04/05/27
5120	Owner Punch List	2	04/12/27	04/13/27
5125	Punch List Corrections	2	04/13/27	04/14/27
5130	Powder Puff	1	04/15/27	04/15/27
5135	Owner Acceptance	1	04/16/27	04/16/27
Building Exterior				
Roof				
5140	TPO Roofing	10	07/23/26	08/05/26
North Elevation				
5145	Windows	10	06/22/26	07/03/26
5150	Waterproofing	10	06/25/26	07/08/26
5155	Exterior Storefront	10	07/02/26	07/15/26
5160	Storefront Glass	10	07/02/26	07/15/26
5165	Masonry/Brick	10	07/14/26	07/27/26
5170	Hardi & Trim	10	07/24/26	08/06/26
5175	Paint Prep (Caulk, Prime, 1st Coat)	10	08/05/26	08/18/26
5180	Final Paint	10	08/17/26	08/28/26
South Elevation (Right)				
5185	Windows	10	07/06/26	07/17/26
5190	Waterproofing	10	07/09/26	07/22/26
5195	Exterior Storefront	10	07/16/26	07/29/26
5200	Storefront Glass	10	07/16/26	07/29/26
5205	Masonry/Brick	10	07/28/26	08/10/26
5210	Hardi & Trim	10	08/07/26	08/20/26
5215	Paint Prep (Caulk, Prime, 1st Coat)	10	08/19/26	09/01/26
5220	Final Paint	10	08/31/26	09/14/26
Exterior Punch List				
5225	Arch-Con Punch List	1	09/15/26	09/15/26
5230	Arch-Con Punch List Corrections	2	09/16/26	09/17/26
5235	Final Clean	1	09/18/26	09/18/26
5240	Owner Punch List	1	09/21/26	09/21/26
5245	Punch List Corrections	1	09/22/26	09/22/26
5250	Powder Puff	1	09/23/26	09/23/26
5255	Owner Acceptance	1	09/24/26	09/24/26
Stair				
D				
5260	Stair D	30	07/17/26	08/27/26
5265	Landings, Stringers, and Metal Pans	30	07/23/26	09/02/26
Pool Courtyard				
5270	Pool Courtyard	90	08/19/26	12/24/26
Exterior Punch List				
5275	Arch-Con Punch List	1	12/28/26	12/28/26
5280	Arch-Con Punch List Corrections	2	12/29/26	12/30/26
5285	Final Clean	1	12/31/26	12/31/26
5290	Owner Punch List	1	01/04/27	01/04/27
5295	Punch List Corrections	1	01/05/27	01/05/27
5300	Powder Puff	1	01/06/27	01/06/27
5305	Owner Acceptance	1	01/07/27	01/07/27
Final Inspections				
5310	HEALTH	10	01/08/27	01/21/27
5315	Knox Boxes	15	01/22/27	02/11/27
5320	MECHANICAL	15	04/15/27	05/05/27
5325	ELECTRICAL	15	05/06/27	05/26/27
5330	PLUMBING	15	05/27/27	06/16/27
5335	STRUCTURAL	15	06/17/27	07/07/27
5340	FIRE SPRINKLER & FIRE ALARM	15	07/08/27	07/28/27
5345	EGRESS	15	07/29/27	08/18/27
Systems Verification				
5350	Systems Verification	40	08/19/27	10/14/27
Weather				
5355	Weather Impacts Days	25	10/15/27	11/18/27

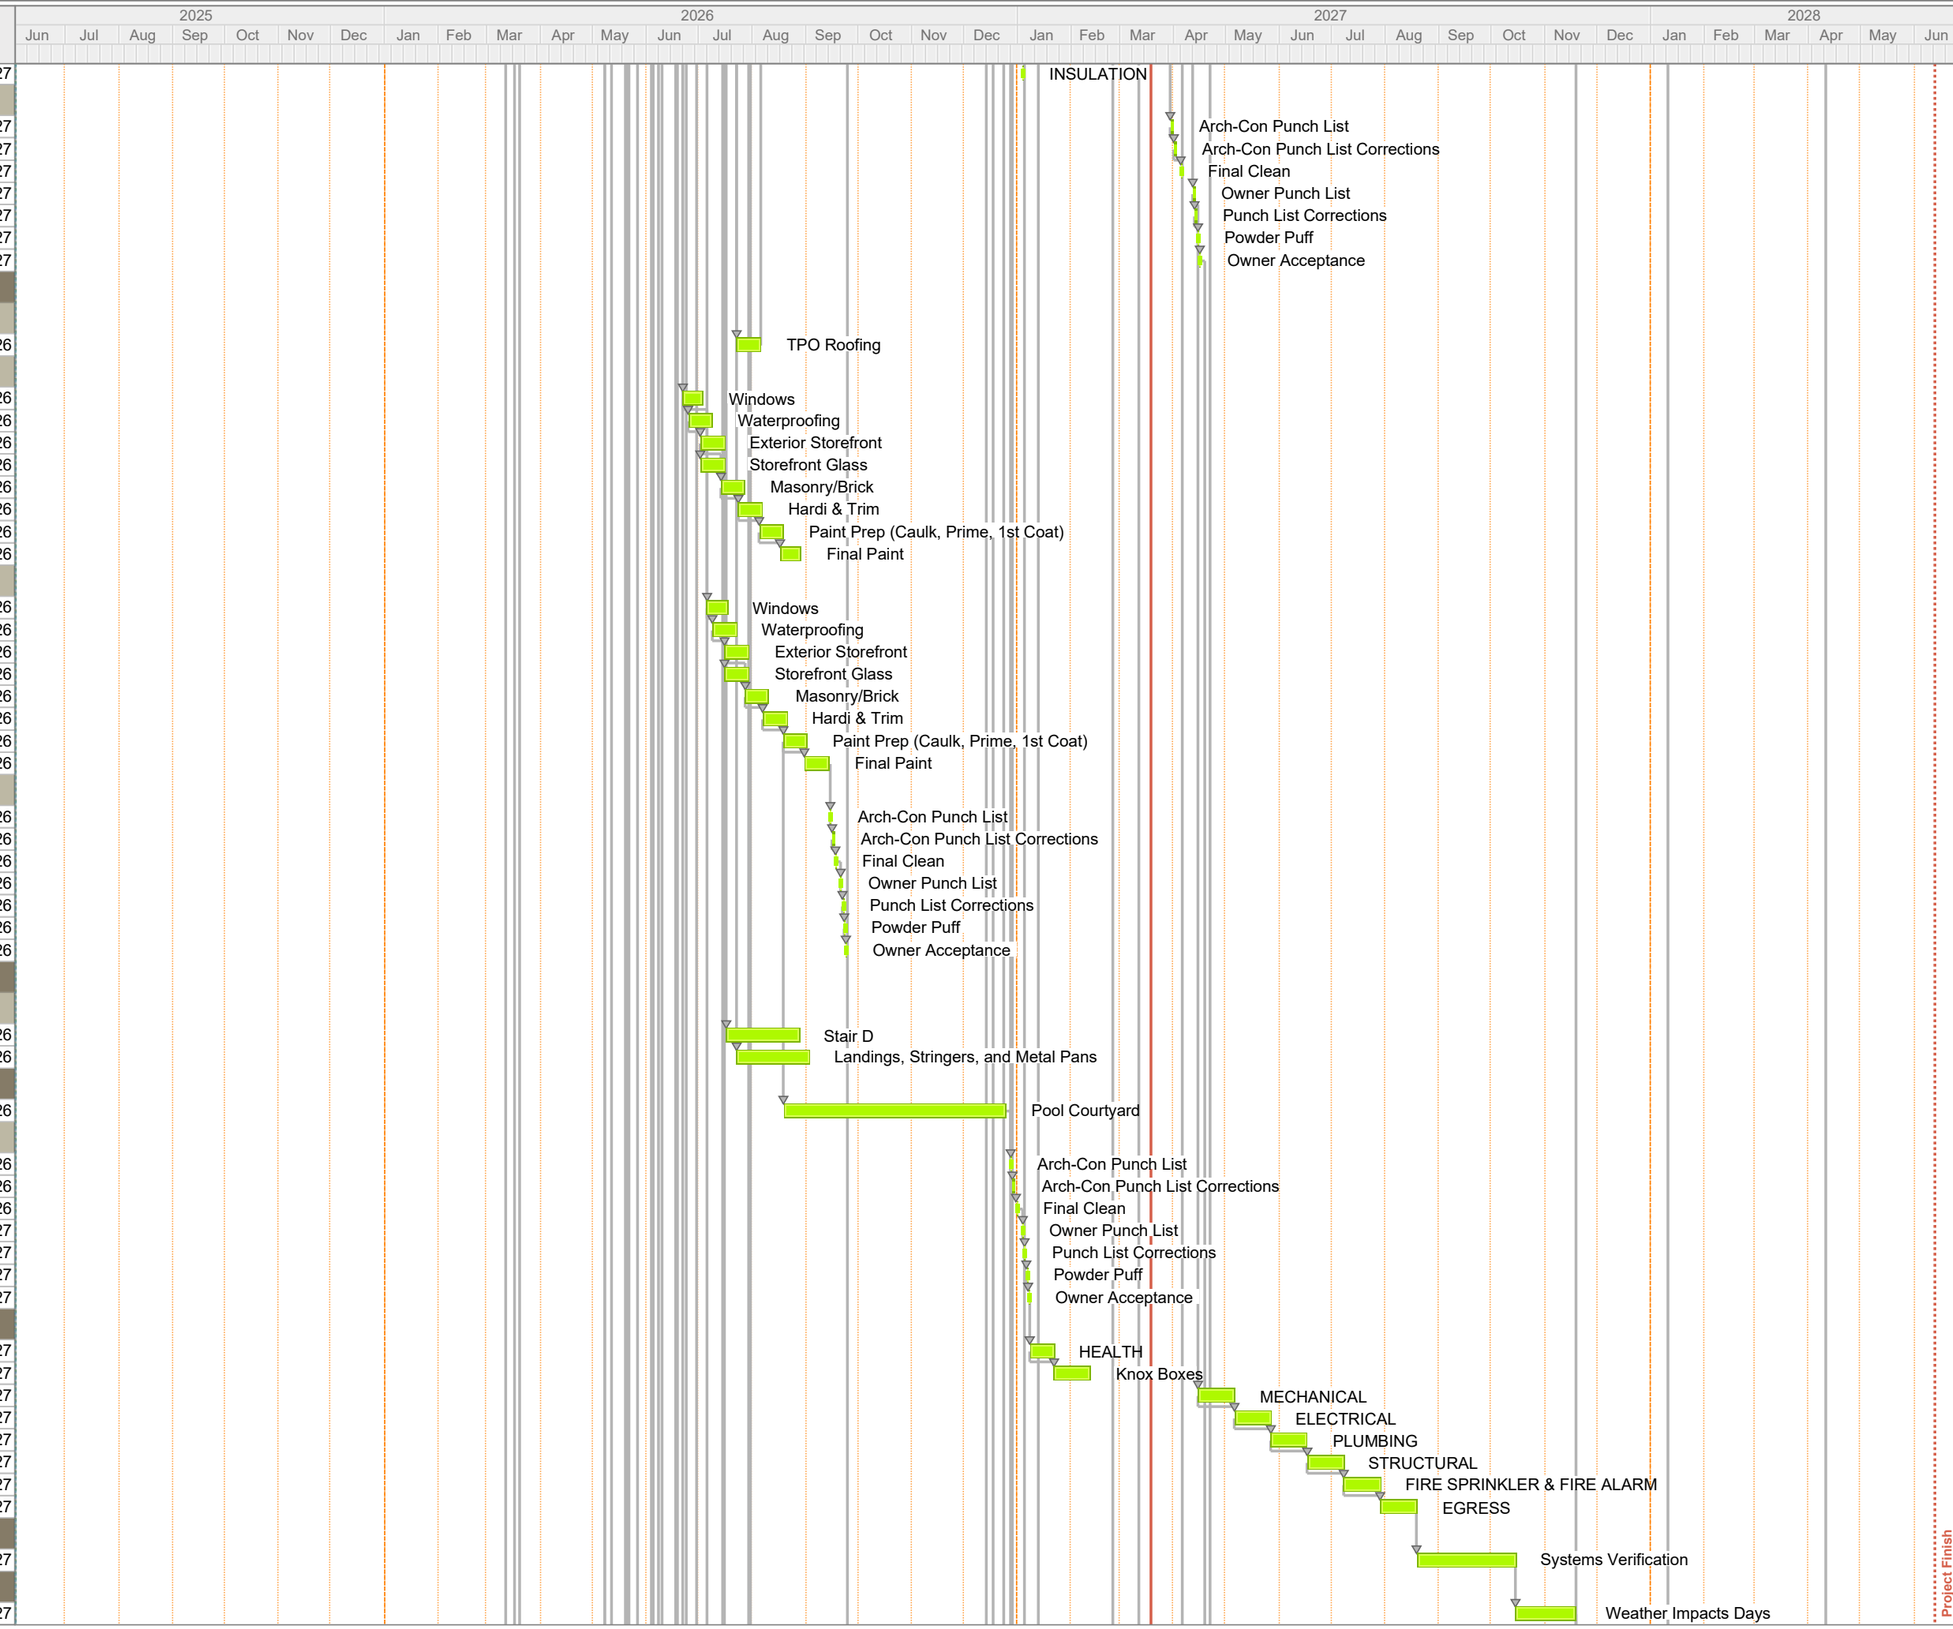

Initials: _____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

Substatial Completion				
5360	Substantial Completion	0		11/18/27
Phase 3 (75 Units)				
Slab on Grade				
Pour #01				
Earthwork				
5365	Building Pad (Pour #01)	3	03/12/26	03/16/26
Concrete				
5370	Batter Boards	1	03/17/26	03/17/26
5375	Plumbing Underground	2	03/18/26	03/19/26
5380	Backfill Plumbing	1	03/23/26	03/23/26
5385	Grade Pad	1	03/24/26	03/24/26
5390	Form SOG	1	03/25/26	03/25/26
5395	Termite Treatment	1	03/26/26	03/26/26
5400	Vapor Barrier	1	03/27/26	03/27/26
5405	Under Slab Electrical	1	03/30/26	03/30/26
5410	Rebar/PT Cables	1	03/31/26	03/31/26
5415	Hardware/Anchor Bolts	1	04/01/26	04/01/26
5420	Prep For Inspection	1	04/02/26	04/02/26
5425	Pour SOG	1	04/07/26	04/07/26
5430	Remove Forms	1	04/08/26	04/08/26
5435	Breaks, Stress, EOR Approval, Cut & (	5	04/09/26	04/15/26
Inspections				
5440	PLUMBING	1	03/20/26	03/20/26
5445	ELECTRICAL	1	03/30/26	03/30/26
5450	3RD PARTY	1	04/03/26	04/03/26
5455	STRUCTURAL	1	04/06/26	04/06/26
Pour #02				
Earthwork				
5460	Building Pad (Pour #02)	3	03/17/26	03/19/26
Concrete				
5465	Batter Boards	1	04/09/26	04/09/26
5470	Plumbing Underground	2	04/10/26	04/13/26
5475	Backfill Plumbing	1	04/15/26	04/15/26
5480	Grade Pad	1	04/16/26	04/16/26
5485	Form SOG	1	04/17/26	04/17/26
5490	Termite Treatment	1	04/20/26	04/20/26
5495	Vapor Barrier	1	04/20/26	04/20/26
5500	Under Slab Electrical	1	04/21/26	04/21/26
5505	Rebar/PT Cables	1	04/22/26	04/22/26
5510	Hardware/Anchor Bolts	1	04/23/26	04/23/26
5515	Prep For Inspection	1	04/24/26	04/24/26
5520	Pour SOG	1	04/29/26	04/29/26
5525	Remove Forms	1	04/30/26	04/30/26
5530	Breaks, Stress, EOR Approval, Cut & (	5	05/01/26	05/07/26
Inspections				
5535	PLUMBING	1	04/14/26	04/14/26
5540	ELECTRICAL	1	04/21/26	04/21/26
5545	SOG	1	04/27/26	04/27/26
5550	3RD PARTY - STRUCTURAL	1	04/28/26	04/28/26
Lvl. 1				
Wood Framing				
5555	Layout	1	05/07/26	05/07/26
5560	Frame Walls	2	05/08/26	05/11/26
5565	Plumb Line Walls	1	05/12/26	05/12/26
5570	Wall Sheathing	1	05/13/26	05/13/26
5575	Floor Joists	3	05/14/26	05/18/26
5580	Floor Decking	1	05/19/26	05/19/26
Inspections				
5585	STRUCTURAL	1	05/20/26	05/20/26
MEPF				
5590	Plumbing R/I	4	12/14/26	12/17/26
5595	Fire Sprinkler	4	12/21/26	12/24/26
5600	Electrical R/I	4	12/24/26	12/30/26

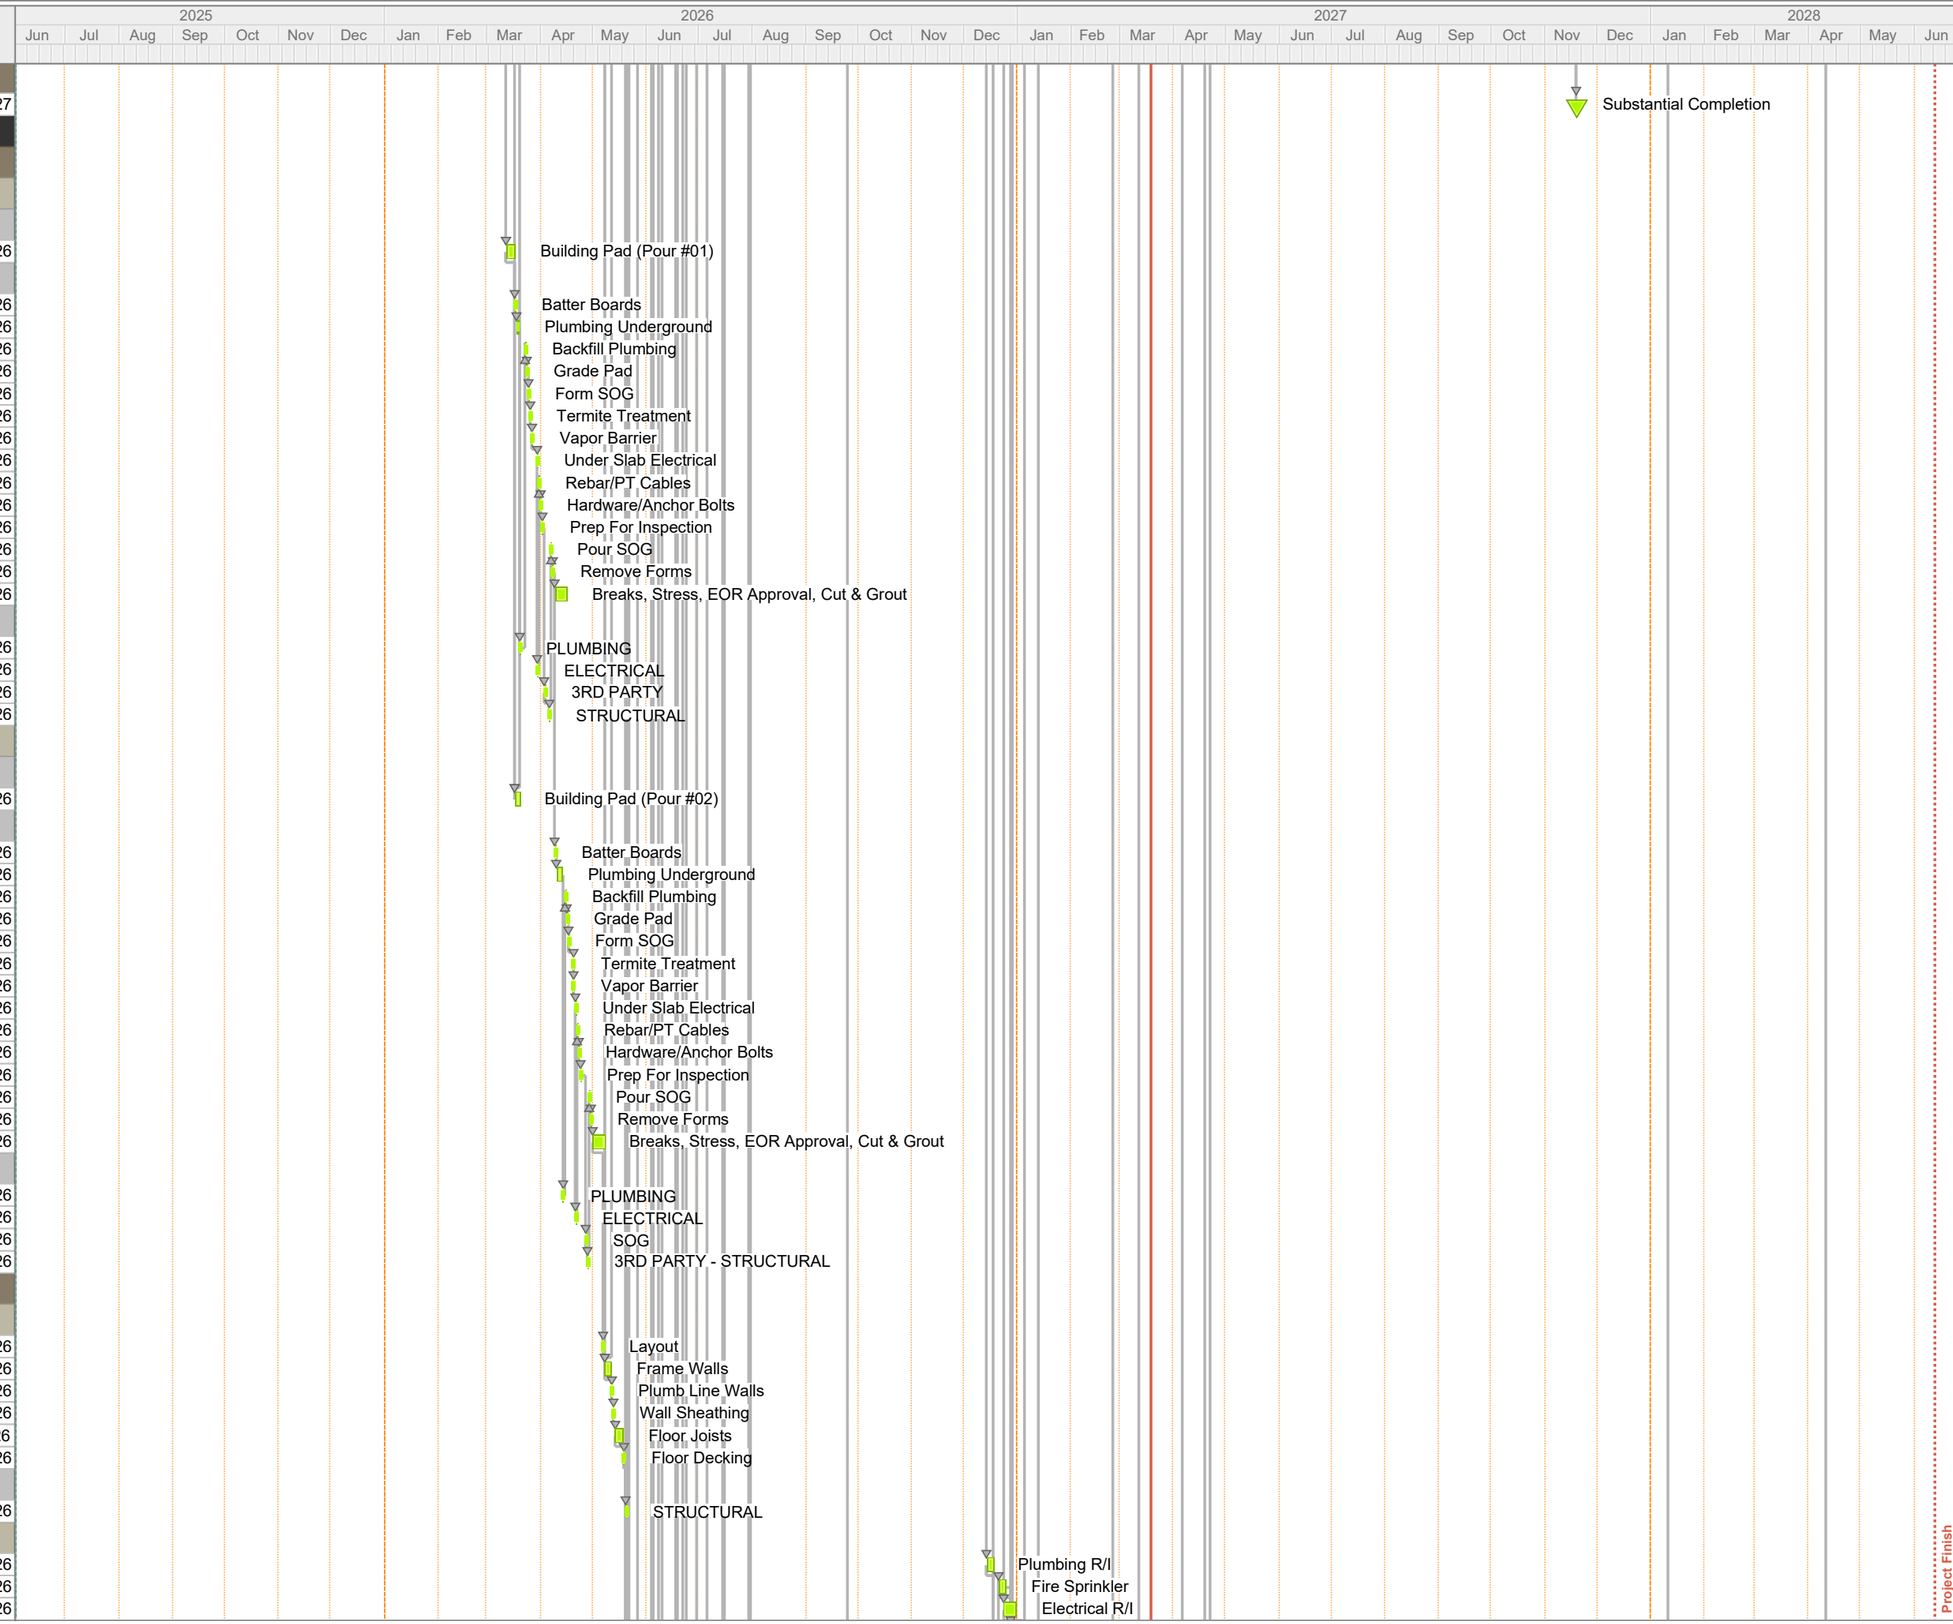

Initials: _____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

5605	Mechanical R/I	4	12/28/26	12/31/26
5610	Low Votltage RI	4	12/29/26	01/04/27
5615	MEP 1st Trim	3	02/03/27	02/05/27
5620	Hot Punch	2	02/08/27	02/09/27
5625	HVAC Startup	3	02/10/27	02/12/27
5630	MEP 2nd Trim	2	02/22/27	02/23/27
5635	Low Voltage Trim Out	2	02/22/27	02/23/27
Inspections				
5640	PLUMBING	1	12/18/26	12/18/26
5645	PIPE SIZE & HANGER	1	12/28/26	12/28/26
5650	FIRE SPRINKLER HYDRO	1	12/29/26	12/29/26
5655	MECHANICAL	1	01/04/27	01/04/27
5660	ELECTRICAL	1	01/05/27	01/05/27
Buildout				
5665	Pre-Rock	1	01/07/27	01/07/27
5670	Gypcrete Pre-Pour (Tub & Shower)	1	01/08/27	01/08/27
5675	Insulation	1	01/11/27	01/11/27
5680	Drywall	4	01/13/27	01/18/27
5685	Tub/Shower Pans	1	01/19/27	01/19/27
5690	Gypcrete	1	01/19/27	01/19/27
5695	Tape/Float/Sand Walls & Ceilings	6	01/20/27	01/27/27
5700	Spray Texture	2	01/27/27	01/28/27
5705	Doors & Trim	2	01/28/27	01/29/27
5710	Prime & 1st Coat Paint	2	02/01/27	02/02/27
5715	Tub/Shower Wall Tile	4	02/03/27	02/08/27
5720	Bathroom Floor Tile	4	02/10/27	02/15/27
5725	Shower Doors & Mirrors	2	02/16/27	02/17/27
5730	Toilet Accessories	1	02/18/27	02/18/27
5735	Cabinets	3	02/03/27	02/05/27
5740	Countertops	2	02/08/27	02/09/27
5745	Drywall Touch Up	1	02/10/27	02/10/27
5750	Tile Backsplash	4	02/16/27	02/19/27
5755	LVT	5	03/19/27	03/25/27
5760	Shoe/Scribe Molding	2	03/26/27	03/29/27
5765	Rough Clean	1	03/30/27	03/30/27
5770	Completion List	1	03/31/27	03/31/27
5775	Appliances	1	04/01/27	04/01/27
5780	Blinds	1	04/02/27	04/02/27
5785	Final Paint	1	04/05/27	04/05/27
Inspections				
5790	STRUCTURAL	1	01/06/27	01/06/27
5795	INSULATION	1	01/12/27	01/12/27
Interior Punch List				
5800	Arch-Con Punch List	2	04/06/27	04/07/27
5805	Arch-Con Punch List Corrections	2	04/08/27	04/09/27
5810	Final Clean	1	04/12/27	04/12/27
5815	Owner Punch List	2	04/19/27	04/20/27
5820	Punch List Corrections	2	04/21/27	04/22/27
5825	Powder Puff	1	04/23/27	04/23/27
5830	Owner Acceptance	1	04/26/27	04/26/27
Lvl. 2				
Wood Framing				
5835	Layout	1	05/20/26	05/20/26
5840	Frame Walls	2	05/22/26	05/26/26
5845	Plumb Line Walls	1	05/27/26	05/27/26
5850	Wall Sheathing	1	05/28/26	05/28/26
5855	Floor joists	3	05/29/26	06/02/26
5860	Floor Decking	1	06/03/26	06/03/26
Inspections				
5865	STRUCTURAL	1	06/04/26	06/04/26
MEPF				
5870	Plumbing R/I	4	12/21/26	12/24/26
5875	Fire Sprinkler	4	12/29/26	01/04/27
5880	Electrical R/I	4	01/04/27	01/07/27
5885	Mechanical R/I	4	01/05/27	01/08/27
5890	Low Votltage RI	4	01/06/27	01/11/27
5895	MEP 1st Trim	3	02/10/27	02/12/27

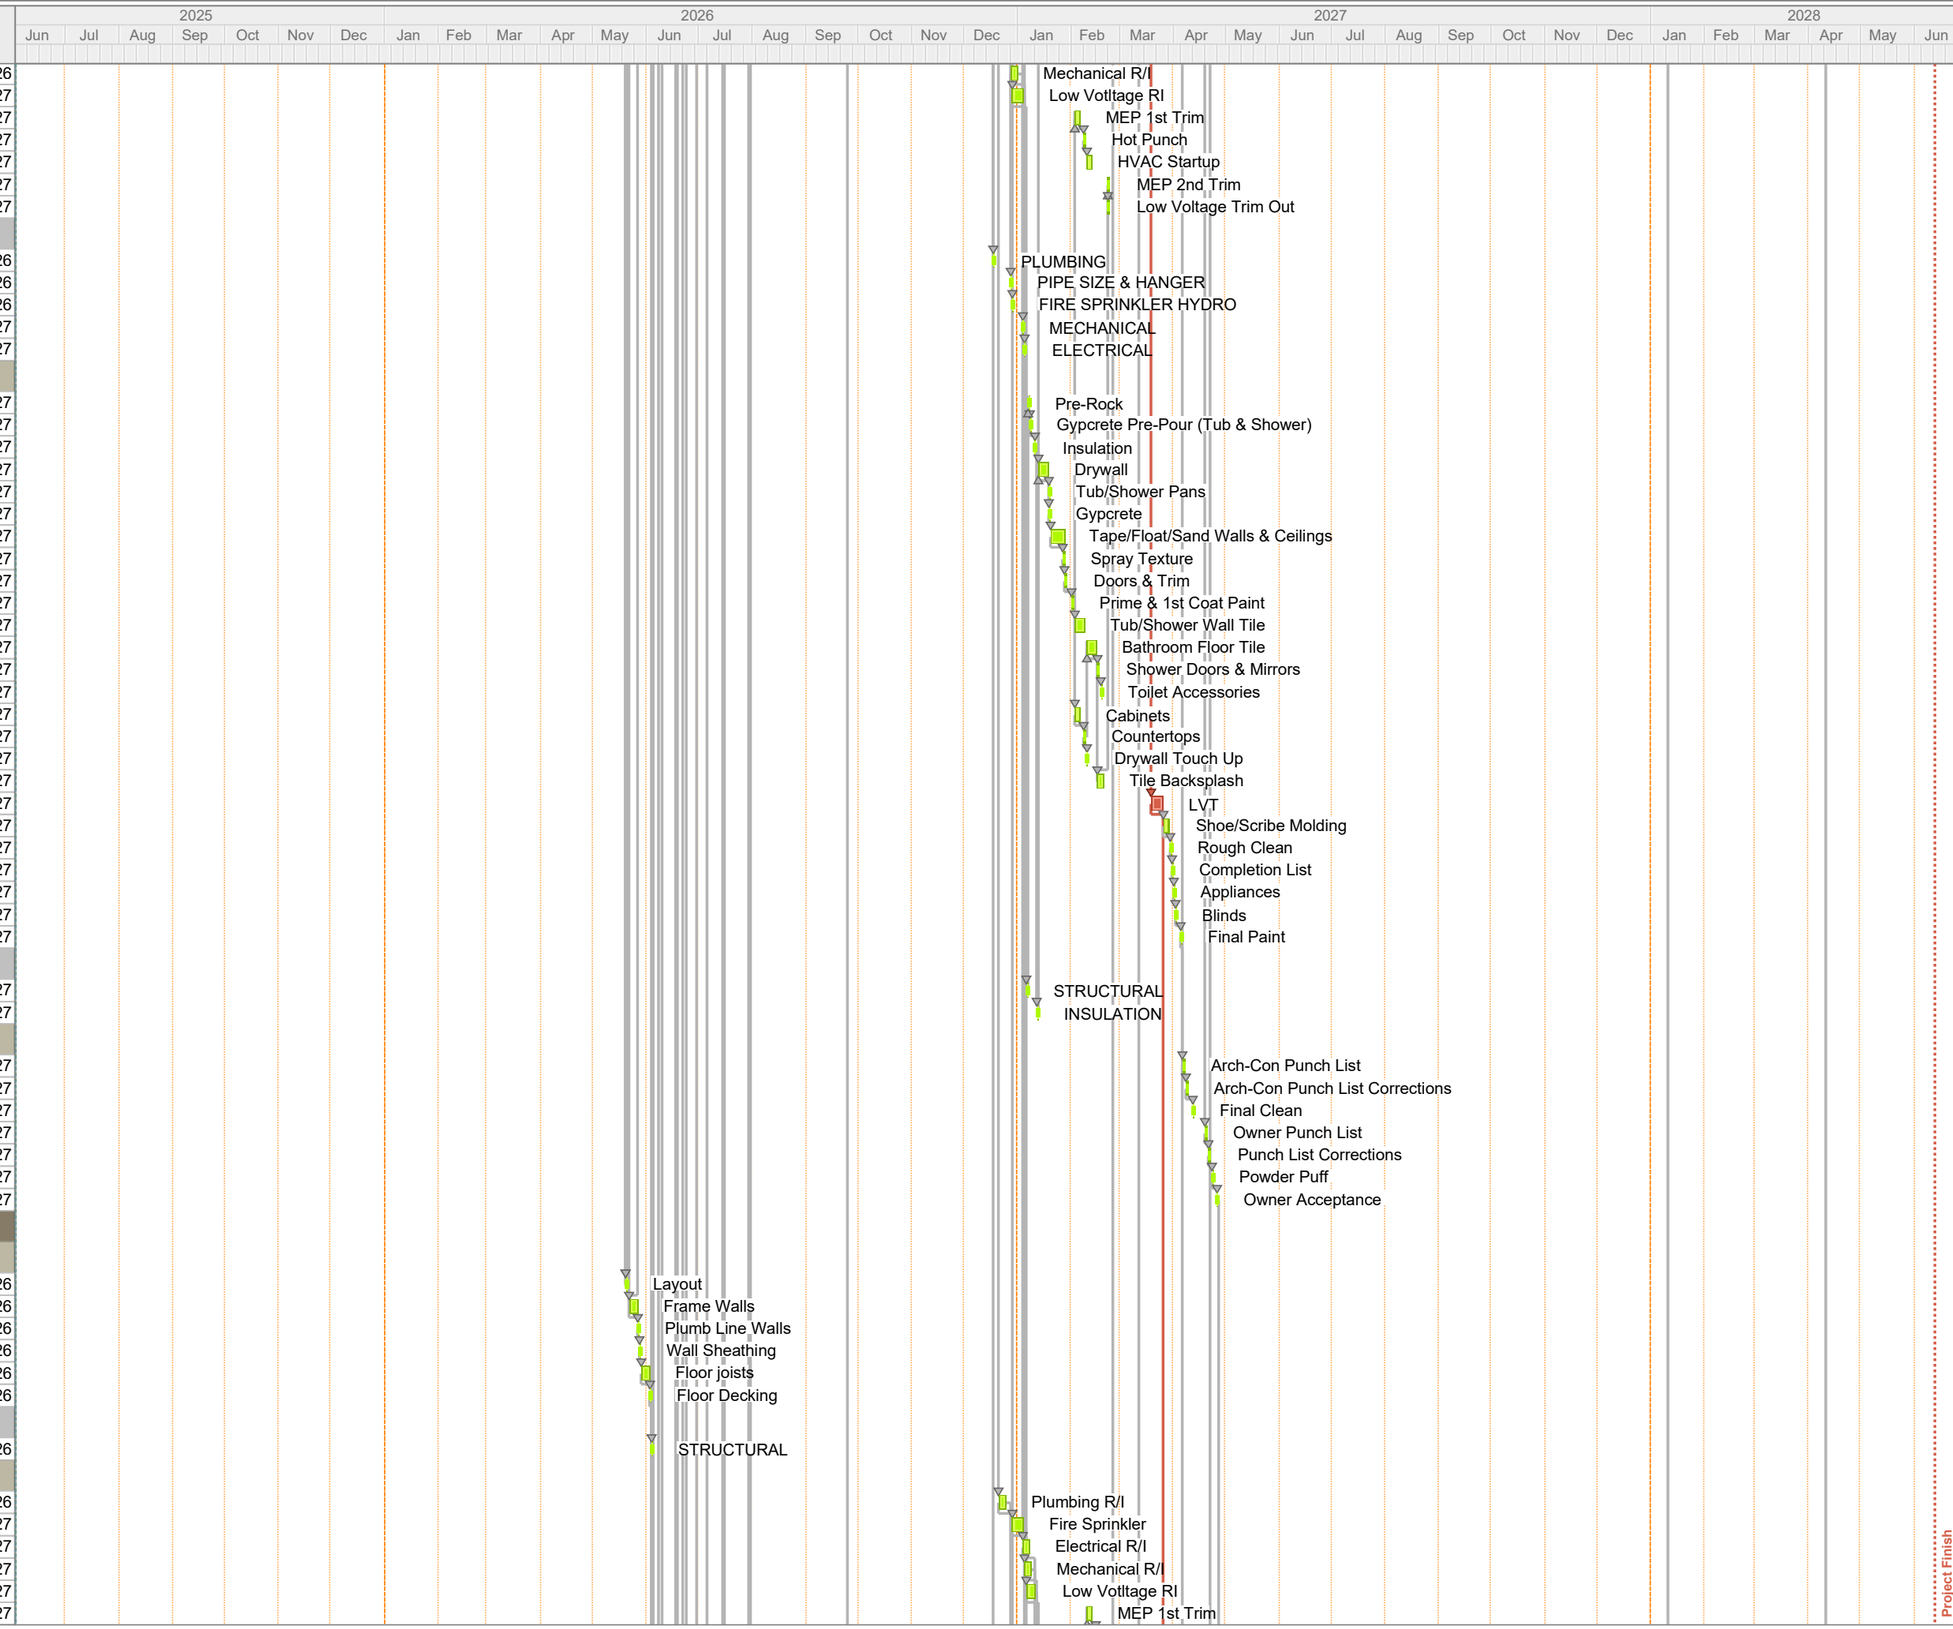

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

5900	Hot Punch	2	02/15/27	02/16/27
5905	HVAC Startup	3	02/17/27	02/19/27
5910	MEP 2nd Trim	2	03/01/27	03/02/27
5915	Low Voltage Trim Out	2	03/01/27	03/02/27
Inspections				
5920	PLUMBING	1	12/28/26	12/28/26
5925	PIPE SIZE & HANGER	1	01/05/27	01/05/27
5930	FIRE SPRINKLER HYDRO	1	01/06/27	01/06/27
5935	MECHANICAL	1	01/11/27	01/11/27
5940	ELECTRICAL	1	01/12/27	01/12/27
Buildout				
5945	Pre-Rock	1	01/14/27	01/14/27
5950	Gypcrete Pre-Pour (Tub & Shower)	1	01/15/27	01/15/27
5955	Insulation	1	01/18/27	01/18/27
5960	Drywall	4	01/20/27	01/25/27
5965	Tub/Shower Pans	1	01/26/27	01/26/27
5970	Gypcrete	1	01/26/27	01/26/27
5975	Tape/Float/Sand Walls & Ceilings	6	01/27/27	02/03/27
5980	Spray Texture	2	02/03/27	02/04/27
5985	Doors & Trim	2	02/04/27	02/05/27
5990	Prime & 1st Coat Paint	2	02/08/27	02/09/27
5995	Tub/Shower Wall Tile	4	02/10/27	02/15/27
6000	Bathroom Floor Tile	4	02/17/27	02/22/27
6005	Shower Doors & Mirrors	2	02/23/27	02/24/27
6010	Toilet Accessories	1	02/25/27	02/25/27
6015	Cabinets	3	02/10/27	02/12/27
6020	Countertops	2	02/15/27	02/16/27
6025	Drywall Touch Up	1	02/17/27	02/17/27
6030	Tile Backsplash	4	02/23/27	02/26/27
6035	LVT	5	03/26/27	04/01/27
6040	Shoe/Scribe Molding	2	04/02/27	04/05/27
6045	Rough Clean	1	04/06/27	04/06/27
6050	Completion List	1	04/07/27	04/07/27
6055	Appliances	1	04/08/27	04/08/27
6060	Blinds	1	04/09/27	04/09/27
6065	Final Paint	1	04/12/27	04/12/27
Inspections				
6070	STRUCTURAL	1	01/13/27	01/13/27
6075	INSULATION	1	01/19/27	01/19/27
Interior Punch List				
6080	Arch-Con Punch List	2	04/13/27	04/14/27
6085	Arch-Con Punch List Corrections	2	04/15/27	04/16/27
6090	Final Clean	1	04/19/27	04/19/27
6095	Owner Punch List	2	04/27/27	04/28/27
6100	Punch List Corrections	2	04/29/27	04/30/27
6105	Powder Puff	1	05/03/27	05/03/27
6110	Owner Acceptance	1	05/04/27	05/04/27
Lvl. 3				
Wood Framing				
6115	Layout	1	06/04/26	06/04/26
6120	Frame Walls	2	06/08/26	06/09/26
6125	Plumb Line Walls	1	06/10/26	06/10/26
6130	Wall Sheathing	1	06/11/26	06/11/26
6135	Floor Joists	3	06/12/26	06/16/26
6140	Floor Decking	1	06/17/26	06/17/26
Inspections				
6145	STRUCTURAL	1	06/18/26	06/18/26
MEPF				
6150	Plumbing R/I	4	12/29/26	01/04/27
6155	Fire Sprinkler	4	01/06/27	01/11/27
6160	Electrical R/I	4	01/11/27	01/14/27
6165	Mechanical R/I	4	01/12/27	01/15/27
6170	Low Votltage RI	4	01/13/27	01/18/27
6175	MEP 1st Trim	3	02/17/27	02/19/27
6180	Hot Punch	2	02/22/27	02/23/27
6185	HVAC Startup	3	02/24/27	02/26/27
6190	MEP 2nd Trim	2	03/08/27	03/09/27

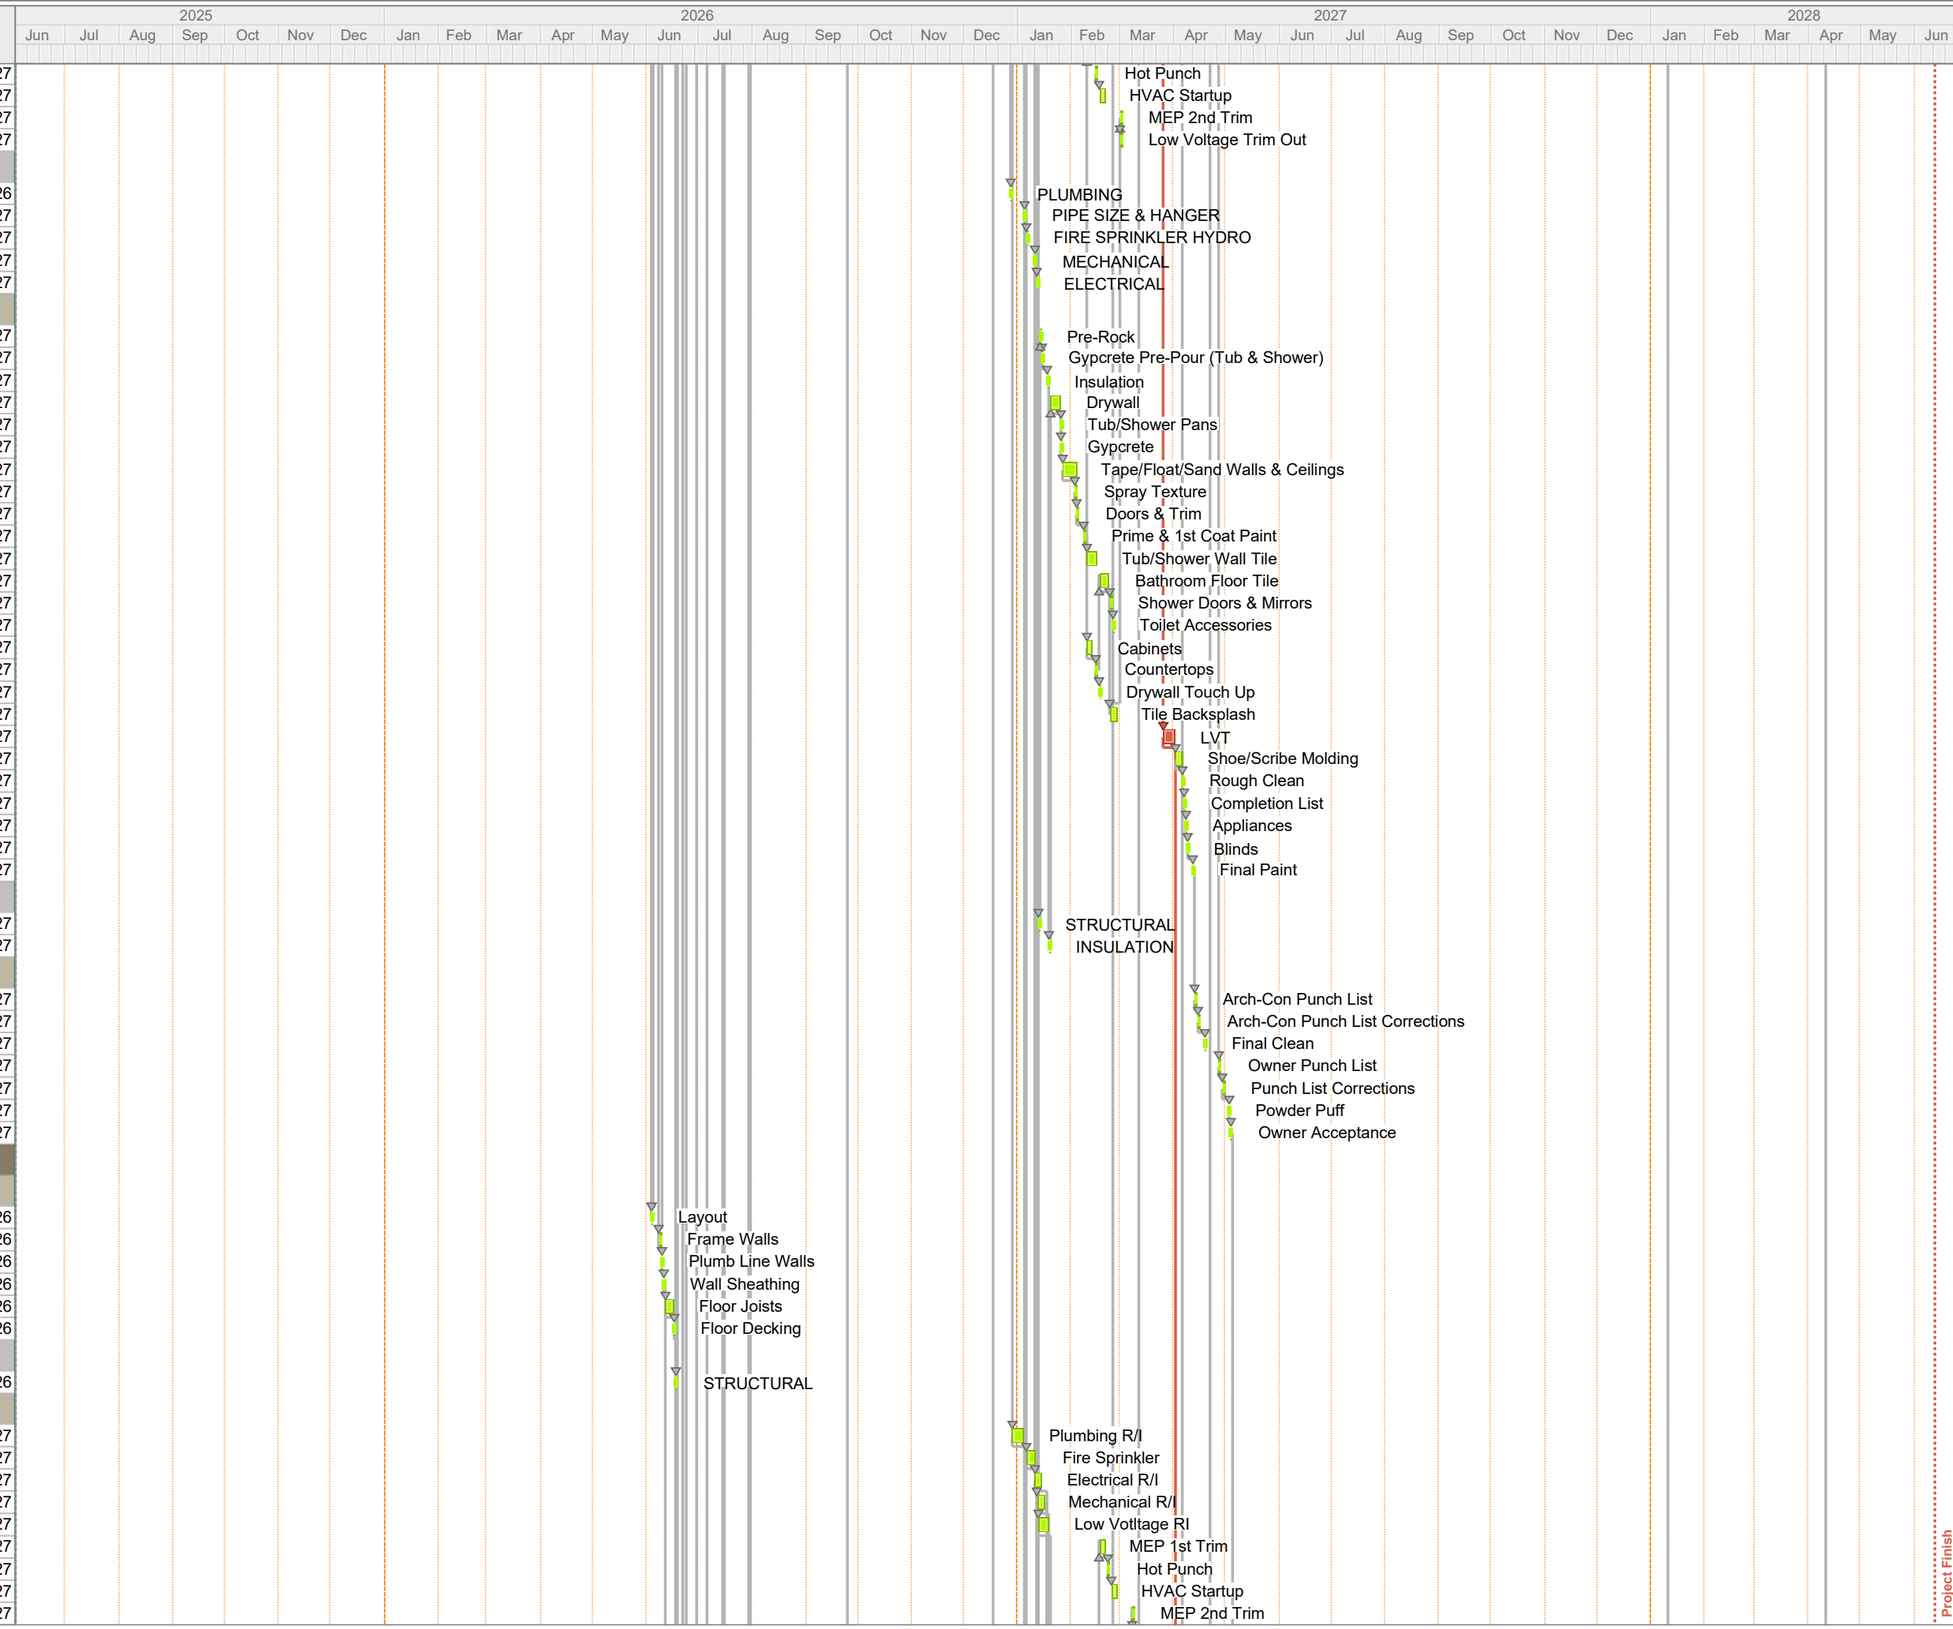

Initials: _____

6195	Low Voltage Trim Out	2	03/08/27	03/09/27
Inspections				
6200	PLUMBING	1	01/05/27	01/05/27
6205	PIPE SIZE & HANGER	1	01/12/27	01/12/27
6210	FIRE SPRINKLER HYDRO	1	01/13/27	01/13/27
6215	MECHANICAL	1	01/18/27	01/18/27
6220	ELECTRICAL	1	01/19/27	01/19/27
Buildout				
6225	Pre-Rock	1	01/21/27	01/21/27
6230	Gypcrete Pre-Pour (Tub & Shower)	1	01/22/27	01/22/27
6235	Insulation	1	01/25/27	01/25/27
6240	Drywall	4	01/27/27	02/01/27
6245	Tub/Shower Pans	1	02/02/27	02/02/27
6250	Gypcrete	1	02/02/27	02/02/27
6255	Tape/Float/Sand Walls & Ceilings	6	02/03/27	02/10/27
6260	Spray Texture	2	02/10/27	02/11/27
6265	Doors & Trim	2	02/12/27	02/15/27
6270	Prime & 1st Coat Paint	1	02/16/27	02/16/27
6275	Tub/Shower Wall Tile	4	02/17/27	02/22/27
6280	Bathroom Floor Tile	4	02/24/27	03/01/27
6285	Shower Doors & Mirrors	2	03/02/27	03/03/27
6290	Toilet Accessories	1	03/04/27	03/04/27
6295	Cabinets	3	02/17/27	02/19/27
6300	Countertops	2	02/22/27	02/23/27
6305	Drywall Touch Up	1	02/24/27	02/24/27
6310	Tile Backsplash	4	03/02/27	03/05/27
6315	LVT	5	04/02/27	04/08/27
6320	Shoe/Scribe Molding	2	04/09/27	04/12/27
6325	Rough Clean	1	04/13/27	04/13/27
6330	Completion List	1	04/14/27	04/14/27
6335	Appliances	1	04/15/27	04/15/27
6340	Blinds	1	04/16/27	04/16/27
6345	Final Paint	1	04/19/27	04/19/27
Inspections				
6350	STRUCTURAL	1	01/20/27	01/20/27
6355	INSULATION	1	01/26/27	01/26/27
Interior Punch List				
6360	Arch-Con Punch List	2	04/20/27	04/21/27
6365	Arch-Con Punch List Corrections	2	04/22/27	04/23/27
6370	Final Clean	1	04/26/27	04/26/27
6375	Owner Punch List	2	05/05/27	05/06/27
6380	Punch List Corrections	2	05/07/27	05/10/27
6385	Powder Puff	1	05/11/27	05/11/27
6390	Owner Acceptance	1	05/12/27	05/12/27
Lvl. 4				
Wood Framing				
6395	Layout	1	06/18/26	06/18/26
6400	Frame Walls	2	06/22/26	06/23/26
6405	Plumb Line Walls	1	06/24/26	06/24/26
6410	Wall Sheathing	1	06/25/26	06/25/26
6415	Floor Joists	3	06/26/26	06/30/26
6420	Floor Decking	1	07/01/26	07/01/26
Inspections				
6425	STRUCTURAL	1	07/02/26	07/02/26
MEPF				
6430	Plumbing R/I	4	01/06/27	01/11/27
6435	Fire Sprinkler	4	01/13/27	01/18/27
6440	Electrical R/I	4	01/18/27	01/21/27
6445	Mechanical R/I	4	01/19/27	01/22/27
6450	Low Votltage RI	4	01/20/27	01/25/27
6455	MEP 1st Trim	3	02/24/27	02/26/27
6460	Hot Punch	2	03/01/27	03/02/27
6465	HVAC Startup	3	03/03/27	03/05/27
6470	MEP 2nd Trim	2	03/15/27	03/16/27
6475	Low Voltage Trim Out	2	03/15/27	03/16/27

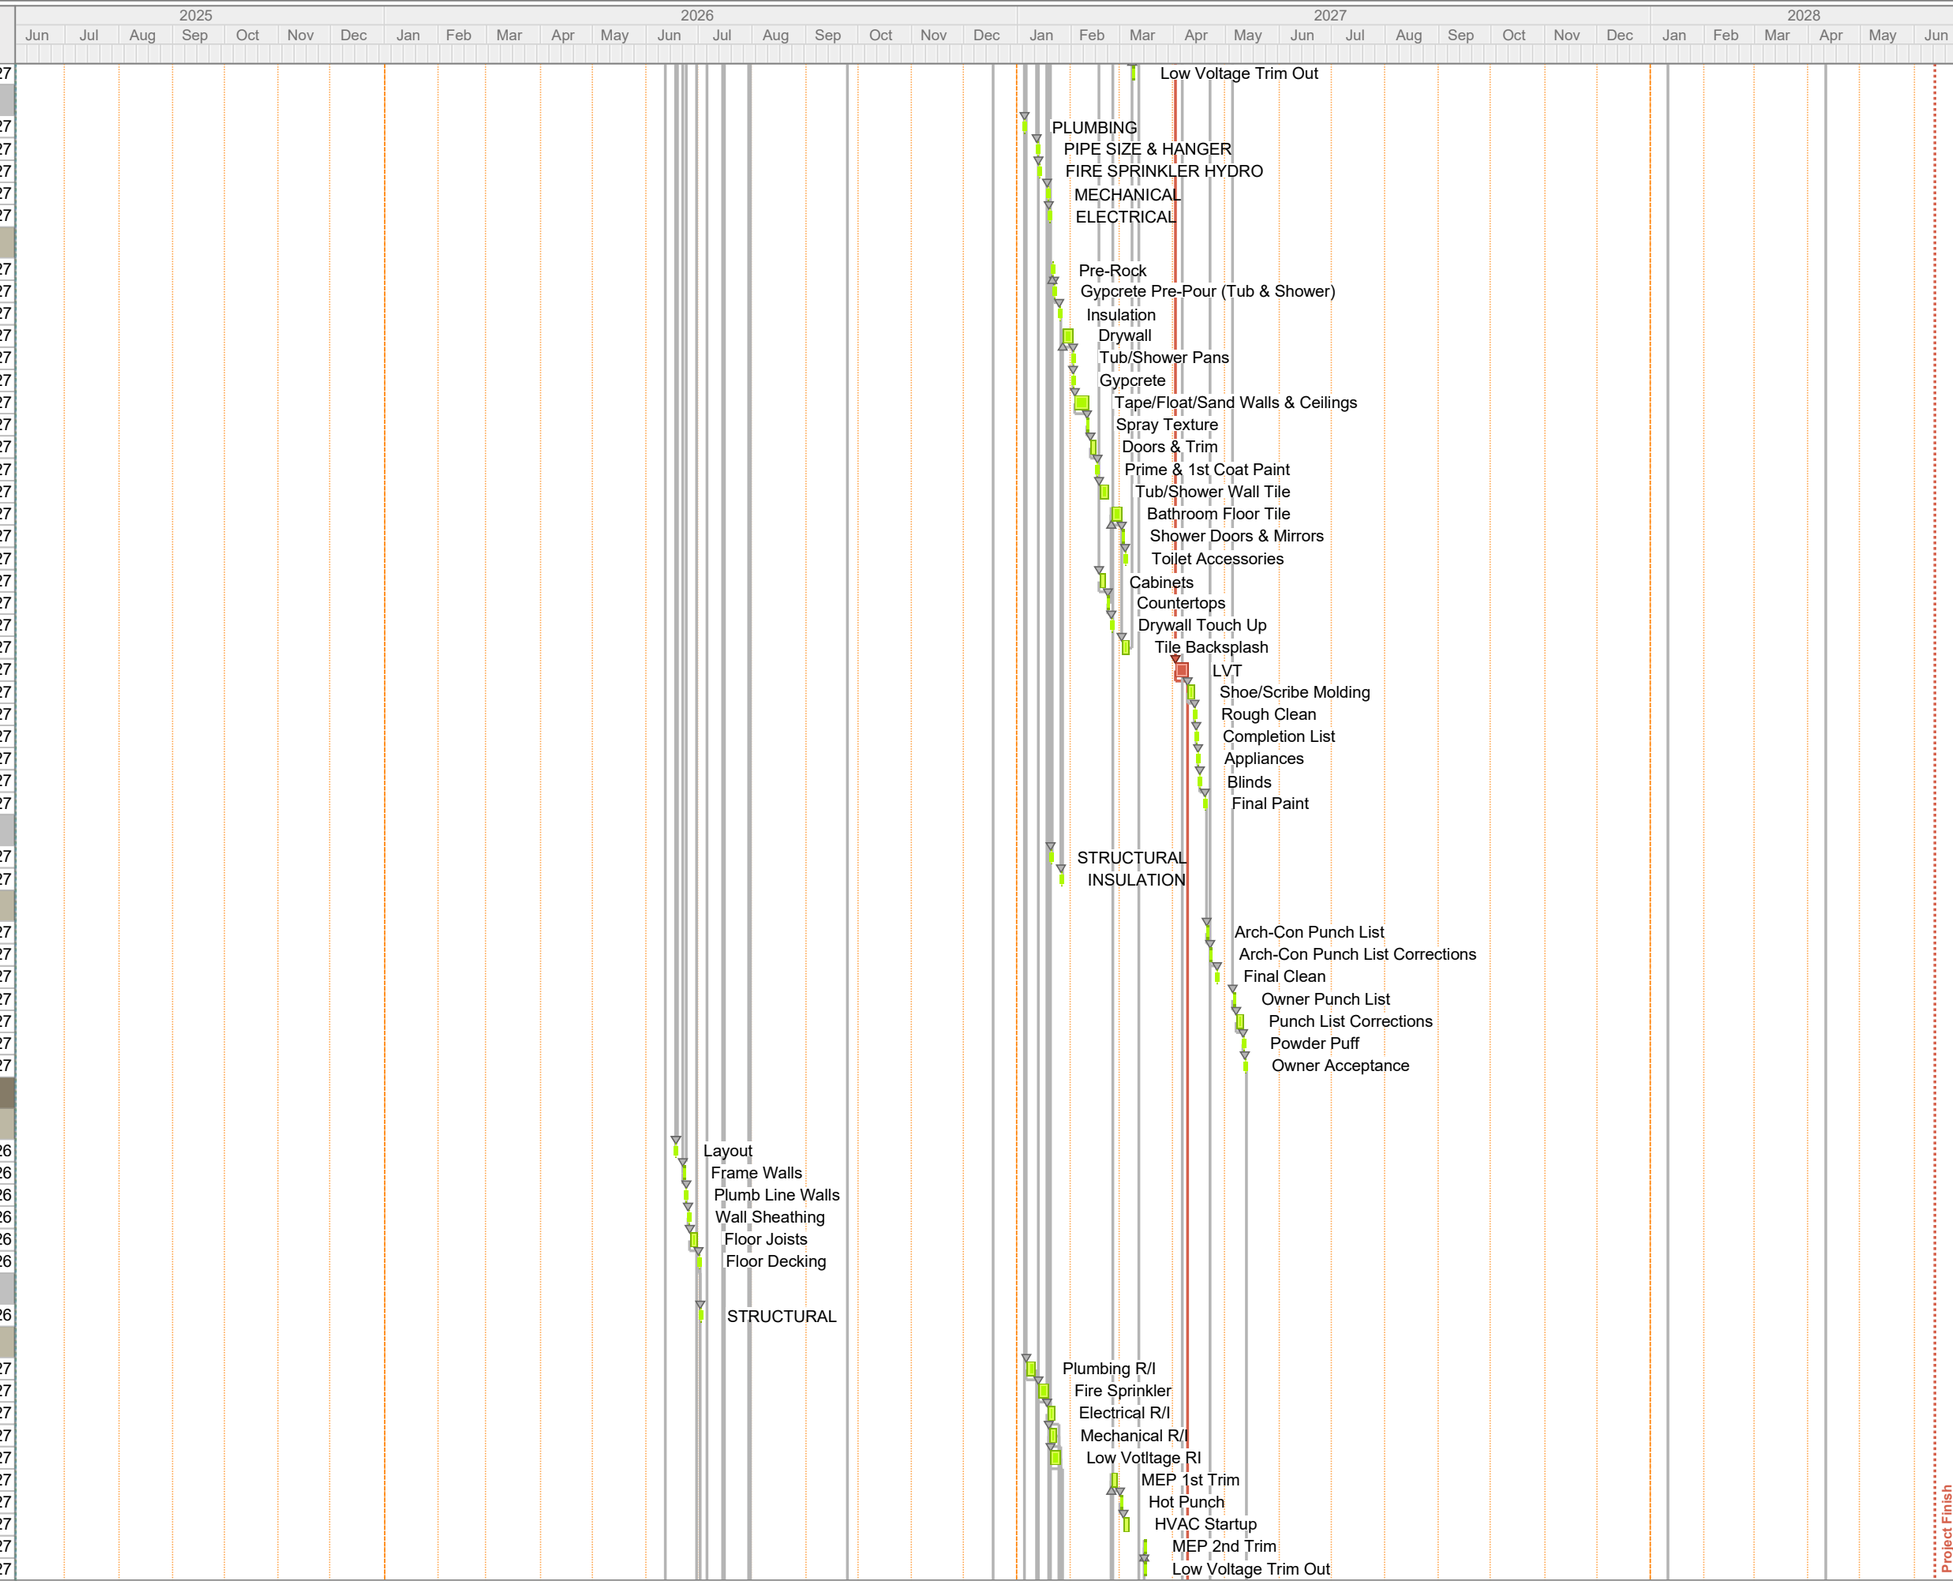

Inspections				
6480	PLUMBING	1	01/12/27	01/12/27
6485	PIPE SIZE & HANGER	1	01/19/27	01/19/27
6490	FIRE SPRINKLER HYDRO	1	01/20/27	01/20/27
6495	MECHANICAL	1	01/25/27	01/25/27
6500	ELECTRICAL	1	01/26/27	01/26/27
Buildout				
6505	Pre-Rock	1	01/28/27	01/28/27
6510	Gypcrete Pre-Pour (Tub & Shower)	1	01/29/27	01/29/27
6515	Insulation	1	02/01/27	02/01/27
6520	Drywall	4	02/03/27	02/08/27
6525	Tub/Shower Pans	1	02/09/27	02/09/27
6530	Gypcrete	1	02/09/27	02/09/27
6535	Tape/Float/Sand Walls & Ceilings	6	02/10/27	02/17/27
6540	Spray Texture	2	02/17/27	02/18/27
6545	Doors & Trim	2	02/19/27	02/22/27
6550	Prime & 1st Coat Paint	1	02/23/27	02/23/27
6555	Tub/Shower Wall Tile	4	02/24/27	03/01/27
6560	Bathroom Floor Tile	4	03/03/27	03/08/27
6565	Shower Doors & Mirrors	2	03/09/27	03/10/27
6570	Toilet Accessories	1	03/11/27	03/11/27
6575	Cabinets	3	02/24/27	02/26/27
6580	Countertops	2	03/01/27	03/02/27
6585	Drywall Touch Up	1	03/03/27	03/03/27
6590	Tile Backsplash	4	03/09/27	03/12/27
6595	LVT	5	04/09/27	04/15/27
6600	Shoe/Scribe Molding	2	04/16/27	04/19/27
6605	Rough Clean	1	04/20/27	04/20/27
6610	Completion List	1	04/21/27	04/21/27
6615	Appliances	1	04/22/27	04/22/27
6620	Blinds	1	04/23/27	04/23/27
6625	Final Paint	1	04/26/27	04/26/27
Inspections				
6630	STRUCTURAL	1	01/27/27	01/27/27
6635	INSULATION	1	02/02/27	02/02/27
Interior Punch List				
6640	Arch-Con Punch List	2	04/27/27	04/28/27
6645	Arch-Con Punch List Corrections	2	04/29/27	04/30/27
6650	Final Clean	1	05/03/27	05/03/27
6655	Owner Punch List	2	05/13/27	05/14/27
6660	Punch List Corrections	2	05/17/27	05/18/27
6665	Powder Puff	1	05/19/27	05/19/27
6670	Owner Acceptance	1	05/20/27	05/20/27
Lvl. 5				
Wood Framing				
6675	Layout	1	07/02/26	07/02/26
6680	Frame Walls	2	07/06/26	07/07/26
6685	Plumb Line Walls	1	07/08/26	07/08/26
6690	Wall Sheathing	1	07/09/26	07/09/26
6695	Roof Joists	3	07/10/26	07/14/26
6700	Roof Decking	1	07/15/26	07/15/26
Inspections				
6705	STRUCTURAL	1	07/16/26	07/16/26
MEPF				
6710	Plumbing R/I	4	01/13/27	01/18/27
6715	Fire Sprinkler	4	01/20/27	01/25/27
6720	Electrical R/I	4	01/25/27	01/28/27
6725	Mechanical R/I	4	01/26/27	01/29/27
6730	Low Votltage RI	4	01/27/27	02/01/27
6735	MEP 1st Trim	3	03/02/27	03/04/27
6740	Hot Punch	2	03/05/27	03/08/27
6745	HVAC Startup	3	03/09/27	03/11/27
6750	MEP 2nd Trim	2	03/19/27	03/22/27
6755	Low Voltage Trim Out	2	03/23/27	03/24/27
Inspections				
6760	PLUMBING	1	01/19/27	01/19/27

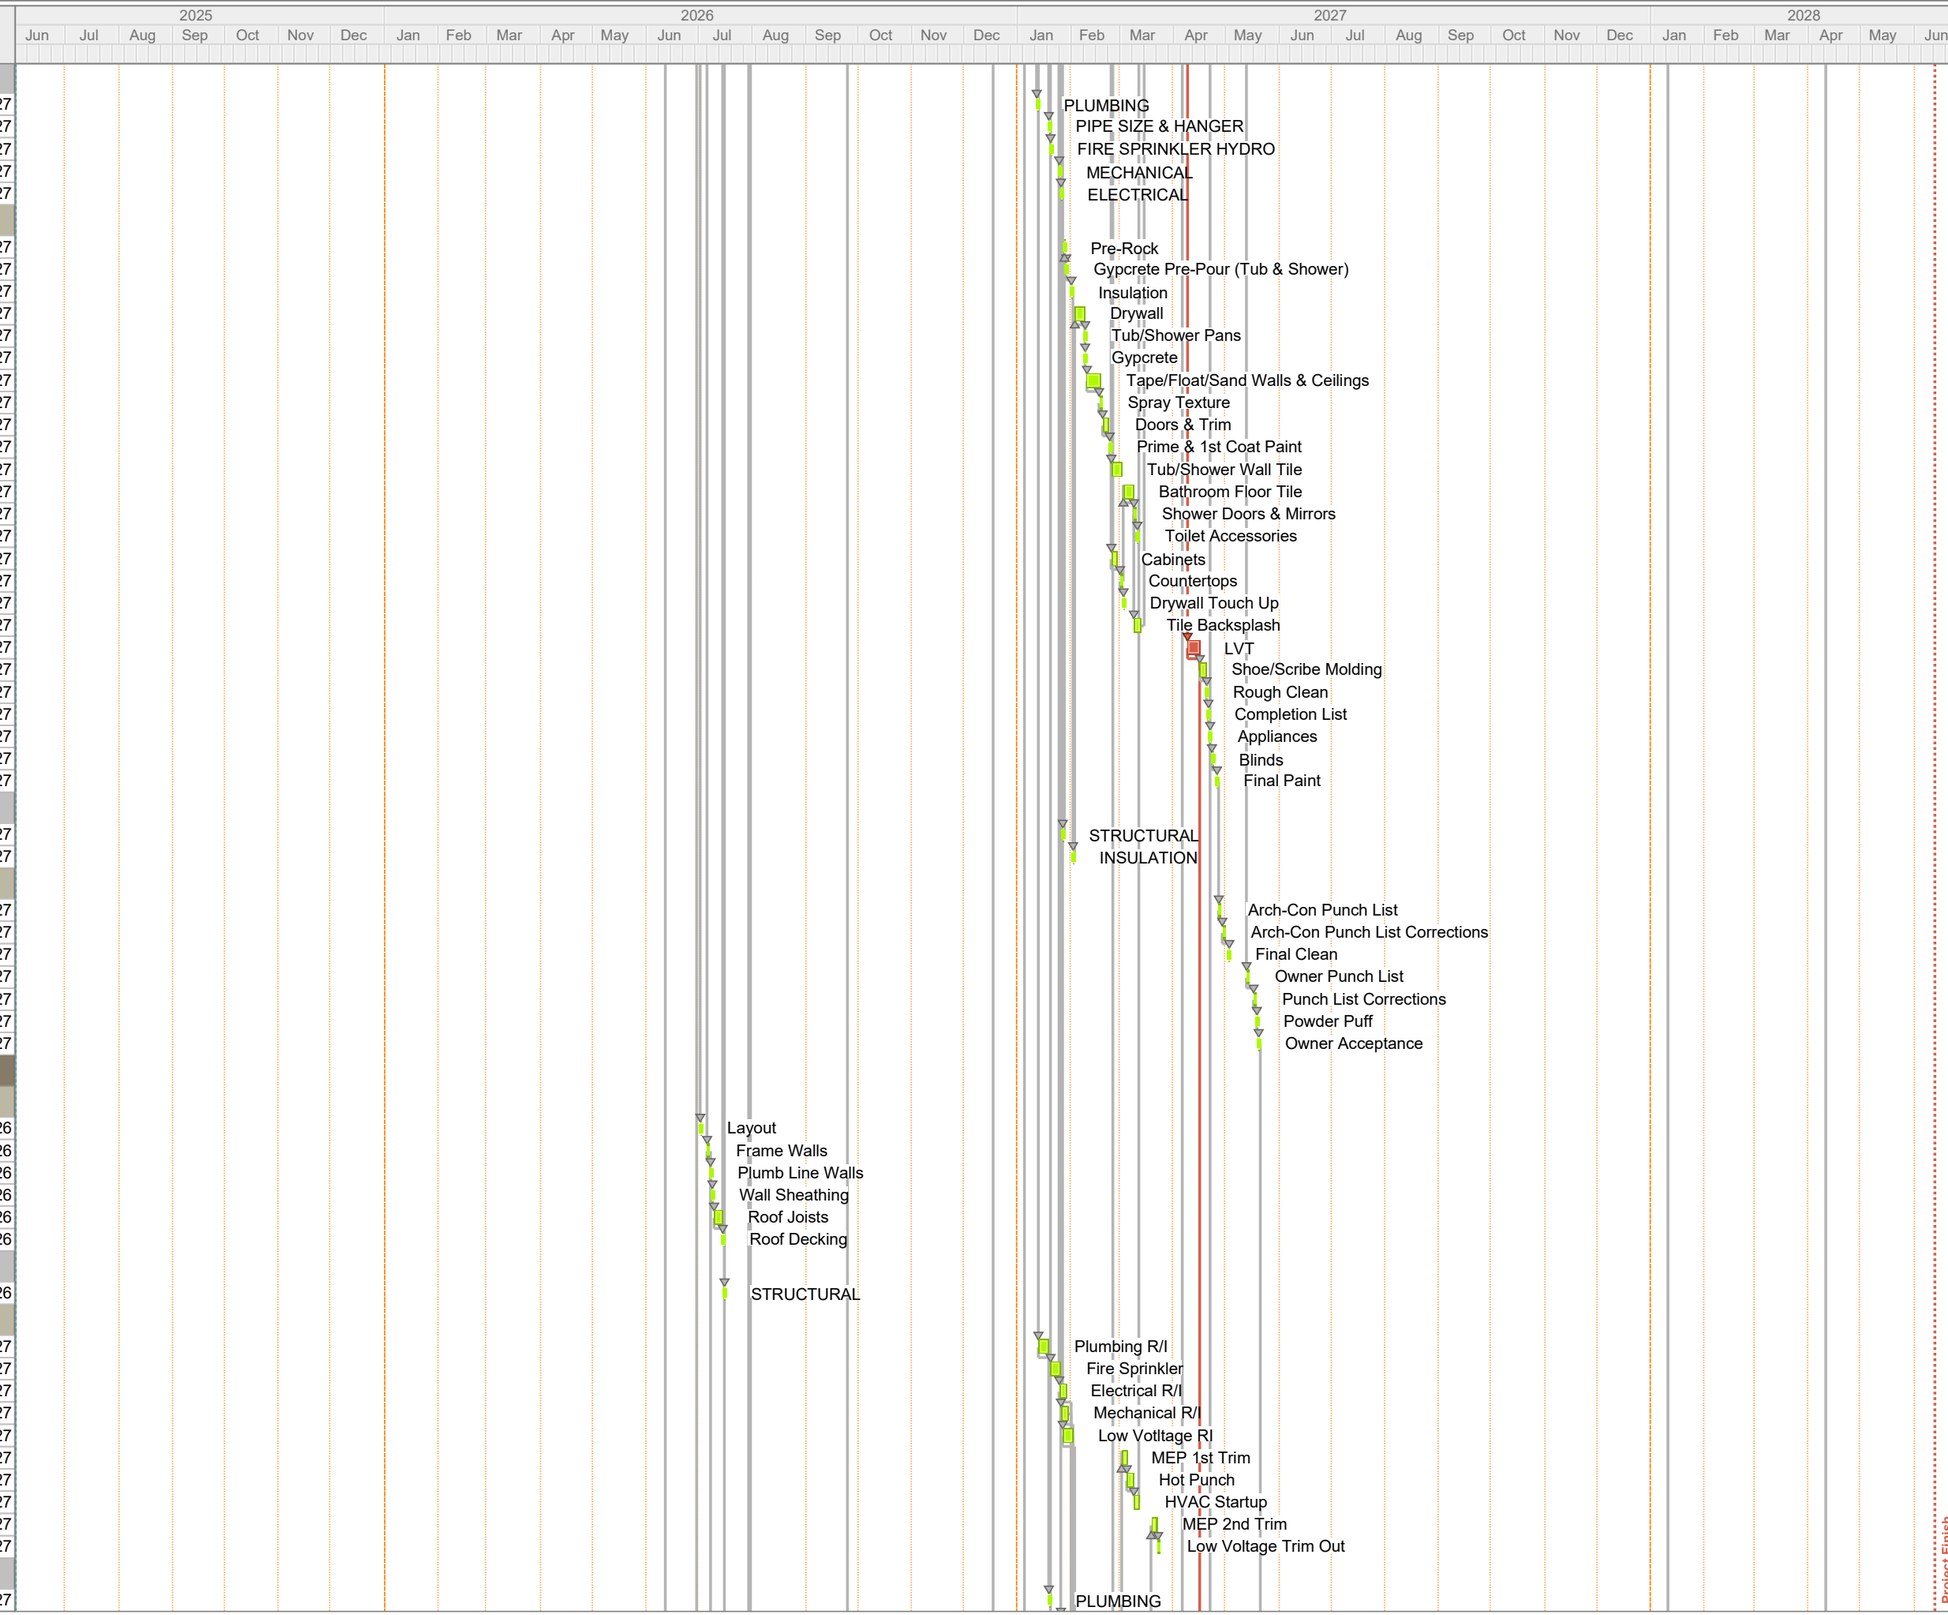

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

6765	PIPE SIZE & HANGER	1	01/25/27	01/25/27
6770	FIRE SPRINKLER HYDRO	1	01/26/27	01/26/27
6775	MECHANICAL	1	02/01/27	02/01/27
6780	ELECTRICAL	1	02/02/27	02/02/27
Buildout				
6785	Pre-Rock	1	02/04/27	02/04/27
6790	Gypcrete Pre-Pour (Tub & Shower)	1	02/05/27	02/05/27
6795	Insulation	1	02/08/27	02/08/27
6800	Drywall	4	02/10/27	02/15/27
6805	Tub/Shower Pans	1	02/16/27	02/16/27
6810	Gypcrete	1	02/16/27	02/16/27
6815	Tape/Float/Sand Walls & Ceilings	6	02/17/27	02/24/27
6820	Spray Texture	2	02/24/27	02/25/27
6825	Doors & Trim	2	02/25/27	02/26/27
6830	Prime & 1st Coat Paint	1	03/01/27	03/01/27
6835	Tub/Shower Wall Tile	4	03/02/27	03/05/27
6840	Bathroom Floor Tile	4	03/09/27	03/12/27
6845	Shower Doors & Mirrors	2	03/15/27	03/16/27
6850	Toilet Accessories	1	03/17/27	03/17/27
6855	Cabinets	3	03/02/27	03/04/27
6860	Countertops	2	03/05/27	03/08/27
6865	Drywall Touch Up	1	03/09/27	03/09/27
6870	Tile Backsplash	4	03/15/27	03/18/27
6875	LVT	5	04/16/27	04/22/27
6880	Shoe/Scribe Molding	2	04/23/27	04/26/27
6885	Rough Clean	1	04/27/27	04/27/27
6890	Completion List	1	04/28/27	04/28/27
6895	Appliances	1	04/29/27	04/29/27
6900	Blinds	1	04/30/27	04/30/27
6905	Final Paint	1	05/03/27	05/03/27
Inspections				
6910	STRUCTURAL	1	02/03/27	02/03/27
6915	INSULATION	1	02/09/27	02/09/27
Interior Punch List				
6920	Arch-Con Punch List	2	05/04/27	05/05/27
6925	Arch-Con Punch List Corrections	2	05/06/27	05/07/27
6930	Final Clean	1	05/10/27	05/10/27
6935	Owner Punch List	2	05/21/27	05/24/27
6940	Punch List Corrections	2	05/25/27	05/26/27
6945	Powder Puff	1	05/27/27	05/27/27
6950	Owner Acceptance	1	05/28/27	05/28/27
Building Exterior				
Roof				
6955	TPO Roofing	10	07/16/26	07/29/26
North Elevation				
6960	Windows	10	06/12/26	06/25/26
6965	Waterproofing	10	06/17/26	06/30/26
6970	Exterior Storefront	10	06/24/26	07/07/26
6975	Storefront Glass	10	06/24/26	07/07/26
6980	Masonry/Brick	10	07/06/26	07/17/26
6985	Hardi & Trim	10	07/16/26	07/29/26
6990	Paint Prep (Caulk, Prime, 1st Coat)	10	07/28/26	08/10/26
6995	Final Paint	10	08/07/26	08/20/26
East Elevation (Right)				
7000	Windows	10	06/26/26	07/09/26
7005	Waterproofing	10	07/01/26	07/14/26
7010	Exterior Storefront	10	07/08/26	07/21/26
7015	Storefront Glass	10	07/08/26	07/21/26
7020	Masonry/Brick	10	07/20/26	07/31/26
7025	Hardi & Trim	10	07/30/26	08/12/26
7030	Paint Prep (Caulk, Prime, 1st Coat)	10	08/11/26	08/24/26
7035	Final Paint	10	08/21/26	09/03/26
South Elevation (Right)				
7040	Windows	10	07/10/26	07/23/26
7045	Waterproofing	10	07/15/26	07/28/26
7050	Exterior Storefront	10	07/27/26	08/07/26
7055	Storefront Glass	10	07/27/26	08/07/26

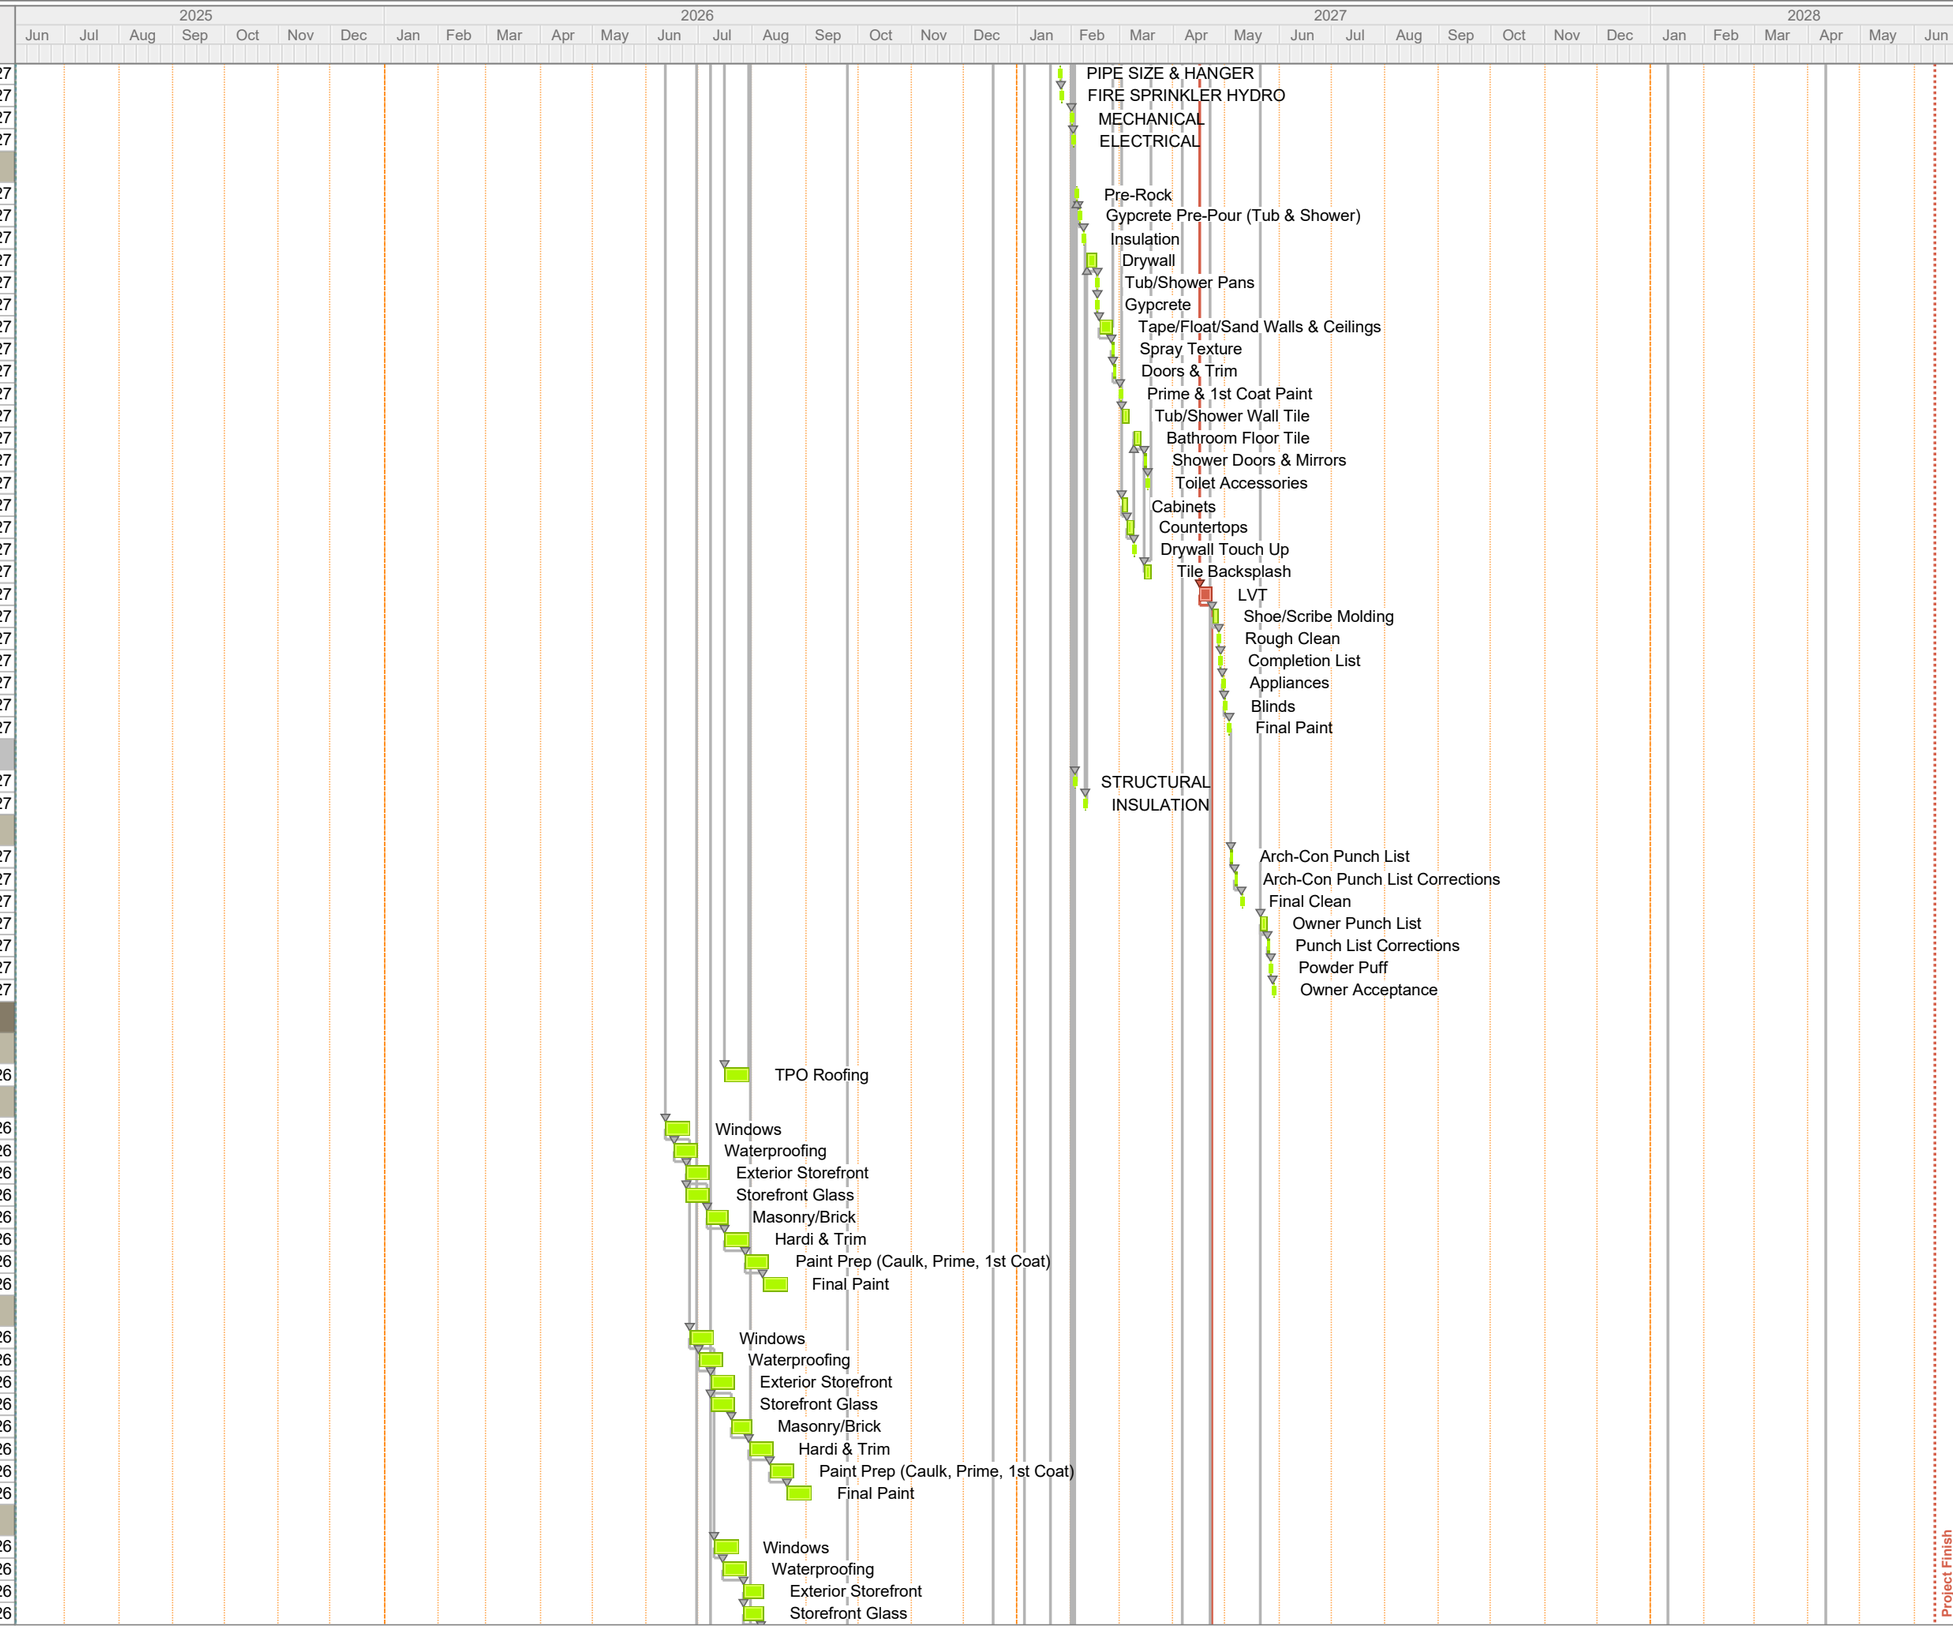

7060	Masonry/Brick	10	08/06/26	08/19/26
7065	Hardi & Trim	10	08/18/26	08/31/26
7070	Paint Prep (Caulk, Prime, 1st Coat)	10	08/28/26	09/11/26
7075	Final Paint	10	09/10/26	09/23/26
Exterior Punch List				
7080	Arch-Con Punch List	1	09/24/26	09/24/26
7085	Arch-Con Punch List Corrections	2	09/25/26	09/28/26
7090	Final Clean	1	09/29/26	09/29/26
7095	Owner Punch List	1	09/30/26	09/30/26
7100	Punch List Corrections	1	10/01/26	10/01/26
7105	Powder Puff	1	10/02/26	10/02/26
7110	Owner Acceptance	1	10/05/26	10/05/26
Stair				
E				
7115	Stair E	30	07/08/26	08/18/26
Final Inspections				
7120	MECHANICAL	15	05/21/27	06/10/27
7125	ELECTRICAL	15	06/11/27	07/01/27
7130	PLUMBING	15	07/02/27	07/22/27
7135	STRUCTURAL	15	07/23/27	08/12/27
7140	FIRE SPRINKLER & FIRE ALARM	15	08/13/27	09/02/27
7145	EGRESS	15	09/03/27	09/24/27
Systems Verification				
7150	Systems Verification	50	09/27/27	12/06/27
Weather				
7155	Weather Impacts Days	25	12/07/27	01/10/28
Substatial Completion				
7160	Substantial Completion	0		01/10/28
Phase 4 (95 Units)				
Slab on Grade				
Pour #09				
Earthwork				
7165	Building Pad (Pour #09)	4	06/30/26	07/03/26
Concrete				
7170	Batter Boards	1	07/06/26	07/06/26
7175	Plumbing Underground	1	07/07/26	07/07/26
7180	Backfill Plumbing	1	07/09/26	07/09/26
7185	Grade Pad	1	07/10/26	07/10/26
7190	Form SOG	1	07/13/26	07/13/26
7195	Termite Treatment	1	07/14/26	07/14/26
7200	Vapor Barrier	1	07/14/26	07/14/26
7205	Under Slab Electrical	1	07/15/26	07/15/26
7210	Rebar/PT Cables	1	07/16/26	07/16/26
7215	Hardware/Anchor Bolts	1	07/17/26	07/17/26
7220	Prep For Inspection	1	07/20/26	07/20/26
7225	Pour SOG	1	07/23/26	07/23/26
7230	Remove Forms	1	07/24/26	07/24/26
7235	Breaks, Stress, EOR Approval, Cut & (	5	07/27/26	07/31/26
Inspections				
7240	PLUMBING	1	07/08/26	07/08/26
7245	ELECTRICAL	1	07/15/26	07/15/26
7250	SOG	1	07/21/26	07/21/26
7255	3RD PARTY - STRUCTURAL	1	07/22/26	07/22/26
Pour #10				
Earthwork				
7260	Building Pad (Pour #10)	4	07/31/26	08/05/26
Concrete				
7265	Batter Boards	1	08/06/26	08/06/26
7270	Plumbing Underground	1	08/07/26	08/07/26
7275	Backfill Plumbing	1	08/11/26	08/11/26
7280	Grade Pad	1	08/12/26	08/12/26
7285	Form SOG	1	08/13/26	08/13/26
7290	Termite Treatment	1	08/14/26	08/14/26
7295	Vapor Barrier	1	08/14/26	08/14/26

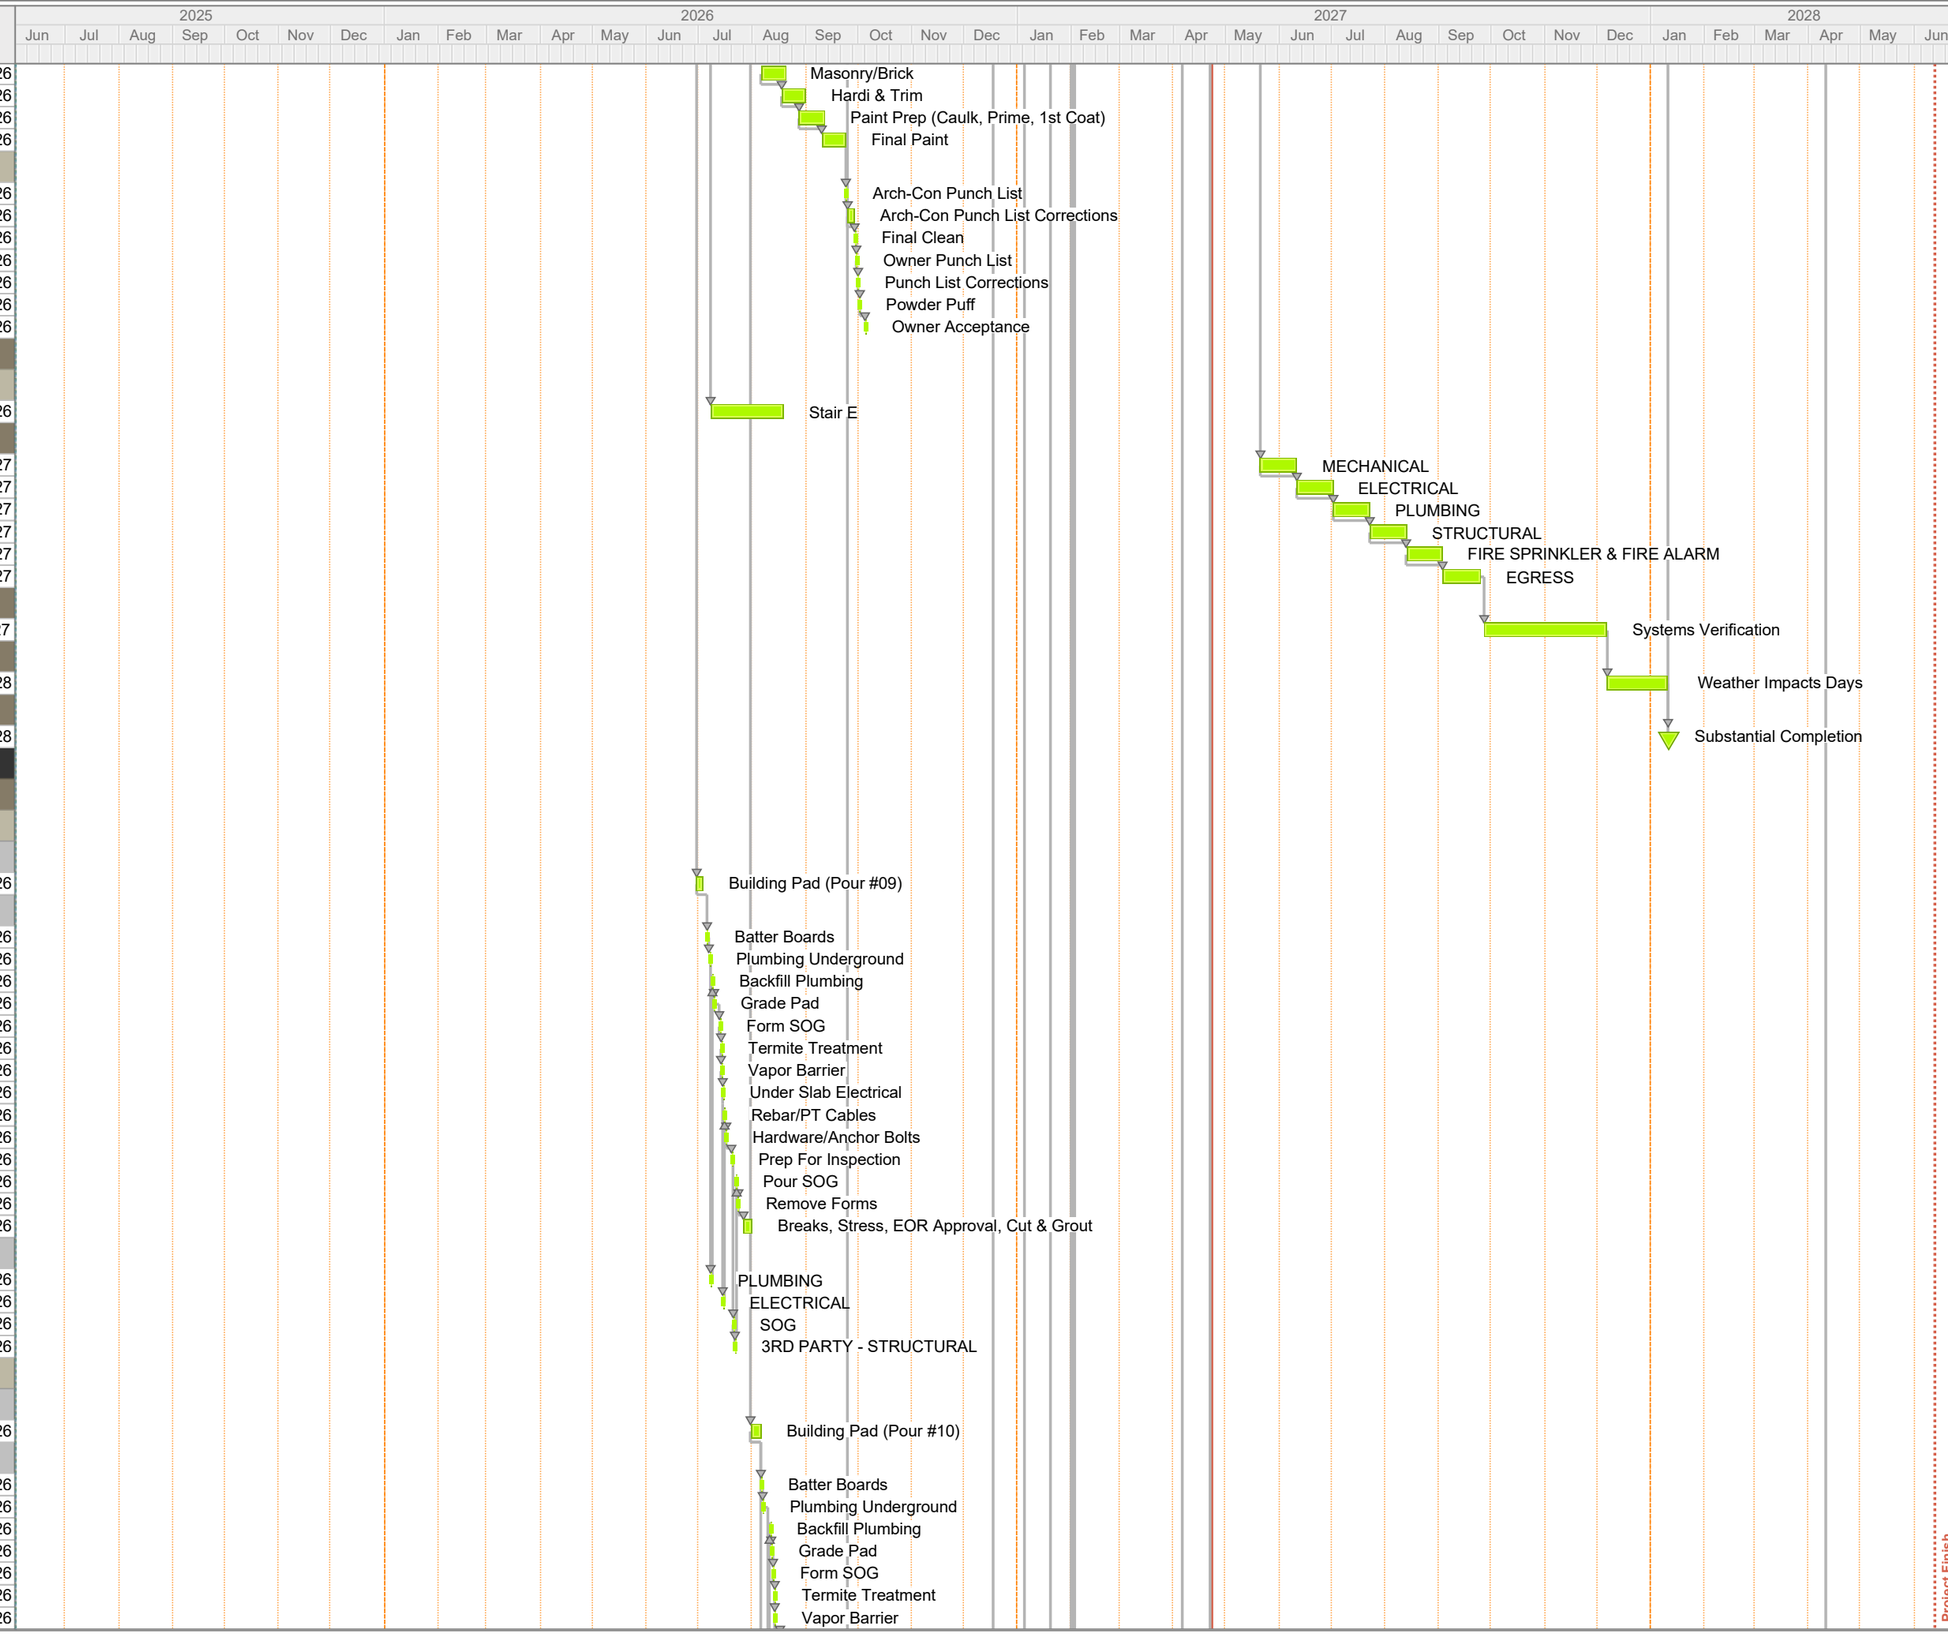

Initials: _____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

7300	Under Slab Electrical	1	08/17/26	08/17/26
7305	Rebar/PT Cables	1	08/18/26	08/18/26
7310	Hardware/Anchor Bolts	1	08/19/26	08/19/26
7315	Prep For Inspection	1	08/20/26	08/20/26
7320	Pour SOG	1	08/25/26	08/25/26
7325	Remove Forms	1	08/26/26	08/26/26
7330	Breaks, Stress, EOR Approval, Cut & (	5	08/27/26	09/02/26
Inspections				
7335	PLUMBING	1	08/10/26	08/10/26
7340	ELECTRICAL	1	08/17/26	08/17/26
7345	SOG	1	08/21/26	08/21/26
7350	3RD PARTY - STRUCTURAL	1	08/24/26	08/24/26
Pour #11				
Earthwork				
7355	Building Pad (Pour #11)	3	08/06/26	08/10/26
Concrete				
7360	Batter Boards	1	08/27/26	08/27/26
7365	Plumbing Underground	1	08/28/26	08/28/26
7370	Backfill Plumbing	1	09/01/26	09/01/26
7375	Grade Pad	1	09/02/26	09/02/26
7380	Form SOG	1	09/03/26	09/03/26
7385	Termite Treatment	1	09/04/26	09/04/26
7390	Vapor Barrier	1	09/04/26	09/04/26
7395	Under Slab Electrical	1	09/08/26	09/08/26
7400	Rebar/PT Cables	1	09/09/26	09/09/26
7405	Hardware/Anchor Bolts	1	09/10/26	09/10/26
7410	Prep For Inspection	1	09/11/26	09/11/26
7415	Pour SOG	1	09/16/26	09/16/26
7420	Remove Forms	1	09/17/26	09/17/26
7425	Breaks, Stress, EOR Approval, Cut & (	5	09/18/26	09/24/26
Inspections				
7430	3RD PARTY - STRUCTURAL	1	09/15/26	09/15/26
7435	PLUMBING	1	08/31/26	08/31/26
7440	ELECTRICAL	1	09/08/26	09/08/26
7445	SOG	1	09/14/26	09/14/26
Lvl. 1				
Wood Framing				
7450	Layout	1	09/25/26	09/25/26
7455	Frame Walls	3	09/28/26	09/30/26
7460	Plumb Line Walls	1	10/01/26	10/01/26
7465	Wall Sheathing	2	10/01/26	10/02/26
7470	Floor Joists	3	10/05/26	10/07/26
7475	Floor Decking	2	10/08/26	10/09/26
Inspections				
7480	STRUCTURAL	1	10/12/26	10/12/26
MEPF				
7485	Plumbing R/I	5	01/20/27	01/26/27
7490	Fire Sprinkler	5	01/27/27	02/02/27
7495	Electrical R/I	5	02/01/27	02/05/27
7500	Mechanical R/I	5	02/02/27	02/08/27
7505	Low Votltage RI	5	02/03/27	02/09/27
7510	MEP 1st Trim	3	03/16/27	03/18/27
7515	Hot Punch	2	03/19/27	03/22/27
7520	HVAC Startup	3	03/23/27	03/25/27
7525	MEP 2nd Trim	2	04/06/27	04/07/27
7530	Low Voltage Trim Out	2	04/06/27	04/07/27
Inspections				
7535	PLUMBING	1	01/27/27	01/27/27
7540	PIPE SIZE & HANGER	1	02/03/27	02/03/27
7545	FIRE SPRINKLER HYDRO	1	02/04/27	02/04/27
7550	MECHANICAL	1	02/09/27	02/09/27
7555	ELECTRICAL	1	02/10/27	02/10/27
Buildout				
7560	Pre-Rock	1	02/12/27	02/12/27
7565	Gypcrete Pre-Pour (Tub & Shower)	1	02/15/27	02/15/27
7570	Insulation	1	02/16/27	02/16/27

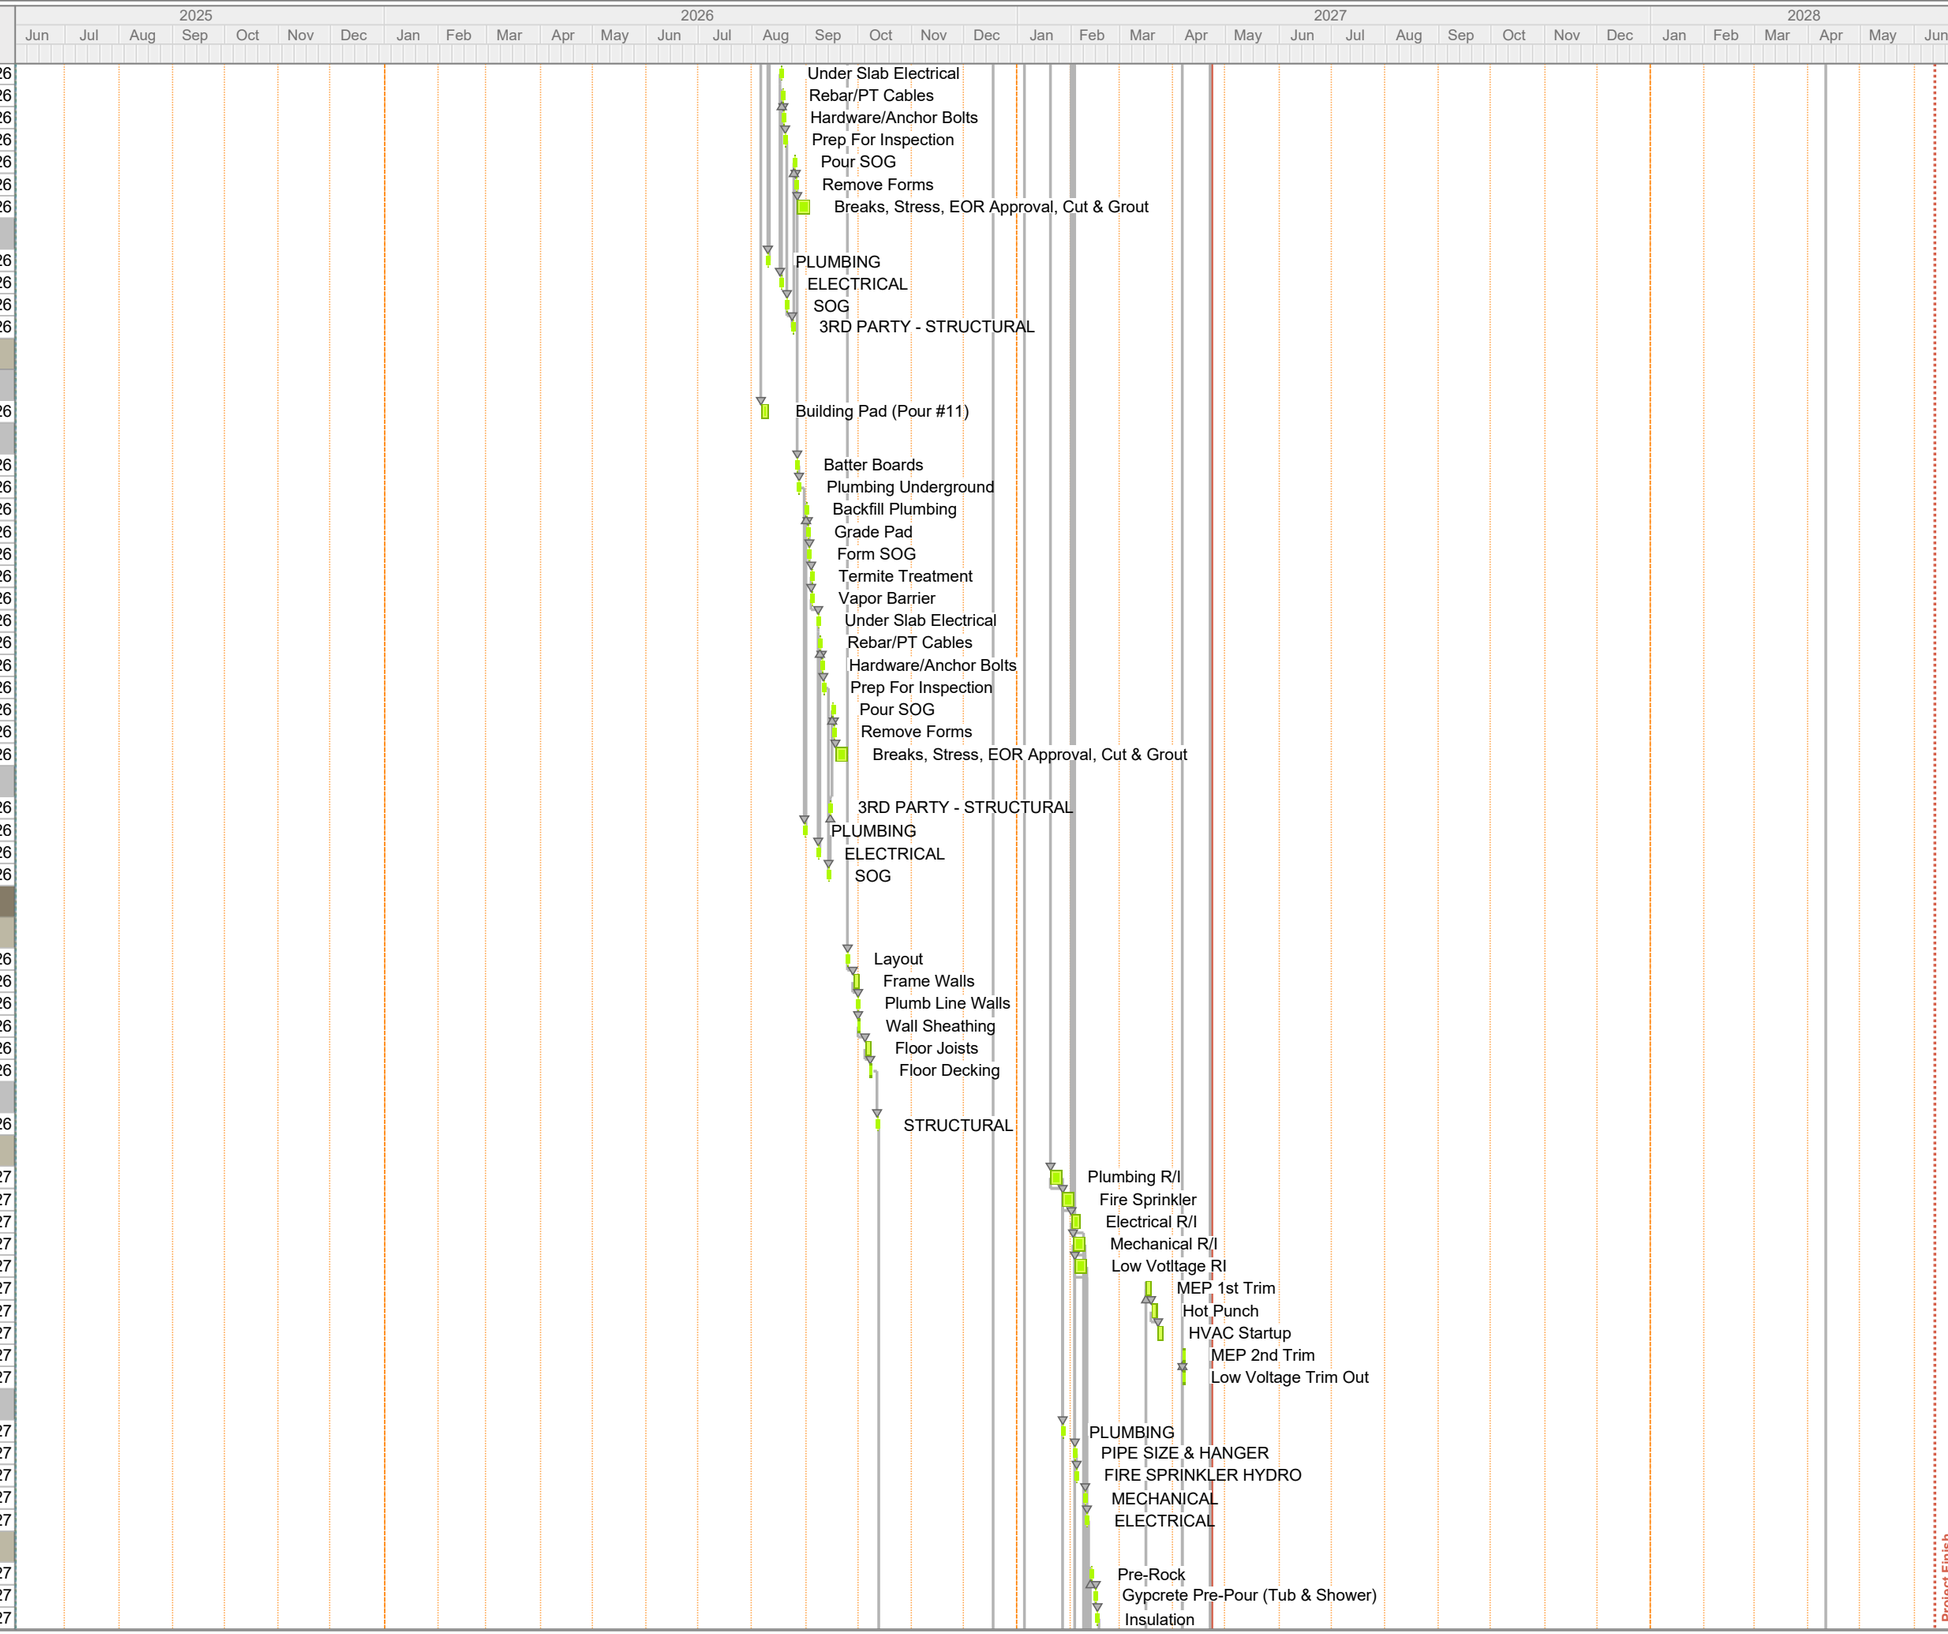

Initials: _____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

7575	Drywall	5	02/18/27	02/24/27
7580	Tub/Shower Pans	1	02/25/27	02/25/27
7585	Gypcrete	1	02/25/27	02/25/27
7590	Tape/Float/Sand Walls & Ceilings	7	02/26/27	03/08/27
7595	Spray Texture	3	03/08/27	03/10/27
7600	Doors & Trim	3	03/10/27	03/12/27
7605	Prime & 1st Coat Paint	2	03/12/27	03/15/27
7610	Tub/Shower Wall Tile	4	03/22/27	03/25/27
7615	Bathroom Floor Tile	4	03/25/27	03/30/27
7620	Shower Doors & Mirrors	1	03/31/27	03/31/27
7625	Toilet Accessories	1	04/01/27	04/01/27
7630	Cabinets	4	03/16/27	03/19/27
7635	Countertops	2	03/22/27	03/23/27
7640	Drywall Touch Up	1	03/24/27	03/24/27
7645	Tile Backsplash	4	03/31/27	04/05/27
7650	LVT	6	04/23/27	04/30/27
7655	Shoe/Scribe Molding	1	05/03/27	05/03/27
7660	Rough Clean	1	05/04/27	05/04/27
7665	Completion List	1	05/05/27	05/05/27
7670	Appliances	1	05/06/27	05/06/27
7675	Blinds	1	05/07/27	05/07/27
7680	Final Paint	1	05/10/27	05/10/27
Inspections				
7685	STRUCTURAL	1	02/11/27	02/11/27
7690	INSULATION	1	02/17/27	02/17/27
Interior Punch List				
7695	Arch-Con Punch List	2	05/11/27	05/12/27
7700	Arch-Con Punch List Corrections	2	05/13/27	05/14/27
7705	Final Clean	1	05/17/27	05/17/27
7710	Owner Punch List	3	05/18/27	05/20/27
7715	Punch List Corrections	3	05/20/27	05/24/27
7720	Powder Puff	1	05/25/27	05/25/27
7725	Owner Acceptance	2	05/26/27	05/27/27
Lvl. 2				
Wood Framing				
7730	Layout	1	10/13/26	10/13/26
7735	Frame Walls	3	10/14/26	10/16/26
7740	Plumb Line Walls	1	10/19/26	10/19/26
7745	Wall Sheathing	2	10/19/26	10/20/26
7750	Floor Joists	3	10/21/26	10/23/26
7755	Floor Decking	2	10/26/26	10/27/26
Inspections				
7760	STRUCTURAL	1	10/28/26	10/28/26
MEPF				
7765	Plumbing R/I	5	01/27/27	02/02/27
7770	Fire Sprinkler	5	02/03/27	02/09/27
7775	Electrical R/I	5	02/08/27	02/12/27
7780	Mechanical R/I	5	02/09/27	02/15/27
7785	Low Votltage RI	5	02/10/27	02/16/27
7790	MEP 1st Trim	3	03/22/27	03/24/27
7795	Hot Punch	2	03/25/27	03/26/27
7800	HVAC Startup	3	03/29/27	03/31/27
7805	MEP 2nd Trim	2	04/09/27	04/12/27
7810	Low Voltage Trim Out	2	04/09/27	04/12/27
Inspections				
7815	PLUMBING	1	02/03/27	02/03/27
7820	PIPE SIZE & HANGER	1	02/10/27	02/10/27
7825	FIRE SPRINKLER HYDRO	1	02/11/27	02/11/27
7830	MECHANICAL	1	02/16/27	02/16/27
7835	ELECTRICAL	1	02/17/27	02/17/27
Buildout				
7840	Pre-Rock	1	02/19/27	02/19/27
7845	Gypcrete Pre-Pour (Tub & Shower)	1	02/22/27	02/22/27
7850	Insulation	1	02/23/27	02/23/27
7855	Drywall	5	02/25/27	03/03/27
7860	Tub/Shower Pans	1	03/04/27	03/04/27
7865	Gypcrete	1	03/04/27	03/04/27

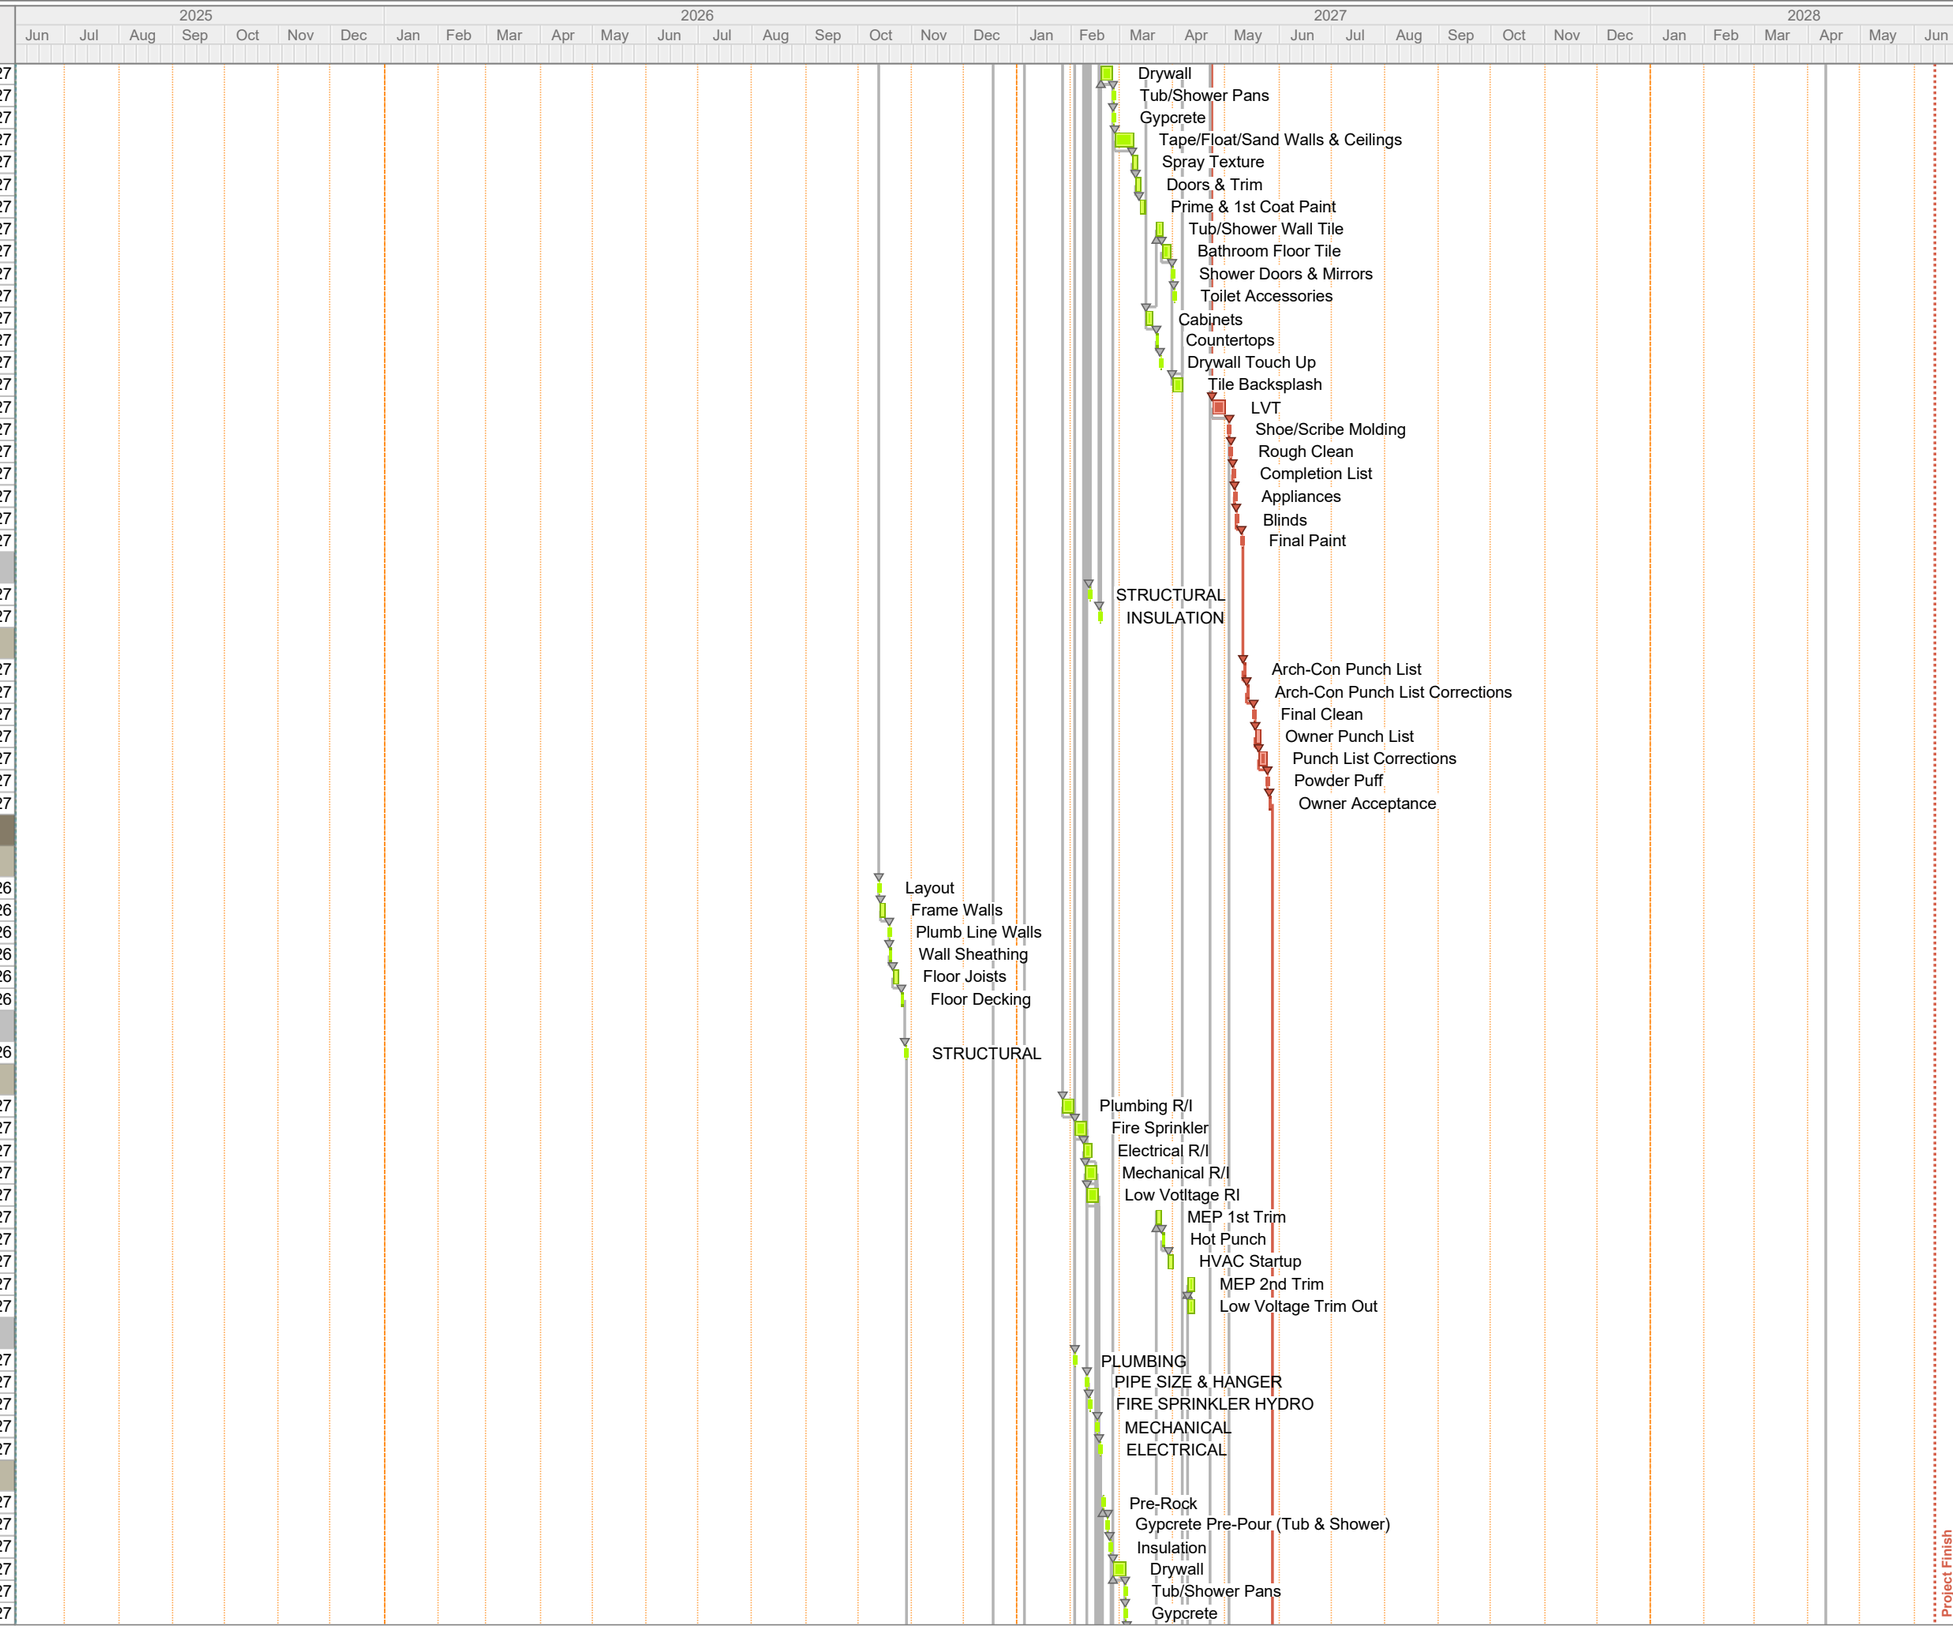

Initials: _____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

7870	Tape/Float/Sand Walls & Ceilings	7	03/05/27	03/15/27
7875	Spray Texture	3	03/15/27	03/17/27
7880	Doors & Trim	3	03/16/27	03/18/27
7885	Prime & 1st Coat Paint	2	03/18/27	03/19/27
7890	Tub/Shower Wall Tile	4	03/22/27	03/25/27
7895	Bathroom Floor Tile	4	03/30/27	04/02/27
7900	Shower Doors & Mirrors	1	04/05/27	04/05/27
7905	Toilet Accessories	1	04/06/27	04/06/27
7910	Cabinets	4	03/22/27	03/25/27
7915	Countertops	2	03/26/27	03/29/27
7920	Drywall Touch Up	1	03/30/27	03/30/27
7925	Tile Backsplash	4	04/05/27	04/08/27
7930	LVT	6	05/03/27	05/10/27
7935	Shoe/Scribe Molding	1	05/11/27	05/11/27
7940	Rough Clean	1	05/12/27	05/12/27
7945	Completion List	1	05/13/27	05/13/27
7950	Appliances	1	05/14/27	05/14/27
7955	Blinds	1	05/17/27	05/17/27
7960	Final Paint	1	05/18/27	05/18/27
Inspections				
7965	STRUCTURAL	1	02/18/27	02/18/27
7970	INSULATION	1	02/24/27	02/24/27
Interior Punch List				
7975	Arch-Con Punch List	2	05/19/27	05/20/27
7980	Arch-Con Punch List Corrections	2	05/21/27	05/24/27
7985	Final Clean	1	05/25/27	05/25/27
7990	Owner Punch List	3	05/28/27	06/01/27
7995	Punch List Corrections	3	06/01/27	06/03/27
8000	Powder Puff	1	06/04/27	06/04/27
8005	Owner Acceptance	2	06/07/27	06/08/27
Lvl. 3				
Wood Framing				
8010	Layout	1	10/29/26	10/29/26
8015	Frame Walls	3	10/30/26	11/03/26
8020	Plumb Line Walls	1	11/04/26	11/04/26
8025	Wall Sheathing	2	11/04/26	11/05/26
8030	Floor Joists	3	11/06/26	11/10/26
8035	Floor Decking	2	11/11/26	11/12/26
Inspections				
8040	STRUCTURAL	1	11/13/26	11/13/26
MEPF				
8045	Plumbing R/I	5	02/03/27	02/09/27
8050	Fire Sprinkler	5	02/10/27	02/16/27
8055	Electrical R/I	5	02/15/27	02/19/27
8060	Mechanical R/I	5	02/16/27	02/22/27
8065	Low Votltage RI	5	02/17/27	02/23/27
8070	MEP 1st Trim	3	03/29/27	03/31/27
8075	Hot Punch	2	04/01/27	04/02/27
8080	HVAC Startup	3	04/05/27	04/07/27
8085	MEP 2nd Trim	2	04/16/27	04/19/27
8090	Low Voltage Trim Out	2	04/16/27	04/19/27
Inspections				
8095	PLUMBING	1	02/10/27	02/10/27
8100	PIPE SIZE & HANGER	1	02/16/27	02/16/27
8105	FIRE SPRINKLER HYDRO	1	02/17/27	02/17/27
8110	MECHANICAL	1	02/23/27	02/23/27
8115	ELECTRICAL	1	02/24/27	02/24/27
Buildout				
8120	Pre-Rock	1	02/26/27	02/26/27
8125	Gypcrete Pre-Pour (Tub & Shower)	1	03/01/27	03/01/27
8130	Insulation	1	03/02/27	03/02/27
8135	Drywall	5	03/04/27	03/10/27
8140	Tub/Shower Pans	1	03/11/27	03/11/27
8145	Gypcrete	1	03/11/27	03/11/27
8150	Tape/Float/Sand Walls & Ceilings	7	03/12/27	03/22/27
8155	Spray Texture	3	03/22/27	03/24/27
8160	Doors & Trim	3	03/23/27	03/25/27

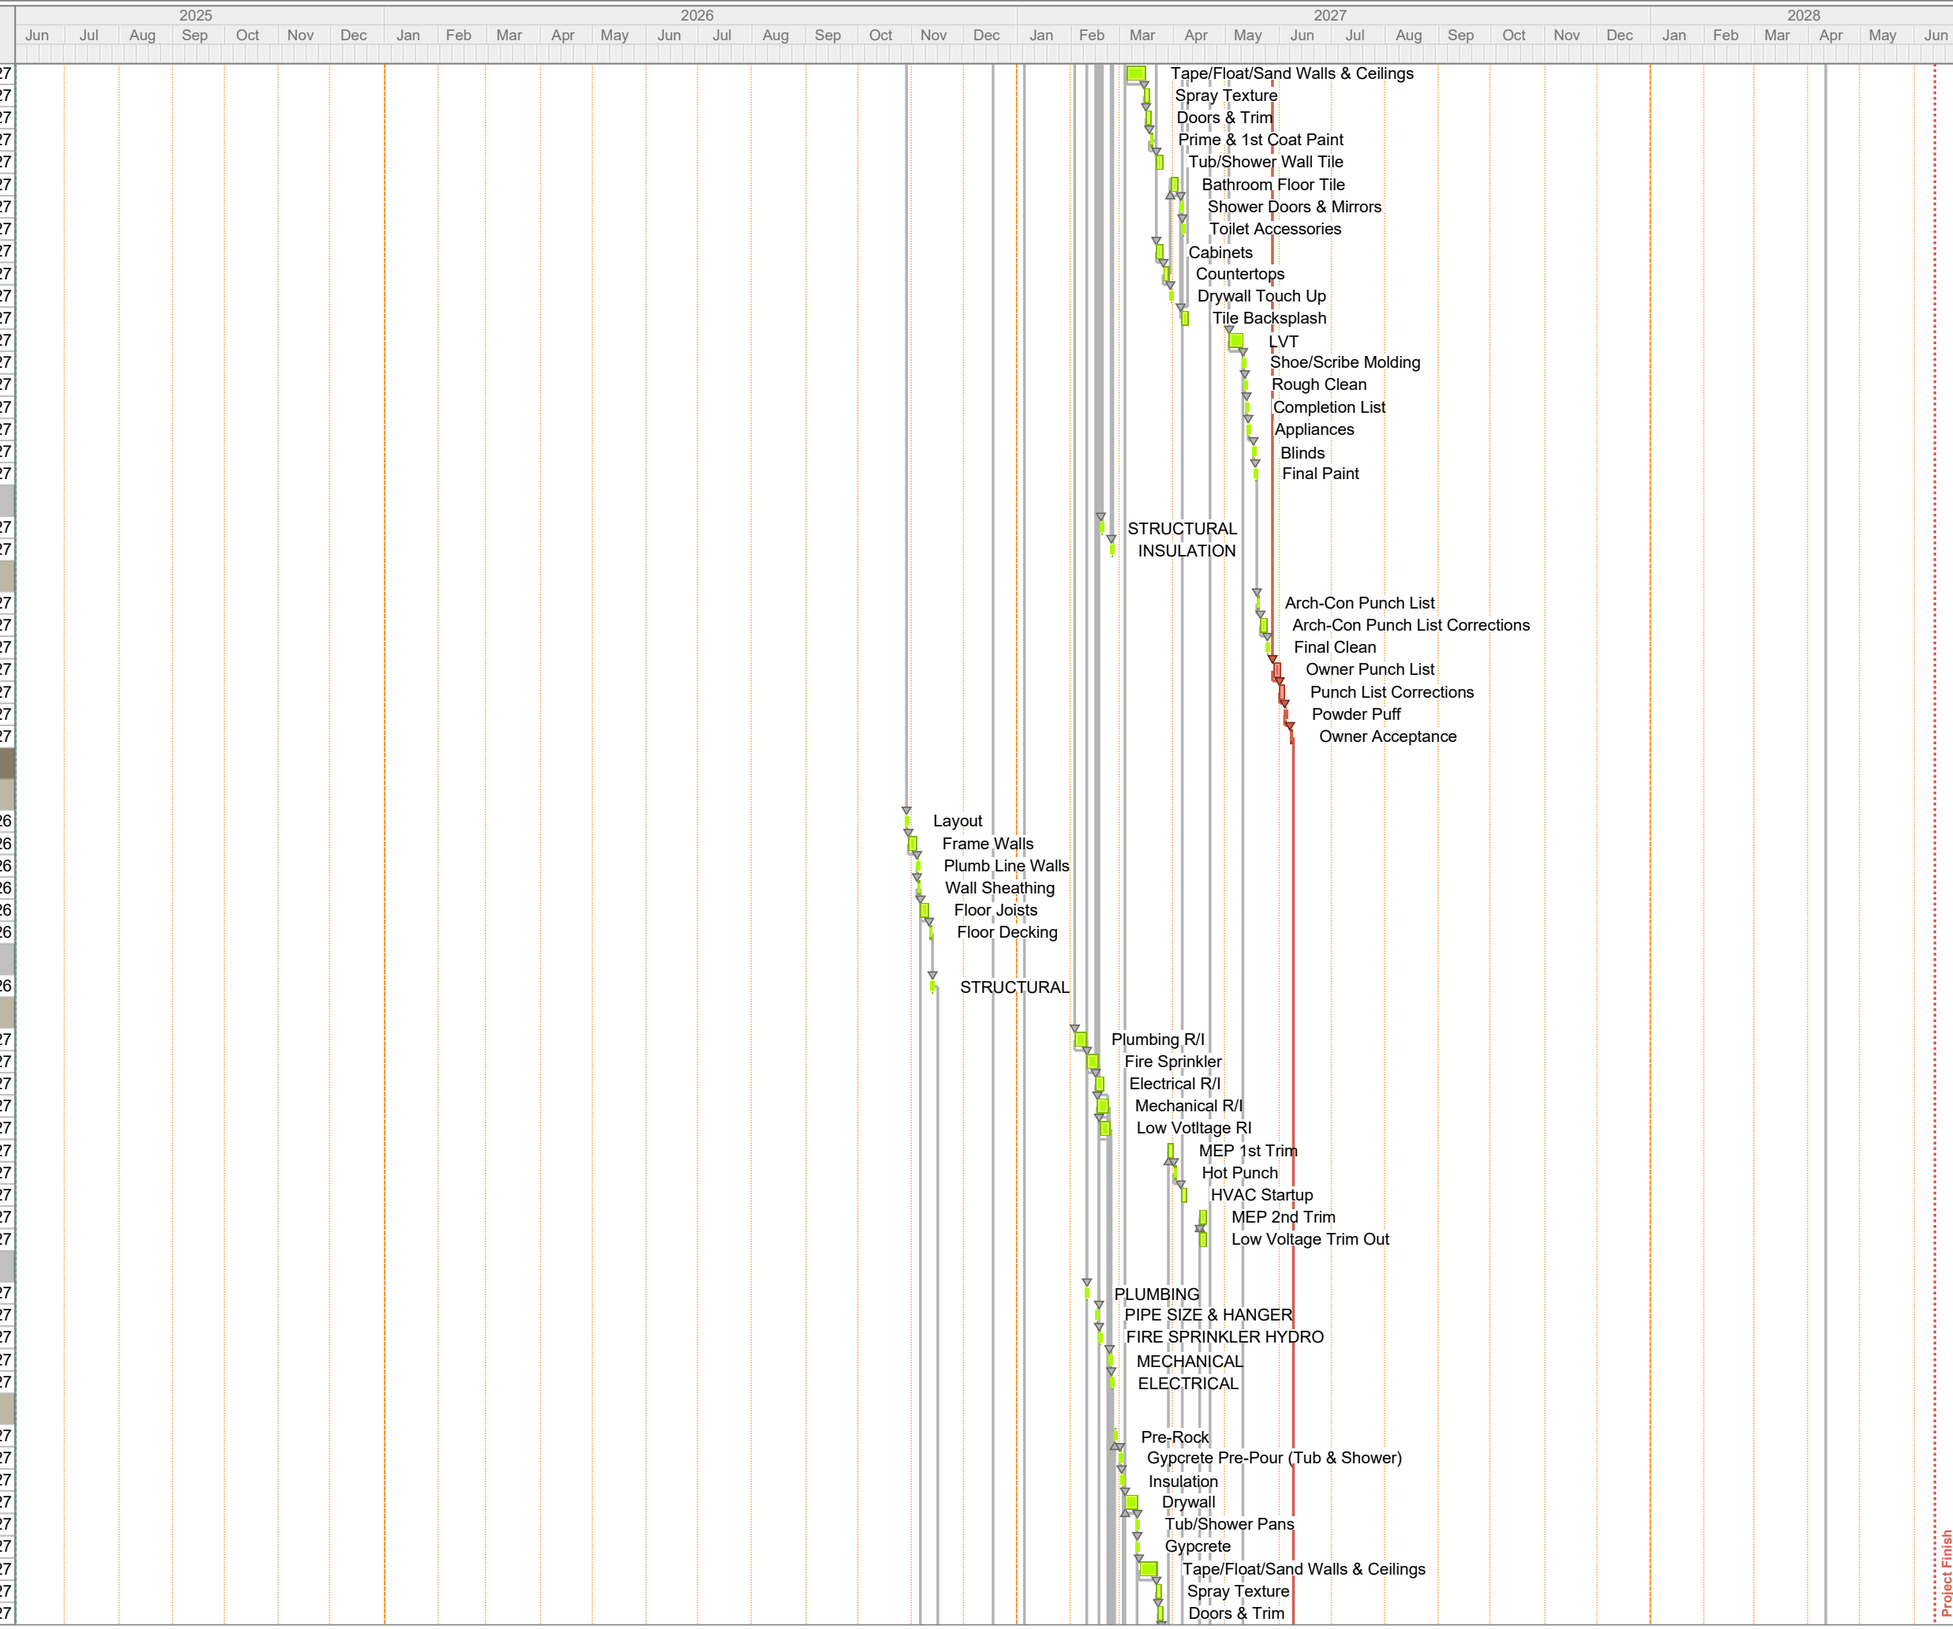

Initials: _____

8165	Prime & 1st Coat Paint	2	03/25/27	03/26/27
8170	Tub/Shower Wall Tile	4	03/29/27	04/01/27
8175	Bathroom Floor Tile	4	04/06/27	04/09/27
8180	Shower Doors & Mirrors	1	04/12/27	04/12/27
8185	Toilet Accessories	1	04/13/27	04/13/27
8190	Cabinets	4	03/29/27	04/01/27
8195	Countertops	2	04/02/27	04/05/27
8200	Drywall Touch Up	1	04/06/27	04/06/27
8205	Tile Backsplash	4	04/12/27	04/15/27
8210	LVT	6	05/11/27	05/18/27
8215	Shoe/Scribe Molding	1	05/19/27	05/19/27
8220	Rough Clean	1	05/20/27	05/20/27
8225	Completion List	1	05/21/27	05/21/27
8230	Appliances	1	05/24/27	05/24/27
8235	Blinds	1	05/25/27	05/25/27
8240	Final Paint	1	05/26/27	05/26/27
Inspections				
8245	STRUCTURAL	1	02/25/27	02/25/27
8250	INSULATION	1	03/03/27	03/03/27
Interior Punch List				
8255	Arch-Con Punch List	2	05/27/27	05/28/27
8260	Arch-Con Punch List Corrections	2	05/31/27	06/01/27
8265	Final Clean	1	06/02/27	06/02/27
8270	Owner Punch List	3	06/09/27	06/11/27
8275	Punch List Corrections	3	06/11/27	06/15/27
8280	Powder Puff	1	06/16/27	06/16/27
8285	Owner Acceptance	2	06/17/27	06/18/27
Lvl. 4				
Wood Framing				
8290	Layout	1	11/16/26	11/16/26
8295	Frame Walls	3	11/17/26	11/19/26
8300	Plumb Line Walls	1	11/20/26	11/20/26
8305	Wall Shearhing	2	11/20/26	11/23/26
8310	Floor Joists	3	11/24/26	11/27/26
8315	Floor Decking	2	11/30/26	12/01/26
Inspections				
8320	STRUCTURAL	1	12/02/26	12/02/26
MEPF				
8325	Plumbing R/I	5	02/10/27	02/16/27
8330	Fire Sprinkler	5	02/17/27	02/23/27
8335	Electrical R/I	5	02/22/27	02/26/27
8340	Mechanical R/I	5	02/23/27	03/01/27
8345	Low Votltage RI	5	02/24/27	03/02/27
8350	MEP 1st Trim	3	04/05/27	04/07/27
8355	Hot Punch	2	04/08/27	04/09/27
8360	HVAC Startup	3	04/12/27	04/14/27
8365	MEP 2nd Trim	2	04/23/27	04/26/27
8370	Low Voltage Trim Out	2	04/23/27	04/26/27
Inspections				
8375	PLUMBING	1	02/17/27	02/17/27
8380	PIPE SIZE & HANGER	1	02/23/27	02/23/27
8385	FIRE SPRINKLER HYDRO	1	02/24/27	02/24/27
8390	MECHANICAL	1	03/02/27	03/02/27
8395	ELECTRICAL	1	03/03/27	03/03/27
Buildout				
8400	Pre-Rock	1	03/05/27	03/05/27
8405	Gypcrete Pre-Pour (Tub & Shower)	1	03/08/27	03/08/27
8410	Insulation	1	03/09/27	03/09/27
8415	Drywall	5	03/11/27	03/17/27
8420	Tub/Shower Pans	1	03/18/27	03/18/27
8425	Gypcrete	1	03/18/27	03/18/27
8430	Tape/Float/Sand Walls & Ceilings	7	03/19/27	03/29/27
8435	Spray Texture	3	03/29/27	03/31/27
8440	Doors & Trim	3	03/30/27	04/01/27
8445	Prime & 1st Coat Paint	2	04/01/27	04/02/27
8450	Tub/Shower Wall Tile	4	04/05/27	04/08/27
8455	Bathroom Floor Tile	4	04/13/27	04/16/27

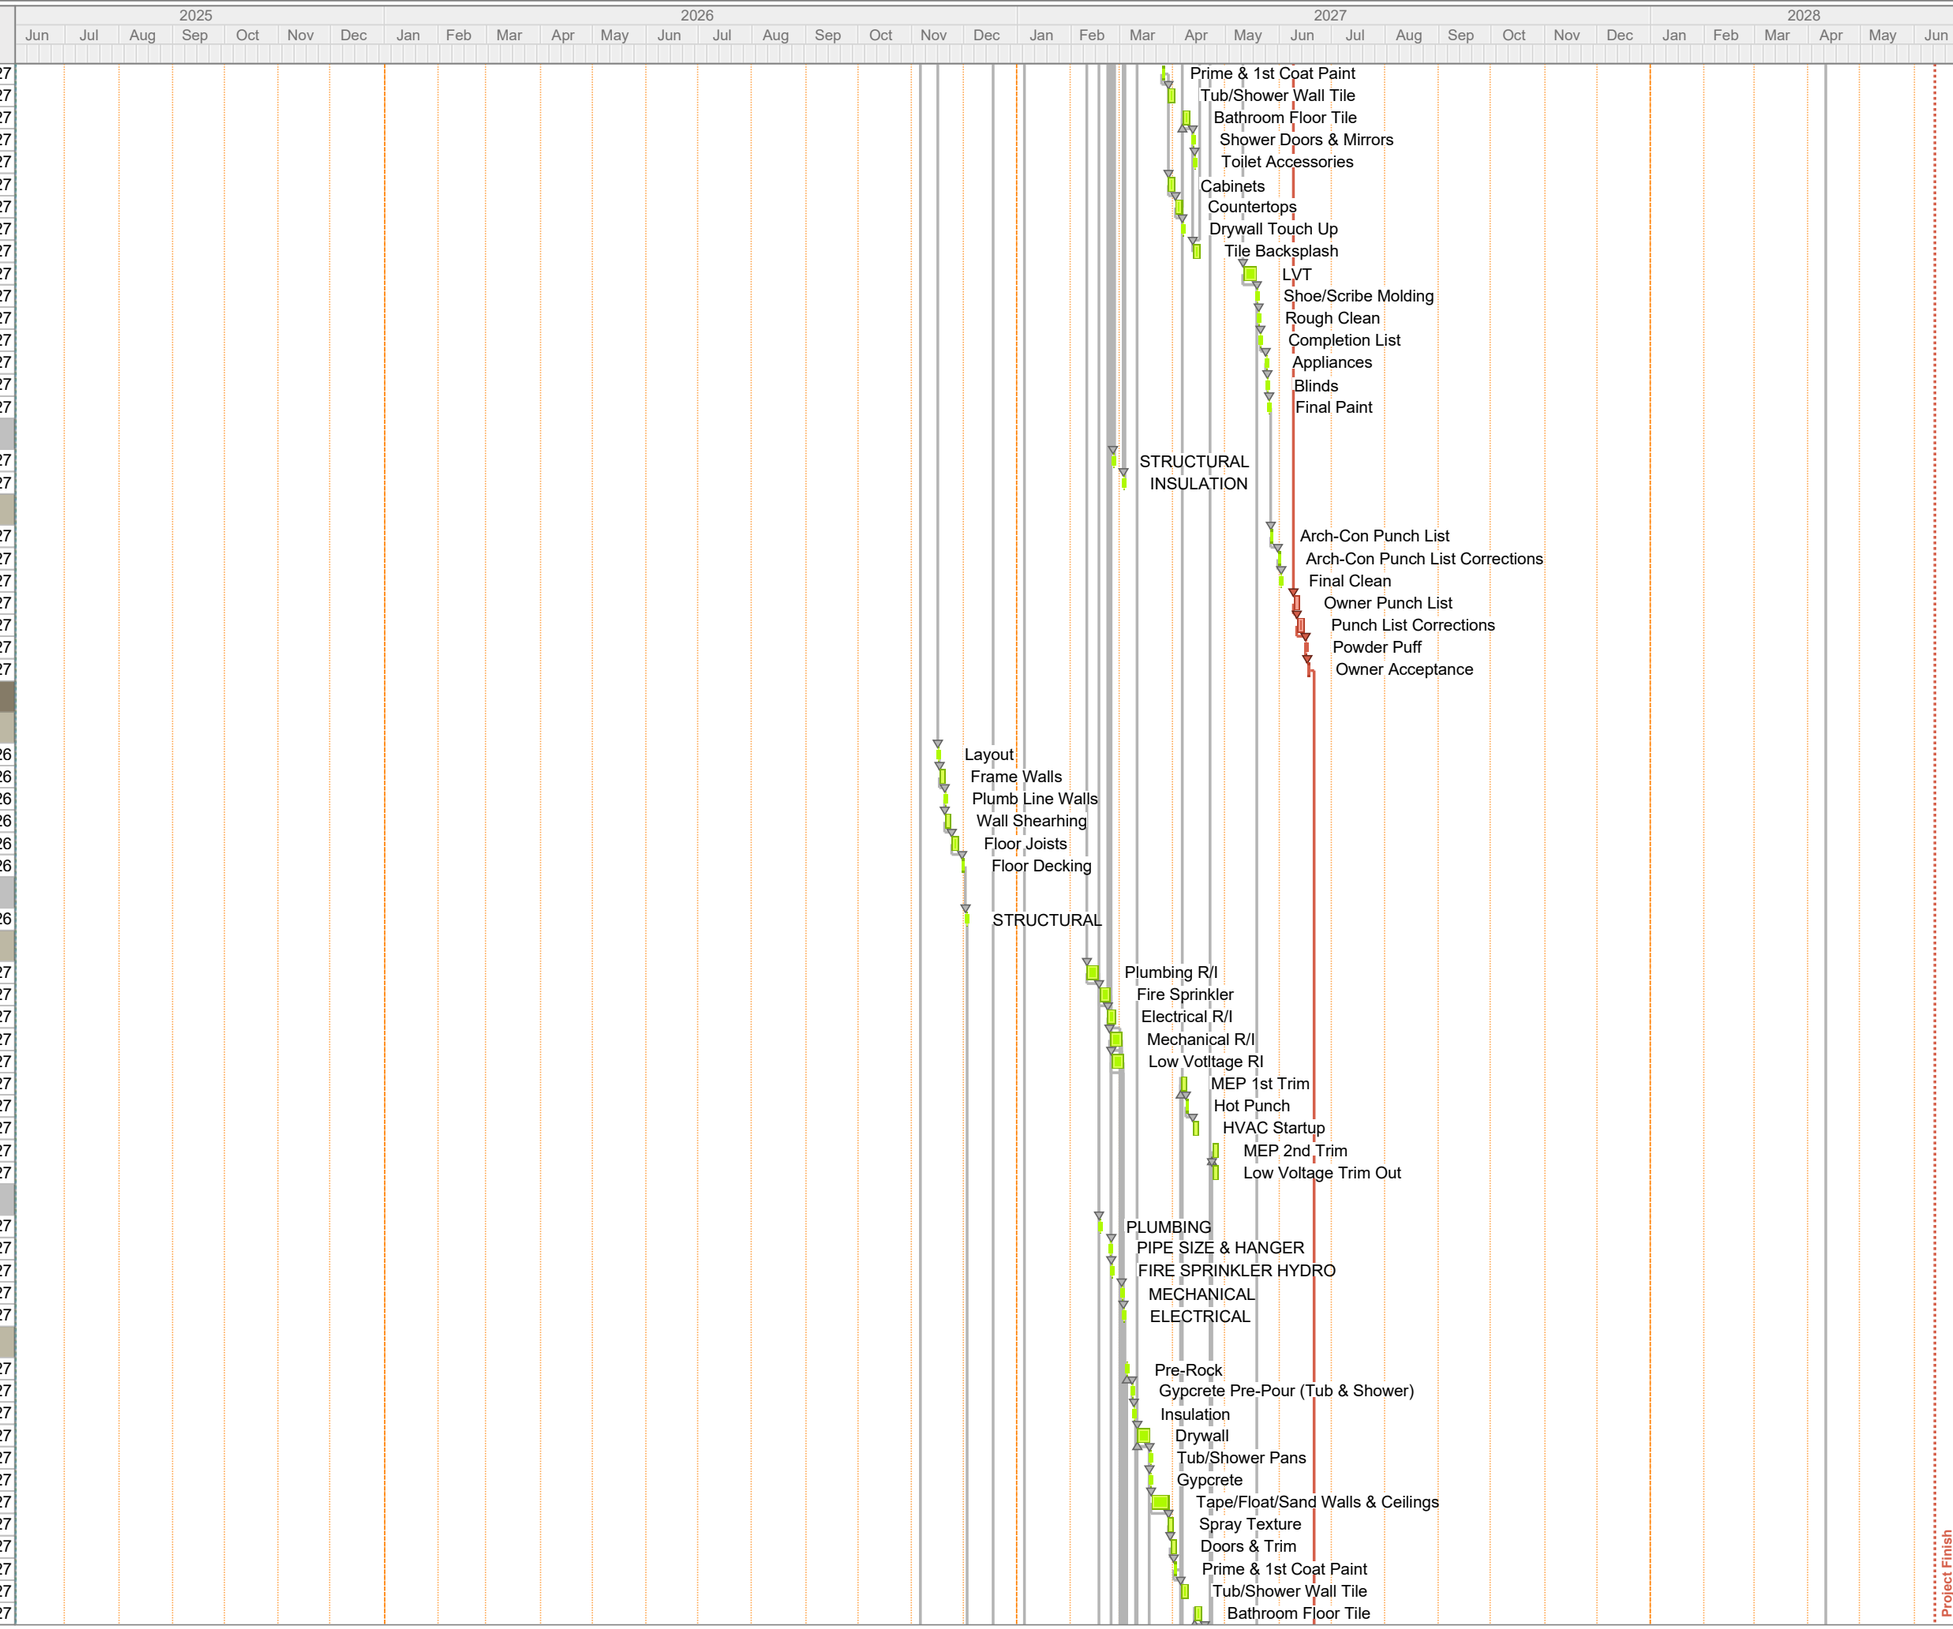

Initials: _____

8460	Shower Doors & Mirrors	1	04/19/27	04/19/27
8465	Toilet Accessories	1	04/20/27	04/20/27
8470	Cabinets	4	04/05/27	04/08/27
8475	Countertops	2	04/09/27	04/12/27
8480	Drywall Touch Up	1	04/13/27	04/13/27
8485	Tile Backsplash	4	04/19/27	04/22/27
8490	LVT	6	05/19/27	05/26/27
8495	Shoe/Scribe Molding	1	05/27/27	05/27/27
8500	Rough Clean	1	05/28/27	05/28/27
8505	Completion List	1	05/31/27	05/31/27
8510	Appliances	1	06/01/27	06/01/27
8515	Blinds	1	06/02/27	06/02/27
8520	Final Paint	1	06/03/27	06/03/27
Inspections				
8525	STRUCTURAL	1	03/04/27	03/04/27
8530	INSULATION	1	03/10/27	03/10/27
Interior Punch List				
8535	Arch-Con Punch List	2	06/04/27	06/07/27
8540	Arch-Con Punch List Corrections	2	06/08/27	06/09/27
8545	Final Clean	1	06/10/27	06/10/27
8550	Owner Punch List	3	06/21/27	06/23/27
8555	Punch List Corrections	3	06/23/27	06/25/27
8560	Powder Puff	1	06/28/27	06/28/27
8565	Owner Acceptance	2	06/29/27	06/30/27
Lvl. 5				
Wood Framing				
8570	Layout	1	12/03/26	12/03/26
8575	Frame Walls	3	12/04/26	12/08/26
8580	Plumb Line Walls	1	12/09/26	12/09/26
8585	Wall Sheathing	2	12/09/26	12/10/26
8590	Roof Joists	3	12/11/26	12/15/26
8595	Roof Decking	2	12/16/26	12/17/26
Inspections				
8600	STRUCTURAL	1	12/18/26	12/18/26
MEPF				
8605	Plumbing R/I	5	02/17/27	02/23/27
8610	Fire Sprinkler	5	02/24/27	03/02/27
8615	Electrical R/I	5	03/01/27	03/05/27
8620	Mechanical R/I	5	03/02/27	03/08/27
8625	Low Votltage RI	5	03/03/27	03/09/27
8630	MEP 1st Trim	3	04/12/27	04/14/27
8635	Hot Punch	2	04/15/27	04/16/27
8640	HVAC Startup	3	04/19/27	04/21/27
8645	MEP 2nd Trim	2	04/30/27	05/03/27
8650	Low Voltage Trim Out	2	04/30/27	05/03/27
Inspections				
8655	PLUMBING	1	02/24/27	02/24/27
8660	PIPE SIZE & HANGER	1	03/02/27	03/02/27
8665	FIRE SPRINKLER HYDRO	1	03/03/27	03/03/27
8670	MECHANICAL	1	03/09/27	03/09/27
8675	ELECTRICAL	1	03/10/27	03/10/27
Buildout				
8680	Pre-Rock	1	03/12/27	03/12/27
8685	Gypcrete Pre-Pour (Tub & Shower)	1	03/15/27	03/15/27
8690	Insulation	1	03/16/27	03/16/27
8695	Drywall	5	03/18/27	03/24/27
8700	Tub/Shower Pans	1	03/25/27	03/25/27
8705	Gypcrete	1	03/25/27	03/25/27
8710	Tape/Float/Sand Walls & Ceilings	7	03/26/27	04/05/27
8715	Spray Texture	3	04/05/27	04/07/27
8720	Doors & Trim	3	04/06/27	04/08/27
8725	Prime & 1st Coat Paint	2	04/08/27	04/09/27
8730	Tub/Shower Wall Tile	4	04/12/27	04/15/27
8735	Bathroom Floor Tile	4	04/20/27	04/23/27
8740	Shower Doors & Mirrors	1	04/26/27	04/26/27
8745	Toilet Accessories	1	04/27/27	04/27/27
8750	Cabinets	4	04/12/27	04/15/27

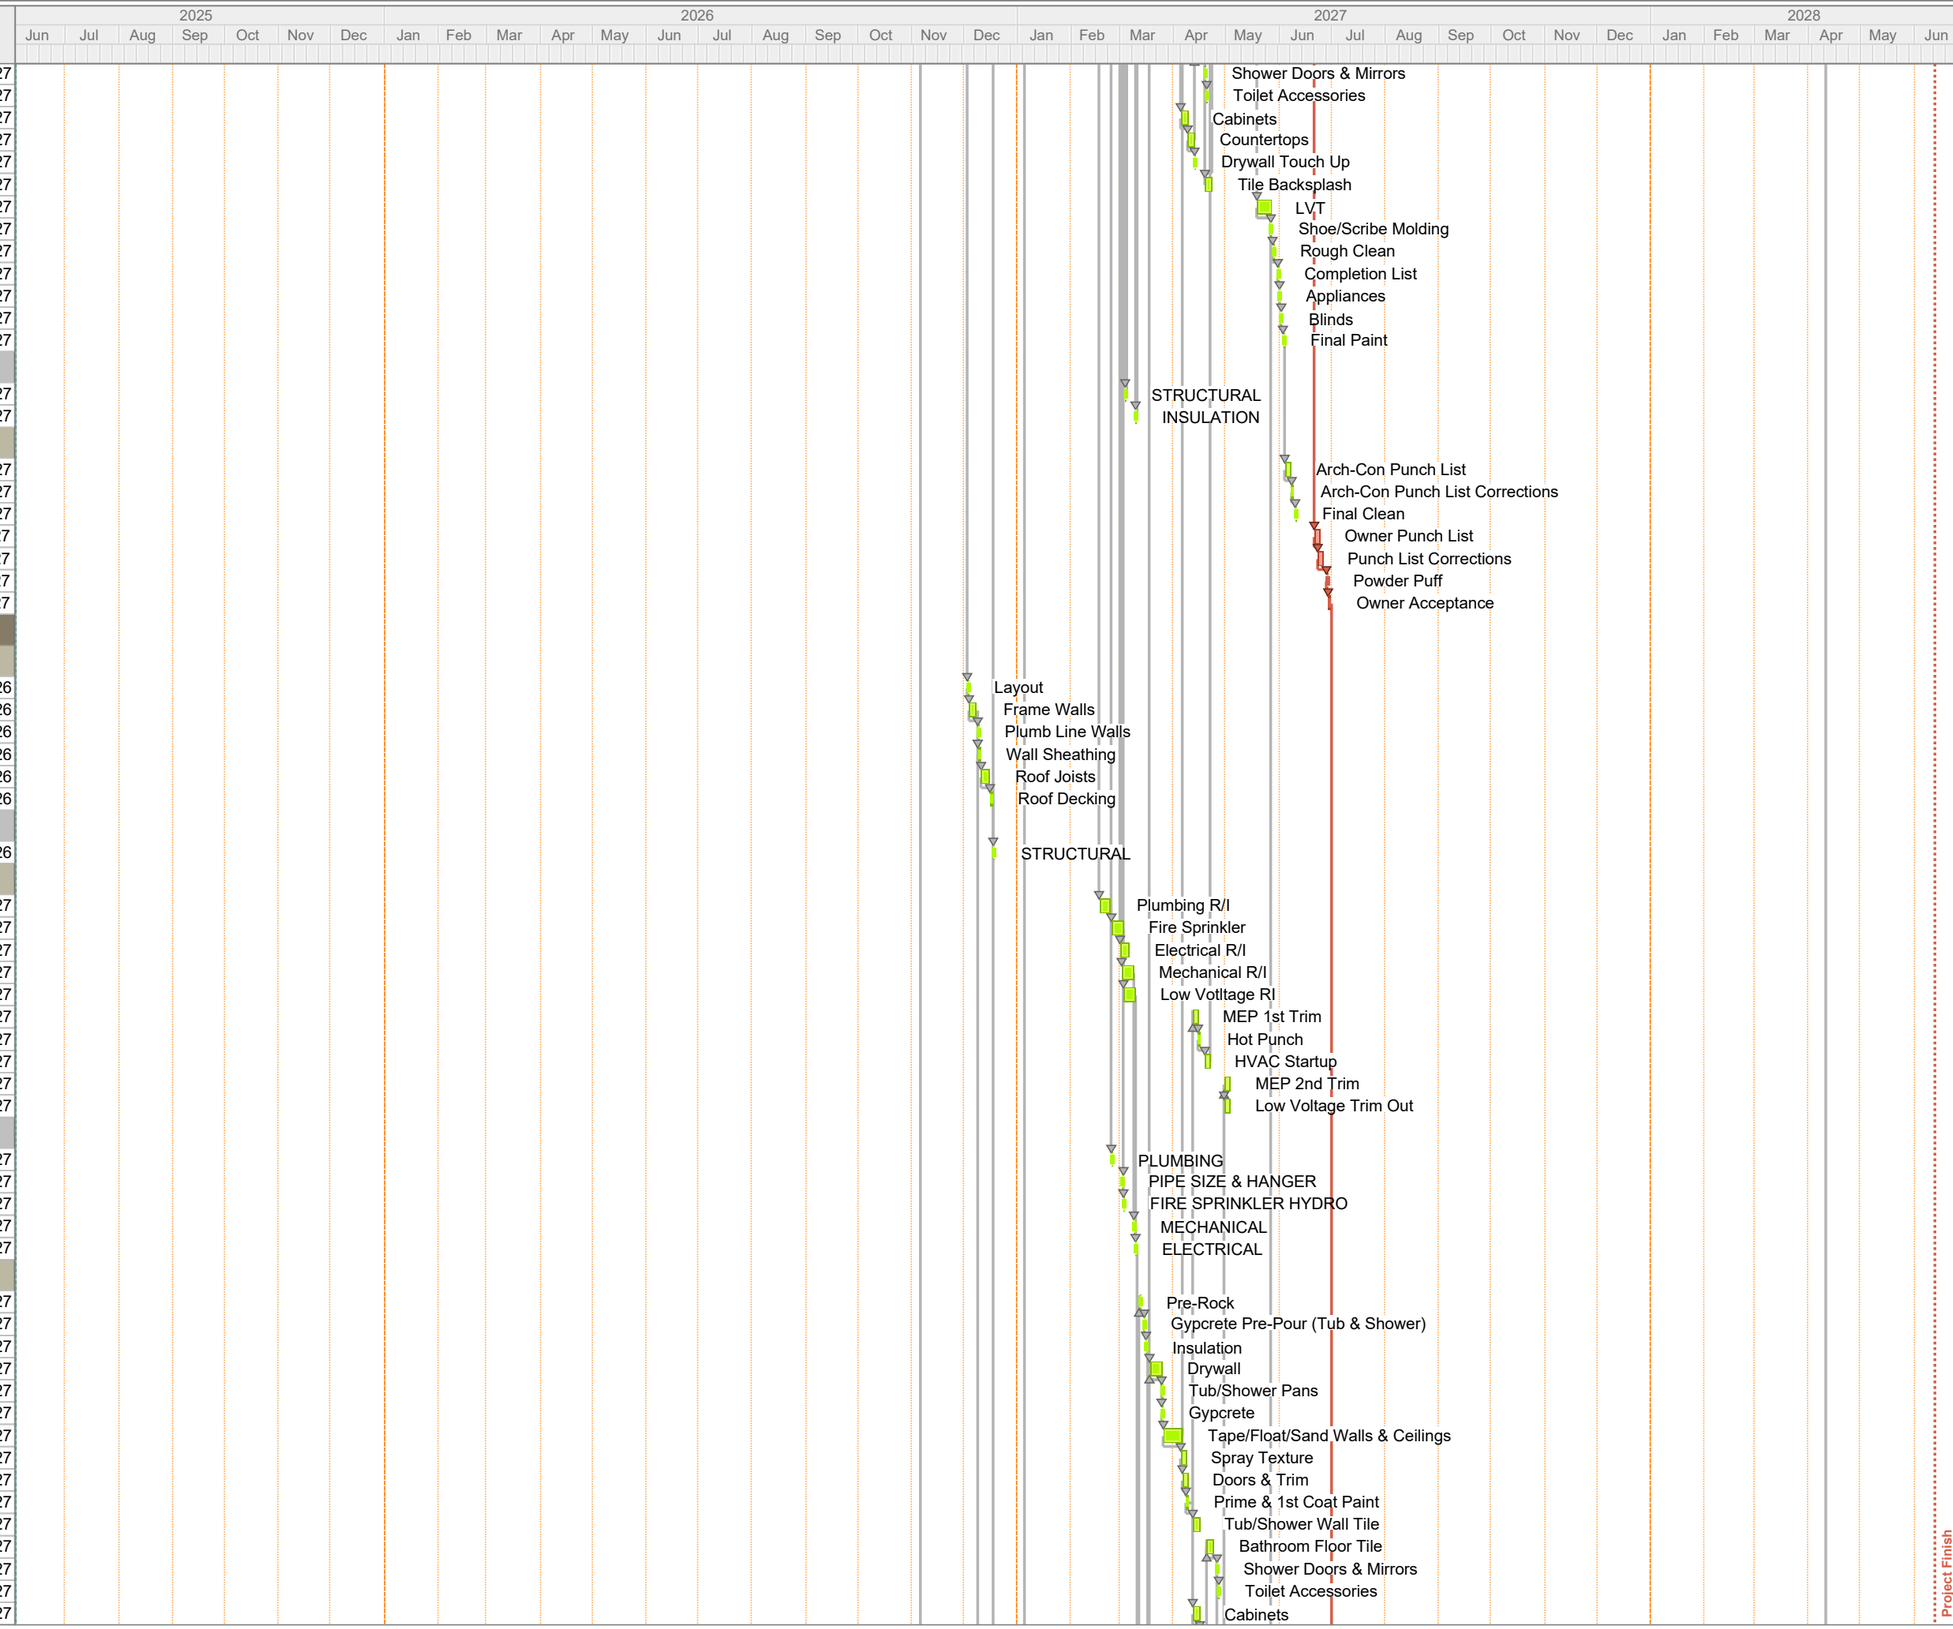

Initials: _____

8755	Countertops	2	04/16/27	04/19/27
8760	Drywall Touch Up	1	04/20/27	04/20/27
8765	Tile Backsplash	4	04/26/27	04/29/27
8770	LVT	6	05/27/27	06/03/27
8775	Shoe/Scribe Molding	1	06/04/27	06/04/27
8780	Rough Clean	1	06/07/27	06/07/27
8785	Completion List	1	06/08/27	06/08/27
8790	Appliances	1	06/09/27	06/09/27
8795	Blinds	1	06/10/27	06/10/27
8800	Final Paint	1	06/11/27	06/11/27
Inspections				
8805	STRUCTURAL	1	03/11/27	03/11/27
8810	INSULATION	1	03/17/27	03/17/27
Interior Punch List				
8815	Arch-Con Punch List	2	06/14/27	06/15/27
8820	Arch-Con Punch List Corrections	2	06/16/27	06/17/27
8825	Final Clean	1	06/18/27	06/18/27
8830	Owner Punch List	3	07/01/27	07/05/27
8835	Punch List Corrections	3	07/05/27	07/07/27
8840	Powder Puff	1	07/08/27	07/08/27
8845	Owner Acceptance	2	07/09/27	07/12/27
Building Exterior				
Roof				
8850	TPO Install	7	12/18/26	12/29/26
8855	Parapet Cap	3	12/30/26	01/04/27
East Elevation (Left)				
8860	Windows	10	11/06/26	11/19/26
8865	Waterproofing	10	11/11/26	11/24/26
8870	Nail Fin Windows	10	11/18/26	12/02/26
8875	Balcony Doors	5	12/03/26	12/09/26
8880	Storefront/Curtainwall	10	11/25/26	12/09/26
8885	Masonry/Brick	10	12/01/26	12/14/26
8890	Hardi & Trim	10	12/11/26	12/24/26
8895	Paint Prep (Caulk, Prime, 1st Coat)	10	12/23/26	01/07/27
8900	Final Paint	10	01/06/27	01/19/27
West Elevation				
8905	Windows	10	11/20/26	12/04/26
8910	Waterproofing	10	11/25/26	12/09/26
8915	Exterior Storefront	10	12/03/26	12/16/26
8920	Storefront Glass	10	12/03/26	12/16/26
8925	Masonry/Brick	10	12/15/26	12/29/26
8930	Hardi & Trim	10	12/28/26	01/11/27
8935	Paint Prep (Caulk, Prime, 1st Coat)	10	01/08/27	01/21/27
8940	Final Paint	10	01/20/27	02/02/27
South Elevation (Left)				
8945	Windows	10	12/07/26	12/18/26
8950	Waterproofing	10	12/10/26	12/23/26
8955	Exterior Storefront	10	12/17/26	12/31/26
8960	Storefront Glass	10	12/17/26	12/31/26
8965	Masonry/Brick	10	12/30/26	01/13/27
8970	Hardi & Trim	10	01/12/27	01/25/27
8975	Paint Prep (Caulk, Prime, 1st Coat)	10	01/22/27	02/04/27
8980	Final Paint	10	02/03/27	02/16/27
Courtyard #1 South Elevation				
8985	Windows	10	12/21/26	01/05/27
8990	Waterproofing	10	12/24/26	01/08/27
8995	Exterior Storefront	10	01/04/27	01/15/27
9000	Storefront Glass	10	01/04/27	01/15/27
9005	Masonry/Brick	10	01/14/27	01/27/27
9010	Hardi & Trim	10	01/26/27	02/08/27
9015	Paint Prep (Caulk, Prime, 1st Coat)	10	02/05/27	02/18/27
9020	Final Paint	10	02/17/27	03/02/27
Courtyard #1 West Elevation				
9025	Windows	10	01/06/27	01/19/27
9030	Waterproofing	10	01/11/27	01/22/27
9035	Exterior Storefront	10	01/18/27	01/29/27

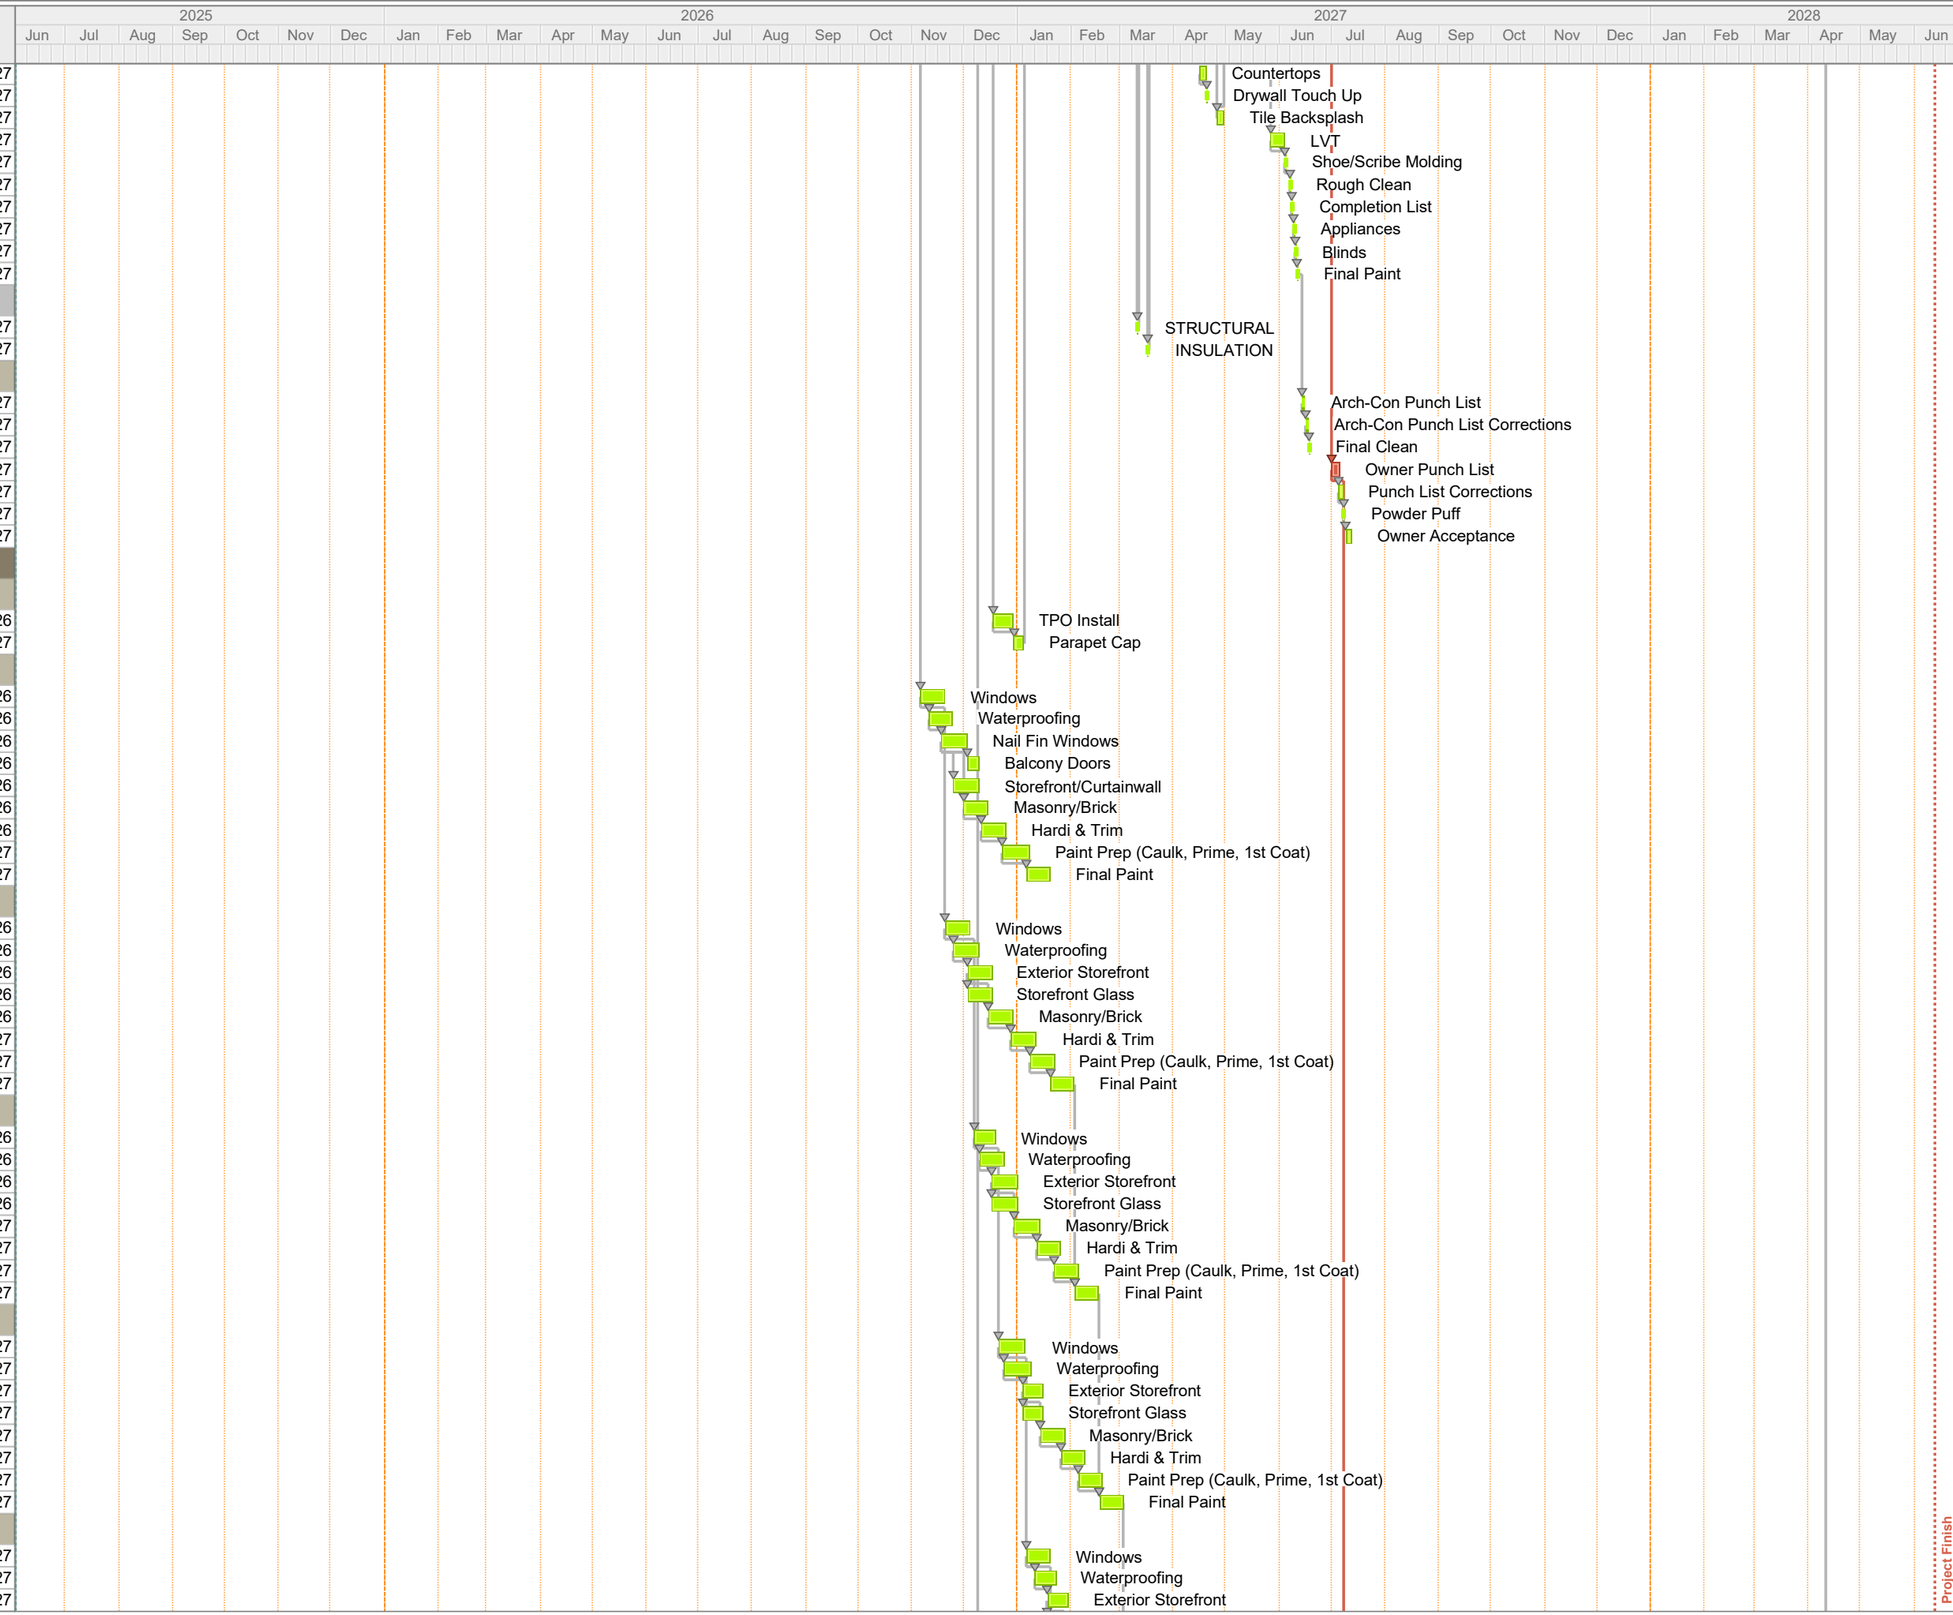

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

9040	Storefront Glass	10	01/18/27	01/29/27
9045	Masonry/Brick	10	01/28/27	02/10/27
9050	Hardi & Trim	10	02/09/27	02/22/27
9055	Paint Prep (Caulk, Prime, 1st Coat)	10	02/19/27	03/04/27
9060	Final Paint	10	03/03/27	03/16/27
Courtyard #2 North Elevation				
9065	Windows	10	01/20/27	02/02/27
9070	Waterproofing	10	01/25/27	02/05/27
9075	Exterior Storefront	10	02/01/27	02/12/27
9080	Storefront Glass	10	02/01/27	02/12/27
9085	Masonry/Brick	10	02/11/27	02/24/27
9090	Hardi & Trim	10	02/23/27	03/08/27
9095	Paint Prep (Caulk, Prime, 1st Coat)	10	03/05/27	03/18/27
9100	Final Paint	10	03/17/27	03/30/27
Courtyard #2 South Elevation				
9105	Windows	10	02/03/27	02/16/27
9110	Waterproofing	10	02/08/27	02/19/27
9115	Exterior Storefront	10	02/15/27	02/26/27
9120	Storefront Glass	10	02/15/27	02/26/27
9125	Masonry/Brick	10	02/25/27	03/10/27
9130	Hardi & Trim	10	03/09/27	03/22/27
9135	Paint Prep (Caulk, Prime, 1st Coat)	10	03/19/27	04/01/27
9140	Final Paint	10	03/31/27	04/13/27
Courtyard #2 West Elevation				
9145	Windows	10	02/17/27	03/02/27
9150	Waterproofing	10	02/22/27	03/05/27
9155	Exterior Storefront	10	03/01/27	03/12/27
9160	Storefront Glass	10	03/01/27	03/12/27
9165	Masonry/Brick	10	03/11/27	03/24/27
9170	Hardi & Trim	10	03/23/27	04/05/27
9175	Paint Prep (Caulk, Prime, 1st Coat)	10	04/02/27	04/15/27
9180	Final Paint	10	04/14/27	04/27/27
Exterior Punch List				
9185	Arch-Con Punch List	3	04/28/27	04/30/27
9190	Arch-Con Punch List Corrections	8	05/03/27	05/12/27
9195	Final Clean	3	05/13/27	05/17/27
9200	Owner Punch List	3	05/18/27	05/20/27
9205	Punch List Corrections	8	05/21/27	06/01/27
9210	Powder Puff	2	06/02/27	06/03/27
9215	Owner Acceptance	3	06/04/27	06/08/27
Stair				
G				
9220	Stair G	30	12/09/26	01/21/27
H				
9225	Stair H	30	12/31/26	02/11/27
Final Inspections				
9230	MECHANICAL	15	07/08/27	07/28/27
9235	ELECTRICAL	15	07/29/27	08/18/27
9240	PLUMBING	15	08/19/27	09/09/27
9245	STRUCTURAL	15	09/10/27	09/30/27
9250	FIRE SPRINKLER & FIRE ALARM	15	10/01/27	10/21/27
9255	EGRESS	15	10/22/27	11/11/27
Systems Verification				
9260	Systems Verification	60	11/12/27	02/04/28
Weather				
9265	Weather Impacts Days	46	02/07/28	04/10/28
Substatial Completion				
9275	Substantial Completion	0		04/10/28
Post Construction				
9280	Punch Work Completion	45	04/11/28	06/12/28

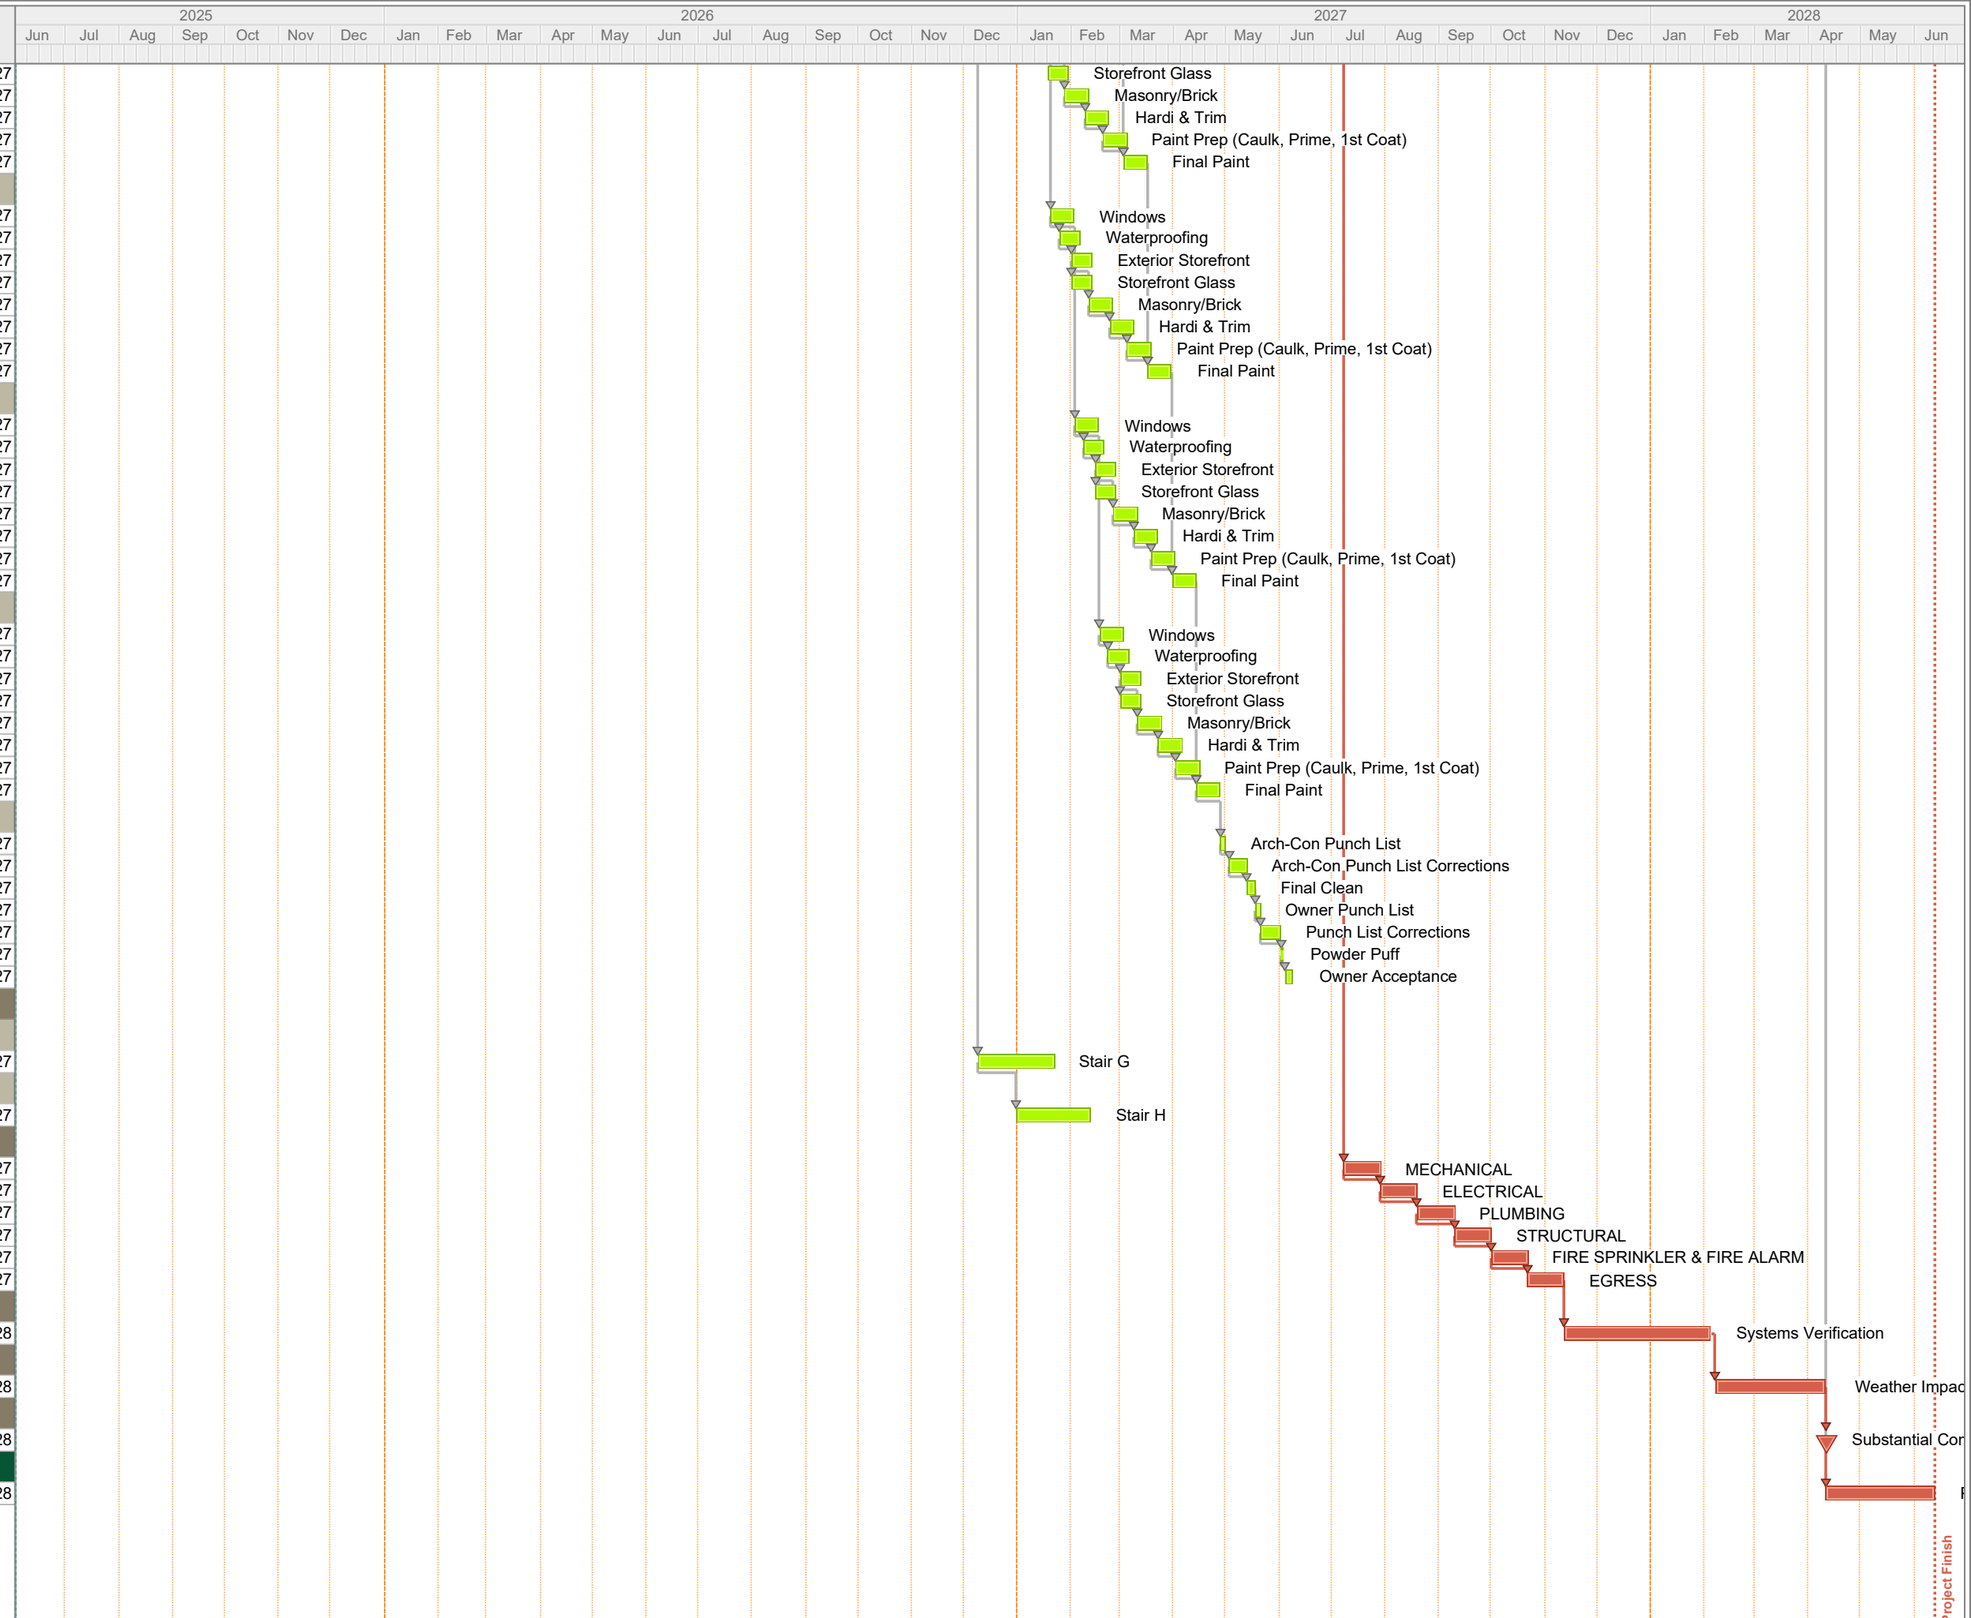

Initials: _____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

EXHIBIT “D”

DRAWING AND SPECIFICATION LOG

[See Attached]

Initials: _____

Docusign Envelope ID: 1B3BE5C2-E9FE-423A-BBE5-9E2951C802C1

Arch-Con Corporation

Initials: _____

Printed on Thu Jan 29, 2026 at 01:45 pm CST

Job #: 2507007 The Silos
1235 Shadowdale Drive
Houston, Texas 77043

Current Drawings

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
General					
G000	COVER PAGE	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
G000a	COVER PAGE - CAFE	1	11/21/2025	01/12/2026	Addendum 005 (11/21/25)
G001	SHEET INDEX	2	08/15/2025	01/27/2026	Addendum 003 (08/15/25)
G001a	SHEET INDEX - (FOUNDATION PERMIT)	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G001b	SHEET INDEX - CAFE	1	11/21/2025	01/23/2026	Addendum 005 (11/21/25)
G002	TABULATIONS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G003a	CODE ANALYSIS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G003b	CODE ANALYSIS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G003c	CODE ANALYSIS AND LIFE SAFETY - CAFE	1	11/21/2025	01/12/2026	Addendum 005 (11/21/25)
G004	GENERAL NOTES, ABBREVIATIONS AND SYMBOLS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G005	COMECHECK COMPLIANT CERTIFICATE	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G006	ADDRESS PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G008a	BUILDING AREA PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G008b	BUILDING AREA PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G008c	BUILDING AREA PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G008d	BUILDING AREA PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G009	PHASING PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G011	LIFE SAFETY PLAN	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
G012	LIFE SAFETY PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G013	LIFE SAFETY PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G014	LIFE SAFETY PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G021	LEVEL 1 ACCESSIBLE ROUTE PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)

Arch-Con Corporation

Initials: _____

Printed on Thu Jan 29, 2026 at 01:45 pm CST

Job #: 2507007 The Silos
1235 Shadowdale Drive
Houston, Texas 77043

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
G025	LOADING AND REFUSE PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G030	ASSEMBLIES 0-HR WALLS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G030a	ASSEMBLIES - CAFE	1	11/21/2025	01/12/2026	Addendum 005 (11/21/25)
G031	ASSEMBLIES 1-HR WALLS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G031a	ASSEMBLIES 1-HR WALLS (CAFE)	0	11/21/2025	01/12/2026	Addendum 005 (11/21/25)
G032	ASSEMBLIES FIRE BARRIERS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G033a	ASSEMBLIES 2-HR EXT. WALLS & AREA SEPARATION WALLS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G033b	ASSEMBLIES 0-HR/1-HR EXT. WALLS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G034	ASSEMBLIES FLR/CLG L546	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G035	ASSEMBLIES FLR/CLG TABLE	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G036	ASSEMBLIES FLR/CLG FW1B/FC2	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G036a	ASSEMBLIES FLR/CLG P545	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G037	ASSEMBLIES BEAM/COLUMN U263/Y624	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G038	ASSEMBLIES FLR/CLG L521	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G050	FIRESTOP SYSTEMS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G051	FIRESTOP SYSTEMS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G052	FIRESTOP SYSTEMS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G053	FIRESTOP SYSTEMS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G054	FIRESTOP SYSTEMS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G060	COH SIGNAGE	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G061	SIGNAGE	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G062	SIGNAGE	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
G063	SIGNAGE	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)

Arch-Con Corporation

Initials: _____

Printed on Thu Jan 29, 2026 at 01:45 pm CST

Job #: 2507007 The Silos
1235 Shadowdale Drive
Houston, Texas 77043

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
Architectural					
A100	SITE PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A100a	SITE PLAN - CAFE	0	09/16/2025	09/23/2025	Cafe IFC (09/16/25)
A101	CAFE FLOOR PLAN AND RCP	1	11/21/2025	01/12/2026	Addendum 005 (11/21/25)
A102	CAFE EQUIPMENT PLAN AND POWER INTENT PLAN	0	09/16/2025	09/23/2025	Cafe IFC (09/16/25)
A110	DIMENSION CONTROL PLAN	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
A110a	SEGMENT A PARTIAL DCP PLAN	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
A110b	SEGMENT B PARTIAL DCP PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A110c	SEGMENT C PARTIAL DCP PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A111	LEVEL 1 OVERALL PLAN	2	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
A111a	LEVEL 1 SEGMENT A PARTIAL FLOOR PLAN	3	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
A111b	LEVEL 1 SEGMENT B PARTIAL FLOOR PLAN	3	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
A111c	LEVEL 1 SEGMENT C PARTIAL FLOOR PLAN	3	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
A112	LEVEL 2 OVERALL PLAN	2	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
A112a	LEVEL 2 SEGMENT A PARTIAL FLOOR PLAN	3	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
A112b	LEVEL 2 SEGMENT B PARTIAL FLOOR PLAN	2	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
A112c	LEVEL 2 SEGMENT C PARTIAL FLOOR PLAN	2	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
A113	LEVEL 3-5 OVERALL PLAN	2	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
A113a	LEVEL 3-5 SEGMENT A PARTIAL FLOOR PLAN	3	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
A113b	LEVEL 3-5 SEGMENT B PARTIAL FLOOR PLAN	2	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
A113c	LEVEL 3-5 SEGMENT C PARTIAL FLOOR PLAN	2	10/31/2025	01/27/2026	Addendum 004 (10/31/25)
A116	ROOF OVERALL PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A116a	ROOF SEGMENT A PARTIAL PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A116b	ROOF SEGMENT B PARTIAL PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A116c	ROOF SEGMENT C PARTIAL PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A140	GARAGE DIMENSION CONTROL PLAN	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
A141	LEVEL 1 GARAGE FLOOR PLAN	3	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
A142	LEVELS 2 & 3 GARAGE FLOOR PLAN	3	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
A143	LEVELS 4 & 5 GARAGE FLOOR PLAN	3	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
A144	LEVEL 6 GARAGE FLOOR PLAN	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
A145	GARAGE ROOF PLAN	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
A151	LEVEL 1 REFLECTED CEILING PLANS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)

Arch-Con Corporation

Initials: _____

Printed on Thu Jan 29, 2026 at 01:45 pm CST

Job #: 2507007 The Silos
1235 Shadowdale Drive
Houston, Texas 77043

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
A152	LEVEL 2 REFLECTED CEILING PLANS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A153	LEVEL 3-4 REFLECTED CEILING PLANS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A154	LEVEL 5 REFLECTED CEILING PLANS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A200	OVERALL NORTH & SOUTH EXTERIOR ELEVATIONS	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
A201	OVERALL EAST & WEST EXTERIOR ELEVATION	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
A202	ENLARGED BUILDING ELEVATIONS	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
A210	3D VIEWS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A211	3D VIEWS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A251	INTERIOR ELEVATIONS RESTROOMS	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
A252	INTERIOR ELEVATIONS MAILROOM	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A253	INTERIOR ELEVATIONS CLUB - LOUNGE - OFFICE	2	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
A254	INTERIOR ELEVATIONS CLUB - LOUNGE - OFFICE	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
A255	INTERIOR ELEVATIONS GARAGE MAINTENANCE RM	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
A300	BUILDING SECTIONS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A301	BUILDING SECTIONS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A303	GARAGE SECTIONS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A310	WALL SECTIONS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A311	WALL SECTIONS	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
A312	WALL SECTIONS	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
A313	WALL SECTIONS	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
A314	WALL SECTIONS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A315	WALL SECTIONS	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
A316	WALL SECTIONS	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
A320	BLDG. STAIR A PLANS & SECTIONS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A321	BLDG. STAIR B PLANS & SECTIONS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A322	BLDG. STAIR C PLANS & SECTIONS	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
A323	BLDG. STAIR D PLANS & SECTIONS	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
A324	BLDG. STAIR E PLANS & SECTIONS	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
A325	BLDG. STAIR F PLANS & SECTIONS	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)

Arch-Con Corporation

Initials: _____

Printed on Thu Jan 29, 2026 at 01:45 pm CST

Job #: 2507007 The Silos
1235 Shadowdale Drive
Houston, Texas 77043

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
A326	BLDG. STAIR G PLANS & SECTIONS	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
A327	BLDG. STAIR H PLANS & SECTIONS	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
A328	ELEVATOR A, B & C PLANS & SECTIONS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A329	TRASH RM ENLARGED PLANS AND SECTIONS	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
A330	MECHANICAL VENT ENLARGED PLANS AND SECTIONS	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
A401	UNIT PLAN A1 & A2	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
A401a	ENLARGED PLANS UNIT A1	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
A401b	ENLARGED PLANS UNIT A2	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
A402	UNIT PLAN A3 & A4	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
A402a	ENLARGED PLANS UNIT A3	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
A402b	ENLARGED PLANS UNIT A4	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
A403	UNIT PLAN A5	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
A403a	ENLARGED PLANS UNIT A5	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
A404	UNIT PLAN B1 & B2	3	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
A404a	ENLARGED PLANS UNIT B1	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
A404a.1	ENLARGED PLANS UNIT B1	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
A404b	ENLARGED PLANS UNIT B2	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
A404b.1	ENLARGED PLANS UNIT B2	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
A405	UNIT PLAN C1	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
A405a	ENLARGED PLANS UNIT C1	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
A405a.1	ENLARGED PLANS UNIT C1	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
A450	ENLARGED FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A450a	ENLARGED FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A450b	ENLARGED FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A450c	ENLARGED FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A451	ENLARGED AMENITY REFLECTED CEILING PLANS	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
A505	DETAILS - EXTERIOR WALL FINISH (FIBER CEMENT)	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A506	DETAILS - EXTERIOR WALL FINISH (BRICK) 24054	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A507	DETAILS - EXTERIOR WALL FINISH (METAL PANEL)	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A508	DETAILS - EXTERIOR WALL FINISH (STONE)	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A511	DETAILS - SEPARATION WALLS (1 HOUR)	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)

Arch-Con Corporation

Initials: _____

Printed on Thu Jan 29, 2026 at 01:45 pm CST

Job #: 2507007 The Silos
1235 Shadowdale Drive
Houston, Texas 77043

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
A512	DETAILS - SEPARATION WALLS (2 HOUR)	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A513	DETAILS - SEPARATION WALLS (3 HOUR)	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A520	DETAILS - PARAPET	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A521	DETAILS - ROOF (LOW SLOPE)	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A522	DETAILS - GARAGE GENERAL	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A525	DETAILS - STAIR, RAILS & RAMP	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A526	DETAILS - STAIR TREADS (BLDG W/ ELEVATORS)	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A531	DETAILS - CORRIDOR	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A531a	DETAILS - GENERAL - CAFE	1	11/21/2025	01/12/2026	Addendum 005 (11/21/25)
A532a	UNIT & COMMON AREA DETAILS (FHA/ADA)	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A536	DETAILS - FLOOR FINISH TRANSITION	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A540	DETAILS - BALCONY	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A540a	DETAILS - BALCONY	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A541	DETAILS - ELEVATORS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A551	DETAILS - WINDOW	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A552	DETAILS - STOREFRONT	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A561	DETAILS - EXTERIOR DOOR	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
A562	DETAILS - INTERIOR DOOR	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A563	DETAILS - GARAGE DOOR	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A570	MILLWORK DETAILS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A600	DOOR SCHEDULE AND ELEVATIONS	3	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
A600a	DOOR AND WINDOW SCHEDULES AND ELEVATIONS - CAFE	1	11/21/2025	01/12/2026	Addendum 005 (11/21/25)
A601	DOOR SCHEDULE AND ELEVATIONS	3	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
A602a	DOOR HARDWARE SCHEDULE	1	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
A602b	DOOR HARDWARE SCHEDULE	1	10/31/2025	01/27/2026	Addendum 004 (10/31/25)

Arch-Con Corporation

Initials: _____

Printed on Thu Jan 29, 2026 at 01:45 pm CST

Job #: 2507007 The Silos
1235 Shadowdale Drive
Houston, Texas 77043

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
A602c	DOOR HARDWARE SCHEDULE	1	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
A603	WINDOW SCHEDULE AND ELEVATION	3	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
A604	AWNING SCHEDULE AND DETAILS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
A900	MOCKUP (DRAFT)	0	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
A901a	INTERIOR RENDERINGS - CAFE	0	09/16/2025	09/23/2025	Cafe IFC (09/16/25)
Interior					
ID000	ID NOTES AND INFORMATION	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
ID100	AMENITY AREA OVERALL FLOOR PLAN - LEVEL 1	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
ID100a	ENLARGED FLOOR PLANS - LEVEL 1	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
ID100b	ENLARGED FLOOR PLANS - LEVEL 1	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
ID101	AMENITY AREA OVERALL FLOOR PLAN - LEVEL 2	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
ID101a	ENLARGED FLOOR PLANS - LEVEL 2	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
ID101c	CAFE FLOOR PLAN AND RCP	0	09/16/2025	01/23/2026	Cafe IFC (09/16/25)
ID111c	CAFE FINISH AND FURNITURE PLAN	1	11/21/2025	01/23/2026	Addendum 005 (11/21/25)
ID120	AMENITY AREA OVERALL FINISH PLAN - LEVEL 1	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
ID120a	ENLARGED FINISH PLAN - LEVEL 1	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
ID120b	ENLARGED FINISH PLANS - LEVEL 1	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
ID121	AMENITY AREA OVERALL FINISH PLAN - LEVEL 2	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
ID121a	ENLARGED FINISH PLANS - LEVEL 2	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
ID122	TYP. LEVELS 3-5 UNIT OVERALL FINISH PLAN	0	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
ID130	AMENITY AREA OVERALL RCP - LEVEL 1	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
ID130a	ENLARGED RCP - LEVEL 1	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
ID130b	ENLARGED RCP - LEVEL 1	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
ID131	AMENITY AREA OVERALL RCP - LEVEL 2	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
ID131a	ENLARGED RCP - LEVEL 2	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
ID140	ENLARGED FURNITURE PLANS - LEVEL 1	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
ID141	ENLARGED FURNITURE PLANS - LEVEL 1	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
ID150	UNIT FLOOR PLANS	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
ID151	UNIT FLOOR PLANS	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)

Arch-Con Corporation

Initials: _____

Printed on Thu Jan 29, 2026 at 01:45 pm CST

Job #: 2507007 The Silos
1235 Shadowdale Drive
Houston, Texas 77043

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
ID152	UNIT FLOOR PLANS	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
ID153	UNIT FLOOR PLANS	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
ID155	ENLARGED UNIT BATHROOM AND KITCHEN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
ID156	ENLARGED UNIT BATHROOM AND KITCHEN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
ID200	INTERIOR ELEVATIONS	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
ID201	INTERIOR ELEVATIONS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
ID202	INTERIOR ELEVATIONS	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
ID203	INTERIOR ELEVATIONS	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
ID204	INTERIOR ELEVATIONS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
ID205	INTERIOR ELEVATIONS	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
ID206	INTERIOR ELEVATIONS	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
ID260c	CAFE INTERIOR ELEVATIONS	0	09/16/2025	01/23/2026	Cafe IFC (09/16/25)
ID261c	CAFE INTERIOR ELEVATIONS	0	09/16/2025	01/23/2026	Cafe IFC (09/16/25)
ID310	UNIT INTERIOR ELEVATIONS	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
ID311	UNIT INTERIOR ELEVATIONS	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
ID312	UNIT INTERIOR ELEVATIONS	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
ID313	UNIT INTERIOR ELEVATIONS	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
ID314	UNIT INTERIOR ELEVATIONS	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
ID500	MILLWORK DETAILS	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
ID500c	CAFE MILLWORK DETAILS	0	09/16/2025	01/23/2026	Cafe IFC (09/16/25)
ID501	MILLWORK DETAILS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
ID501c	CAFE MILLWORK DETAILS	0	09/16/2025	01/23/2026	Cafe IFC (09/16/25)
ID502	MILLWORK DETAILS	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
ID503	MILLWORK DETAILS	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
ID504	ENLARGED DETAILS	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
ID510	ENLARGED DETAILS	3	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
ID510c	CAFE ENLARGED DETAILS	1	10/31/2025	01/23/2026	Addendum 004 (10/31/25)
ID600	DOOR SCHEDULE	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
ID700	INTERIOR SCHEDULES	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
ID700c	CAFE INTERIOR SCHEDULE	1	11/21/2025	01/23/2026	Addendum 005 (11/21/25)
ID701	INTERIOR SCHEDULES	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
ID702	INTERIOR SCHEDULES	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
ID703	INTERIOR SCHEDULES	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)

Arch-Con Corporation

Initials: _____

Printed on Thu Jan 29, 2026 at 01:45 pm CST

Job #: 2507007 The Silos
1235 Shadowdale Drive
Houston, Texas 77043

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
ID704	INTERIOR SCHEDULES	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
ID705	UNIT OPTION SCHEDULE	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
Structural					
S000	COVER SHEET	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S001	GENERAL NOTES	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S110A	PARTIAL BUILDING FOUNDATION PLAN SECTION A	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
S110AS	STEEL PLACEMENT PLAN SECTION A	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
S110B	PARTIAL BUILDING FOUNDATION PLAN SECTION B	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S110C	PARTIAL BUILDING FOUNDATION PLAN SECTION C	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S111A	PARTIAL 1ST FLOOR BUILDING SHEAR WALL & CORRIDOR FRAMING PLAN SECTION A	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S111B	PARTIAL 1ST FLOOR BUILDING SHEAR WALL & CORRIDOR FRAMING PLAN SECTION A	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S111C	PARTIAL 1ST FLOOR BUILDING SHEAR WALL & CORRIDOR FRAMING PLAN SECTION A	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S112A	PARTIAL 2ND FLOOR BUILDING SHEAR WALL & CORRIDOR FRAMING PLAN SECTION A	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S112B	PARTIAL 2ND FLOOR BUILDING SHEAR WALL & CORRIDOR FRAMING PLAN SECTION A	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S112C	PARTIAL 2ND FLOOR BUILDING SHEAR WALL & CORRIDOR FRAMING PLAN SECTION A	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S113A	PARTIAL 3RD FLOOR BUILDING SHEAR WALL & CORRIDOR FRAMING PLAN SECTION A	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S113B	PARTIAL 3RD FLOOR BUILDING SHEAR WALL & CORRIDOR FRAMING PLAN SECTION A	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S113C	PARTIAL 3RD FLOOR BUILDING SHEAR WALL & CORRIDOR FRAMING PLAN SECTION A	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S114A	PARTIAL 4TH FLOOR BUILDING SHEAR WALL & CORRIDOR FRAMING PLAN SECTION A	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S114B	PARTIAL 4TH FLOOR BUILDING SHEAR WALL & CORRIDOR FRAMING PLAN SECTION A	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S114C	PARTIAL 4TH FLOOR BUILDING SHEAR WALL & CORRIDOR FRAMING PLAN SECTION A	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S115A	PARTIAL 5TH FLOOR BUILDING SHEAR WALL & CORRIDOR FRAMING PLAN SECTION A	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S115B	PARTIAL 5TH FLOOR BUILDING SHEAR WALL & CORRIDOR FRAMING PLAN SECTION A	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S115C	PARTIAL 5TH FLOOR BUILDING SHEAR WALL & CORRIDOR FRAMING PLAN SECTION A	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S116A	PARTIAL BUILDING ROOF FRAMING PLAN SECTION A	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/

Arch-Con Corporation

Initials: _____

Printed on Thu Jan 29, 2026 at 01:45 pm CST

Job #: 2507007 The Silos
1235 Shadowdale Drive
Houston, Texas 77043

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
					25)
S116B	PARTIAL BUILDING ROOF FRAMING PLAN SECTION B	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S116C	PARTIAL BUILDING ROOF FRAMING PLAN SECTION C	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S141	GARAGE FOUNDATION PLAN	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
S400	UNIT FRAMING SCHEDULES	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S401	UNIT PLAN A1 & A2	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S402	UNIT PLAN A3 & A4	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S403	UNIT PLAN A5	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S404	UNIT PLAN B1 & B2	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S405	UNIT PLAN C1	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S450	2ND FLOOR CLUB & FITNESS FRAMING PLAN	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
S451	3RD FLOOR CLUB & FITNESS FRAMING PLAN	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
S452	4TH & 5TH FLOOR CLUB & FITNESS FRAMING PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S460	CAFE FRAMING PLAN	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
S500	SCHEDULES	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S501	FOUNDATION SECTIONS & DETAILS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S502	FOUNDATION SECTIONS & DETAILS	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
S601	FLOOR FRAMING SECTIONS & DETAILS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S602	FLOOR FRAMING SECTIONS & DETAILS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S603	FLOOR FRAMING SECTIONS & DETAILS	0	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
S701	BLDG SECTIONS & SHEAR WALL ELEVATOINS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S702	SHEAR WALL FRAMING DETAILS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S801	ROOF FRAMING DETAILS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S802	ROOF FRAMING DETAILS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S901	GARAGE FOUNDATION DETAILS	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
S902	GARAGE FOUNDATION DETAILS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/

Arch-Con Corporation

Initials: _____

Printed on Thu Jan 29, 2026 at 01:45 pm CST

Job #: 2507007 The Silos
1235 Shadowdale Drive
Houston, Texas 77043

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
					25)
S903	GARAGE FOUNDATION DETAILS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
S904	GARAGE FOUNDATION DETAILS	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
Fire Protection					
FP000	NOTES, LEGENDS, SCHEDULES & DETAILS - FIRE PROTECTION	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
FP001	DETAILS - FIRE PROTECTION	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
FP002	DETAILS - FIRE PROTECTION	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
FP100	SITE PLAN - FIRE PROTECTION	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
FP111	LEVEL 1 FLOOR PLAN - FIRE PROTECTION	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
FP112	LEVEL 2 FLOOR PLAN - FIRE PROTECTION	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
FP113	LEVELS 3-4 FLOOR PLAN - FIRE PROTECTION	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
FP114	LEVEL 5 FLOOR PLAN - FIRE PROTECTION	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
FP115	ROOF PLAN - FIRE PROTECTION	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
FP201	RISERS - FIRE PROTECTION	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
Plumbing					
P000	GENERAL NOTES, LEGENDS, AND SYMBOLS - PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P001	SCHEDULES - PLUMBING	2	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
P002	DETAILS - PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P.2-000	GENERAL NOTES, SYMBOLS & SCHEDULES - PLUMBING	0	09/16/2025	09/23/2025	Cafe IFC (09/16/25)
P.2-001	DETAILS - PLUMBING	0	09/16/2025	09/23/2025	Cafe IFC (09/16/25)
P.2-100	FLOOR PLAN - PLUMBING	0	11/21/2025	01/12/2026	Addendum 005 (11/21/25)
P.2-101	CAFE FLOOR PLAN - PLUMBING	1	11/21/2025	01/12/2026	Addendum 005 (11/21/25)
P.2-201	RISERS - PLUMBING	0	11/21/2025	01/12/2026	Addendum 005 (11/21/25)
P003	DETAILS - PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P004	DETAILS - PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P005	DETAILS - PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P006	DETAILS - PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)

Arch-Con Corporation

Initials: _____

Printed on Thu Jan 29, 2026 at 01:45 pm CST

Job #: 2507007 The Silos
1235 Shadowdale Drive
Houston, Texas 77043

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
P007	DETAILS - PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P100	SITE PLAN - PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P110	LEVEL 1 OVERALL PLAN - PLUMBING	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
P110a	LEVEL 1 SEGMENT A PARTIAL FLOOR PLAN - PLUMBING	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
P110b	LEVEL 1 SEGMENT B PARTIAL FLOOR PLAN - PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P110c	LEVEL 1 SEGMENT C PARTIAL FLOOR PLAN - PLUMBING	1	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
P111	LEVEL 1 OVERALL PLAN - OVERHEAD PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P111a	LEVEL 1 SEGMENT A PARTIAL FLOOR PLAN - OVERHEAD PLUMBING	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
P111b	LEVEL 1 SEGMENT B PARTIAL FLOOR PLAN - OVERHEAD PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P111c	LEVEL 1 SEGMENT C PARTIAL FLOOR PLAN - OVERHEAD PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P112	LEVEL 2 OVERALL PLAN - PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P112a	LEVEL 2 SEGMENT A PARTIAL FLOOR PLAN - PLUMBING	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
P112b	LEVEL 2 SEGMENT B PARTIAL FLOOR PLAN - PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P112c	LEVEL 2 SEGMENT C PARTIAL FLOOR PLAN - PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P113	LEVELS 3-5 OVERALL PLAN - PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P113a	LEVELS 3-5 SEGMENT A PARTIAL FLOOR PLAN - PLUMBING	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
P113b	LEVELS 3-5 SEGMENT B PARTIAL FLOOR PLAN - PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P113c	LEVELS 3-5 SEGMENT C PARTIAL FLOOR PLAN - PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P114	LEVEL 4 OVERALL PLAN - OVERHEAD WATER	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P114a	LEVEL 4 SEGMENT A PARTIAL FLOOR PLAN - WATER	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P114b	LEVEL 4 SEGMENT B PARTIAL FLOOR PLAN - WATER	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P114c	LEVEL 4 SEGMENT C PARTIAL FLOOR PLAN - WATER	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P115	LEVEL 5 OVERALL PLAN - OVERHEAD PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P115a	LEVEL 5 SEGMENT A PARTIAL FLOOR PLAN - OVERHEAD PLUMBING	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
P115b	LEVEL 5 SEGMENT B PARTIAL FLOOR PLAN - OVERHEAD PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)

Arch-Con Corporation

Initials: _____

Printed on Thu Jan 29, 2026 at 01:45 pm CST

Job #: 2507007 The Silos
1235 Shadowdale Drive
Houston, Texas 77043

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
P115c	LEVEL 5 SEGMENT C PARTIAL FLOOR PLAN - OVERHEAD PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P116	ROOF OVERALL PLAN - PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P116a	ROOF SEGMENT A PARTIAL FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P116b	ROOF SEGMENT B PARTIAL FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P116c	ROOF SEGMENT C PARTIAL FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P141	LEVEL 1 GARAGE FLOOR PLAN - PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P142	LEVELS 2-3 GARAGE FLOOR PLAN - PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P143	LEVELS 4-5 GARAGE FLOOR PLAN - PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P144	LEVELS 6-ROOF GARAGE FLOOR PLAN - PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P400	UNIT PLANS - PLUMBING	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
P401	UNIT PLANS - PLUMBING	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
P402	UNIT PLANS - PLUMBING	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
P450	ENLARGED FLOOR PLANS - PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P451	ENLARGED FLOOR PLANS - PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P601	RISERS - PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P602	RISERS - PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P603	RISERS - PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P604	RISERS - PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
P605	RISERS - PLUMBING	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
Mechanical					
M000	GENERAL NOTES, LEGEND, AND SYMBOLS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
M001	NOTES	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
M002	SCHEDULES	1	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
M003	SCHEDULES	1	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
M004	CALCULATIONS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)

Arch-Con Corporation

Initials: _____

Printed on Thu Jan 29, 2026 at 01:45 pm CST

Job #: 2507007 The Silos
1235 Shadowdale Drive
Houston, Texas 77043

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
M005	DETAILS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
M006	DETAILS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
M007	DETAILS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
M008	DETAILS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
M111	LEVEL 1 OVERALL PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
M111a	LEVEL 1 SEGMENT A PARTIAL FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
M111b	LEVEL 1 SEGMENT B PARTIAL FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
M111c	LEVEL 1 SEGMENT C PARTIAL FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
M112	LEVEL 2 OVERALL PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
M112a	LEVEL 2 SEGMENT A PARTIAL FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
M112b	LEVEL 2 SEGMENT B PARTIAL FLOOR PLAN	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
M112c	LEVEL 2 SEGMENT C PARTIAL FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
M113	LEVELS 3-5 OVERALL PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
M113a	LEVELS 3-5 SEGMENT A PARTIAL FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
M113b	LEVELS 3-5 SEGMENT B PARTIAL FLOOR PLAN	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
M113c	LEVELS 3-5 SEGMENT C PARTIAL FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
M114	ROOF OVERALL PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
M114a	ROOF SEGMENT A PARTIAL FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
M114b	ROOF SEGMENT B PARTIAL FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
M114c	ROOF SEGMENT C PARTIAL FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
M141	LEVELS 1 & 2 GARAGE FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
M142	LEVELS 3 & 4 GARAGE FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
M143	LEVEL 5 GARAGE FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)

Arch-Con Corporation

Initials: _____

Printed on Thu Jan 29, 2026 at 01:45 pm CST

Job #: 2507007 The Silos
1235 Shadowdale Drive
Houston, Texas 77043

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
M144	LEVEL 6 GARAGE FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
M400	UNIT PLANS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
M401	UNIT PLANS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
M402	UNIT PLANS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
M450	ENLARGED FLOOR PLANS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
M451	ENLARGED FLOOR PLANS	1	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
M452	ENLARGED FLOOR PLANS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
M500	GENERAL NOTES, LEGEND, AND SYMBOLS	0	09/16/2025	09/23/2025	Cafe IFC (09/16/25)
M501	NOTES	0	09/16/2025	09/23/2025	Cafe IFC (09/16/25)
M502	SCHEDULES & CALCS	0	09/16/2025	09/23/2025	Cafe IFC (09/16/25)
M503	DETAILS	0	09/16/2025	09/23/2025	Cafe IFC (09/16/25)
M510	CAFE FLOOR & ROOF PLAN	0	09/16/2025	09/23/2025	Cafe IFC (09/16/25)
Electrical					
E000	LEGENDS & NOTES - ELECTRICAL	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
E001	NOTES & DETAILS - ELECTRICAL	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
E002	NOTES & DETAILS - ELECTRICAL	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
E003	NOTES & DETAILS - ELECTRICAL	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
E004	RESIDENTIAL RISER DIAGRAM - ELECTRICAL	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
E005	HOUSE RISER DIAGRAM - ELECTRICAL	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
E006	RESIDENTIAL CALCS - ELECTRICAL	1	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
E007	RESIDENTIAL CALCS - ELECTRICAL	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
E008	HOUSE CALCS - ELECTRICAL	2	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
E009	HOUSE CALCS - ELECTRICAL	2	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
E010	HOUSE CALCS - ELECTRICAL	2	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
E011	HOUSE CALCS - ELECTRICAL	2	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
E100	SITE PLAN - ELECTRICAL	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
E111	LEVEL 1 OVERALL PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
E111a	LEVEL 1 SEGMENT A PARTIAL FLOOR PLAN	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
E111b	LEVEL 1 SEGMENT B PARTIAL FLOOR PLAN	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)

Arch-Con Corporation

Initials: _____

Printed on Thu Jan 29, 2026 at 01:45 pm CST

Job #: 2507007 The Silos
1235 Shadowdale Drive
Houston, Texas 77043

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
E111c	LEVEL 1 SEGMENT C PARTIAL FLOOR PLAN	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
E112	LEVEL 2 OVERALL PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
E112a	LEVEL 2 SEGMENT A PARTIAL FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
E112b	LEVEL 2 SEGMENT B PARTIAL FLOOR PLAN	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
E112c	LEVEL 2 SEGMENT C PARTIAL FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
E113	LEVELS 3-5 OVERALL PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
E113a	LEVELS 3-5 SEGMENT A PARTIAL FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
E113b	LEVELS 3-5 SEGMENT B PARTIAL FLOOR PLAN	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
E113c	LEVELS 3-5 SEGMENT C PARTIAL FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
E114	ROOF OVERALL PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
E114a	ROOF SEGMENT A PARTIAL FLOOR PLAN	1	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
E114b	ROOF SEGMENT B PARTIAL FLOOR PLAN	1	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
E114c	ROOF SEGMENT C PARTIAL FLOOR PLAN	1	10/31/2025	01/27/2026	Addendum 004 (10/31/25)
E141	LEVEL 1 GARAGE FLOOR PLAN	3	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
E142	LEVEL 2 GARAGE FLOOR PLAN	3	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
E143	LEVELS 3-5 GARAGE FLOOR PLAN	3	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
E144	LEVEL 6 GARAGE FLOOR PLAN	3	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
E151	LEVEL 1 OVERALL REFLECTED CEILING PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
E151a	LEVEL 1 SEGMENT A REFLECTED CEILING PLAN	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
E151b	LEVEL 1 SEGMENT B REFLECTED CEILING PLAN	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
E151c	LEVEL 1 SEGMENT C REFLECTED CEILING PLAN	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
E152	LEVEL 2 OVERALL REFLECTED CEILING PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
E152a	LEVEL 2 SEGMENT A REFLECTED CEILING PLAN	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
E152b	LEVEL 2 SEGMENT B REFLECTED CEILING PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
E152c	LEVEL 2 SEGMENT C REFLECTED CEILING PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
E153	LEVELS 3-5 OVERALL REFLECTED CEILING PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
E153a	LEVELS 3-5 SEGMENT A REFLECTED CEILING PLAN	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
E153b	LEVELS 3-5 SEGMENT B REFLECTED CEILING PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
E153c	LEVELS 3-5 SEGMENT C REFLECTED CEILING PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/

Arch-Con Corporation

Initials: _____

Printed on Thu Jan 29, 2026 at 01:45 pm CST

Job #: 2507007 The Silos
1235 Shadowdale Drive
Houston, Texas 77043

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
					25)
E400	UNIT PLANS - ELECTRICAL	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
E401	UNIT PLANS - ELECTRICAL	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
E402	UNIT PLANS - ELECTRICAL	2	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
E450	ENLARGED FLOOR PLANS	2	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
E451	ENLARGED FLOOR PLANS	1	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
E452	ENLARGED FLOOR PLANS	1	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
E453	ENLARGED REFLECTED CEILING PLANS	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
E454	ENLARGED REFLECTED CEILING PLANS	2	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
E455	ENLARGED REFLECTED CEILING PLANS	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
E500	LEGEND & NOTES - CAFE	0	09/16/2025	09/23/2025	Cafe IFC (09/16/25)
E501	DETAILS & NOTES - CAFE	0	09/16/2025	09/23/2025	Cafe IFC (09/16/25)
E502	REFERENCE RISER DIAGRAM & SCHEDULE - CAFE	0	09/16/2025	09/23/2025	Cafe IFC (09/16/25)
E510	CAFE FLOOR PLAN - ELECTRICAL	0	09/16/2025	09/23/2025	Cafe IFC (09/16/25)
E511	CAFE ROOF PLAN - ELECTRICAL	1	11/21/2025	01/12/2026	Addendum 005 (11/21/25)
Telecommunications					
T000	LEGENDS & NOTES - TELECOM	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
T001	COMMUNICATIONS DETAILS - TELECOM	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
T002	COMMUNICATIONS DETAILS - TELECOM	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
T003	COMMUNICATIONS DETAILS - TELECOM	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
T004	COMMUNICATIONS DETAILS - TELECOM	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
T005	ACCESS CONTROL DETAILS - TELECOM	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
T006	SECURITY DETAILS - TELECOM	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
T007	TELE-ENTRY DETAILS - TELECOM	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
T008	TV MOUNT DETAILS - TELECOM	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
T009	SURGE PROTECTION DETAILS - TELECOM	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
T020	CONDUIT RISER - TELECOM	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
T021	GROUNDING RISER DIAGRAM - TELECOM	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
T022	FIBER RISER DIAGRAM - TELECOM	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)

Arch-Con Corporation

Initials: _____

Printed on Thu Jan 29, 2026 at 01:45 pm CST

Job #: 2507007 The Silos
1235 Shadowdale Drive
Houston, Texas 77043

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
T023	COAXIAL RISER DIAGRAM - TELECOM	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
T024	COPPER RISER DIAGRAM - TELECOM	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
T100	SITE PLAN - TELECOM	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
T111	LEVEL 1 OVERALL PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
T111a	LEVEL 1 SEGMENT A PARTIAL FLOOR PLAN	2	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
T111b	LEVEL 1 SEGMENT B PARTIAL FLOOR PLAN	2	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
T111c	LEVEL 1 SEGMENT C PARTIAL FLOOR PLAN	2	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
T112	LEVEL 2 OVERALL PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
T112a	LEVEL 2 SEGMENT A PARTIAL FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
T112b	LEVEL 2 SEGMENT B PARTIAL FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
T112c	LEVEL 2 SEGMENT C PARTIAL FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
T113	LEVELS 3-5 OVERALL PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
T113a	LEVELS 3-5 SEGMENT A PARTIAL FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
T113b	LEVELS 3-5 SEGMENT B PARTIAL FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
T113c	LEVELS 3-5 SEGMENT C PARTIAL FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
T141	LEVEL 1 GARAGE FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
T142	LEVEL 2 GARAGE FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
T143	LEVELS 3-5 GARAGE FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
T144	LEVEL 6 GARAGE FLOOR PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
T400	UNIT PLANS TELECOM	1	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
T401	UNIT PLANS TELECOM	1	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
T402	UNIT PLANS TELECOM	1	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
T450	ENLARGED FLOOR PLANS	1	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
T451	ENLARGED FLOOR PLANS	1	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
T452	ENLARGED FLOOR PLANS	1	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
T453	ENLARGED POOL AREA PLAN	1	10/31/2025	11/10/2025	Addendum 004 (10/31/25)
T454	ENLARGED TELECOM ROOMS	1	10/31/2025	11/10/2025	Addendum 004 (10/31/25)

Arch-Con Corporation

Initials: _____

Printed on Thu Jan 29, 2026 at 01:45 pm CST

Job #: 2507007 The Silos
1235 Shadowdale Drive
Houston, Texas 77043

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
Civil Private					
C01	COVER SHEET	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
C02	GENERAL CONSTRUCTION NOTES	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
C03	EXISTING CONDITIONS	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
C04	DIMENSION CONTROL PLAN	2	10/31/2025	01/27/2026	Addendum 004 (10/31/25)
C05	FIRE LANE PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
C06	PAVING PLAN	2	10/31/2025	01/27/2026	Addendum 004 (10/31/25)
C07	GRADING PLAN	2	10/31/2025	01/27/2026	Addendum 004 (10/31/25)
C08	WATER LINE PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
C09	SANITARY SEWER PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
C10	STORM SEWER PLAN	2	10/31/2025	01/27/2026	Addendum 004 (10/31/25)
C11	DRAINAGE AREA MAP	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
C12	DRAINAGE CALCULATIONS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
C13	STORM WATER POLLUTION PREVENTION PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
C14	PAVING DETAILS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
C15	WATER DETAILS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
C16	SANITARY SEWER DETAILS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
C17	STORM DETAILS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
C18	DETENTION DETAILS	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
C19	STORM WATER POLLUTION PREVENTION PLAN DETAILS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
Civil Public Utilities					
CPU-01	COVER SHEET	0	05/21/2025	06/16/2025	Civil Public Utilities (COH Approved) (05/21/25)
CPU-02	GENERAL CONSTRUCTION NOTES	0	05/21/2025	06/16/2025	Civil Public Utilities (COH Approved) (05/21/25)
CPU-03	OVERALL LAYOUT	0	05/21/2025	06/16/2025	Civil Public Utilities (COH Approved) (05/21/25)
CPU-04	UTILITIES PLAN AND PROFILE	0	05/21/2025	06/16/2025	Civil Public Utilities (COH Approved) (05/21/25)
CPU-04.1	STORM CALCULATIONS	0	05/21/2025	06/16/2025	Civil Public Utilities (COH Approved)

Arch-Con Corporation

Initials: _____

Printed on Thu Jan 29, 2026 at 01:45 pm CST

Job #: 2507007 The Silos
1235 Shadowdale Drive
Houston, Texas 77043

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
					(05/21/25)
CPU-05	WATER LINE DETAILS	0	05/21/2025	06/16/2025	Civil Public Utilities (COH Approved) (05/21/25)
CPU-05.1	WATER LINE DETAILS 2 OF 2	0	05/21/2025	06/16/2025	Civil Public Utilities (COH Approved) (05/21/25)
CPU-06	SANITARY SEWER DETAILS	0	05/21/2025	06/16/2025	Civil Public Utilities (COH Approved) (05/21/25)
CPU-07	PAVING DETAILS	0	05/21/2025	06/16/2025	Civil Public Utilities (COH Approved) (05/21/25)
CPU-08	STORM SEWER DETAILS	0	05/21/2025	06/16/2025	Civil Public Utilities (COH Approved) (05/21/25)
CPU-09	SWPPP DETAILS	1	05/21/2025	06/16/2025	Civil Public Utilities (COH Approved) (05/21/25)
Landscape					
L100	OVERALL SITE PLAN	3	10/31/2025	01/27/2026	Addendum 004 (10/31/25)
L101	OVERALL PLANTING PLAN	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
L110	SITE PLAN NORTH	3	10/31/2025	01/27/2026	Addendum 004 (10/31/25)
L120	SITE PLAN SOUTH	2	10/31/2025	01/27/2026	Addendum 004 (10/31/25)
L210	POOL COURTYARD & PASSIVE PARK SITE PLAN	2	10/31/2025	01/27/2026	Addendum 004 (10/31/25)
L211	POOL COURTYARD & PASSIVE PARK LAYOUT PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
L212	POOL COURTYARD & PASSIVE PARK GRADING PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
L220	COURTYARD 1 & 2 SITE PLAN	2	10/31/2025	01/27/2026	Addendum 004 (10/31/25)
L221	COURTYARD 1 & 2 LAYOUT PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
L222	COURTYARD 1 & 2 GRADING PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
L300	OVERALL PLANTING PLAN	1	10/31/2025	01/27/2026	Addendum 004 (10/31/25)
L310	PLANTING PLAN NORTH	1	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
L320	PLANTING PLAN SOUTH	1	10/31/2025	01/27/2026	Addendum 004 (10/31/25)
L330	POOL COURTYARD & PASSIVE PARK PLANTING PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
L340	COURTYARD 1 & 2 PLANTING PLAN	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
L401	IRRIGATION PLAN	0	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
L402	IRRIGATION PLAN	0	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
L403	IRRIGATION SCHEDULE, COUNTS & CALCULATIONS	0	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
L404	IRRIGATION DETAILS	0	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
L405	IRRIGATION NOTES	0	08/15/2025	08/19/2025	Addendum 003 (08/15/25)
L501	POOL SECTIONS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)

Arch-Con Corporation

Initials: _____

Printed on Thu Jan 29, 2026 at 01:45 pm CST

Job #: 2507007 The Silos
1235 Shadowdale Drive
Houston, Texas 77043

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
L601	PAVILIOIN DETAILS	1	07/09/2025	07/11/2025	Addendum 001 (07/09/25)
L602	FIRE/TV WALL DETAILS	1	08/15/2025	08/25/2025	Addendum 003 (08/15/25)
L603	DETAILS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
L604	FENCING DETAILS	1	10/31/2025	01/27/2026	Addendum 004 (10/31/25)
L605	DETAILS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
L620	PLANTING DETAILS AND SPECIFICATIONS	0	05/30/2025	06/04/2025	Issue For Construction (IFC) (05/30/25)
Food Service					
FS 0.0	KEC NOTES	0	09/16/2025	09/23/2025	Cafe IFC (09/16/25)
FS 1.0	PLANVIEW - PLUMBING	0	09/16/2025	09/23/2025	Cafe IFC (09/16/25)
FS 1.1	PLAN VIEW - BOH & COFFEE BAR	0	09/16/2025	09/23/2025	Cafe IFC (09/16/25)
FS 2.0	ELECTRICAL ROUGH-INS	0	09/16/2025	09/23/2025	Cafe IFC (09/16/25)
FS 3.0	PLUMBING - ROUGH-INS	0	09/16/2025	09/23/2025	Cafe IFC (09/16/25)
FS 4.0	SPECIAL CONDITIONS - PLANVIEW	0	09/16/2025	09/23/2025	Cafe IFC (09/16/25)
FS 5.0	ELEVATIONS	0	09/16/2025	09/23/2025	Cafe IFC (09/16/25)

Arch-Con Corporation

Initials: _____

Printed on Thu Jan 29, 2026 at 02:26 pm CST

Job #: 2507007 The Silos
1235 Shadowdale Drive
Houston, Texas 77043

Current Specifications

Number	Description	Revision	Issued Date	Received Date	Set
00 - Procurement and Contracting Requirements					
00 00 00	PROJECT MANUAL SPECIFICATIONS COVER PAGE	0	05/30/25	06/04/25	IFC
00 00 01	TABLE OF CONTENTS	2	08/19/25	08/19/25	Addendum 003
00 31 32	GEOTECHNICAL DATA	0	05/30/25	06/04/25	IFC
01 - General Requirements					
01 00 00	GENERAL REQUIREMENTS	0	05/30/25	06/04/25	IFC
01 04 10	SPECIAL FORMS	0	05/30/25	06/04/25	IFC
01 05 00	FIELD ENGINEERING	0	05/30/25	06/04/25	IFC
01 11 10	PROFESSIONAL ENGINEERING	0	05/30/25	06/04/25	IFC
01 21 00	ALLOWANCES	0	05/30/25	06/04/25	IFC
01 23 00	ALTERNATES	0	05/30/25	06/04/25	IFC
01 25 00	SUBSTITUTION PROCEDURES	0	05/30/25	06/04/25	IFC
01 26 00	CONTRACT MODIFICATION PROCEDURES	0	05/30/25	06/04/25	IFC
01 29 00	PAYMENT PROCEDURES	0	05/30/25	06/04/25	IFC
01 31 00	PROJECT MANAGEMENT & COORDINATION	0	05/30/25	06/04/25	IFC
01 32 00	CONSTRUCTION PROGRESS DOCUMENTATION	0	05/30/25	06/04/25	IFC
01 33 00	SUBMITTAL PROCEDURES	0	05/30/25	06/04/25	IFC
01 40 00	QUALITY REQUIREMENTS	0	05/30/25	06/04/25	IFC
01 42 00	REFERENCES	0	05/30/25	06/04/25	IFC
01 50 00	TEMPORARY FACILITIES & CONTROLS	0	05/30/25	06/04/25	IFC
01 60 00	PRODUCT REQUIREMENTS	0	05/30/25	06/04/25	IFC
01 73 00	CONSTRUCTION EXECUTION	0	05/30/25	06/04/25	IFC
01 73 29	CUTTING & PATCHING	0	05/30/25	06/04/25	IFC
01 77 00	PROJECT CLOSEOUT PROCEDURES	0	05/30/25	06/04/25	IFC
01 78 23	OPERATION & MAINTENANCE MANUALS	0	05/30/25	06/04/25	IFC
01 78 39	PROJECT RECORD DOCUMENTS	0	05/30/25	06/04/25	IFC
03 - Concrete					
03 11 00	CONCRETE FORMS	0	05/30/25	06/04/25	IFC
03 11 13.13	CONCRETE FORM LINERS	0	05/30/25	06/04/25	IFC
03 21 00	CONCRETE REINFORCEMENT	0	05/30/25	06/04/25	IFC
03 30 00	CAST-IN-PLACE CONCRETE	0	05/30/25	06/04/25	IFC
03 36 50	POST-TENSIONED CONCRETE	0	05/30/25	06/04/25	IFC
03 41 00	PRECAST STRUCTURAL CONCRETE	0	05/30/25	06/04/25	IFC

Arch-Con Corporation

Initials: _____

Printed on Thu Jan 29, 2026 at 02:26 pm CST

Job #: 2507007 The Silos
1235 Shadowdale Drive
Houston, Texas 77043

Number	Description	Revision	Issued Date	Received Date	Set
03 54 13	GYPSUM CEMENT UNDERLAYMENT OVER SOUND MAT	1	08/19/25	08/19/25	Addendum 003
04 - Masonry					
04 20 00	UNIT MASONRY	0	05/30/25	06/04/25	IFC
04 43 13.13	ANCHORED STONE MASONRY VENEER	0	05/30/25	06/04/25	IFC
04 72 00	CAST STONE MASONRY	0	05/30/25	06/04/25	IFC
05 - Metals					
05 12 00	STRUCTURAL STEEL FRAMING	0	05/30/25	06/04/25	IFC
05 50 00	METAL FABRICATIONS	0	05/30/25	06/04/25	IFC
05 51 16	METAL STAIRS - PRECAST CONCRETE TREADS	0	05/30/25	06/04/25	IFC
05 52 13	PIPE AND TUBE RAILINGS	0	05/30/25	06/04/25	IFC
05 73 10	ORNAMENTAL RAILINGS	1	08/19/25	08/19/25	Addendum 003
06 - Wood, Plastics, and Composites					
06 05 73.13	FIRE-RETARDANT TREATED WOOD PRODUCTS	0	05/30/25	06/04/25	IFC
06 10 00	ROUGH CARPENTRY	0	05/30/25	06/04/25	IFC
06 16 00	SHEATHING	0	05/30/25	06/04/25	IFC
06 17 51	SHOP-FABRICATED WOOD TRUSSES	0	05/30/25	06/04/25	IFC
06 40 23	INTERIOR ARCHITECTURAL WOODWORK	0	05/30/25	06/04/25	IFC
07 - Thermal and Moisture Protection					
07 13 26	SELF-ADHERING SHEET WATERPROOFING	0	05/30/25	06/04/25	IFC
07 18 00	TRAFFIC COATINGS	0	05/30/25	06/04/25	IFC
07 21 00	THERMAL INSULATION	0	05/30/25	06/04/25	IFC
07 21 19	FOAMED-IN-PLACE INSULATION	0	05/30/25	06/04/25	IFC
07 25 00	WEATHER BARRIERS	0	05/30/25	06/04/25	IFC
07 26 00	VAPOR RETARDERS	0	05/30/25	06/04/25	IFC
07 42 13	METAL SIDING PANELS	0	05/30/25	06/04/25	IFC
07 46 46	FIBER-CEMENT SIDING	0	05/30/25	06/04/25	IFC
07 54 23	THERMOPLASTIC-POLYOLEFIN (TPO) ROOFING	0	05/30/25	06/04/25	IFC
07 62 00	SHEET METAL FLASHING AND TRIM	0	05/30/25	06/04/25	IFC
07 72 00	ROOF ACCESSORIES	0	05/30/25	06/04/25	IFC
07 81 00	APPLIED FIREPROOFING	0	05/30/25	06/04/25	IFC
07 84 13	PENETRATION FIRESTOPPING	0	05/30/25	06/04/25	IFC
07 84 46	FIRE-RESISTIVE JOINT SYSTEMS	0	05/30/25	06/04/25	IFC
07 92 00	JOINT SEALANTS	0	05/30/25	06/04/25	IFC
08 - Openings					
08 11 13	HOLLOW METAL DOORS AND FRAMES	0	05/30/25	06/04/25	IFC
08 14 33	MOLDED FACE STILE & RAIL DOORS	0	05/30/25	06/04/25	IFC
08 16 13	FIBERGLASS ENTRY DOORS & FRAMES	0	05/30/25	06/04/25	IFC

Arch-Con Corporation

Initials: _____

Printed on Thu Jan 29, 2026 at 02:26 pm CST

Job #: 2507007 The Silos
1235 Shadowdale Drive
Houston, Texas 77043

Number	Description	Revision	Issued Date	Received Date	Set
08 31 13	ACCESS DOORS AND FRAMES	0	05/30/25	06/04/25	IFC
08 32 16	VINYL PATIO DOORS	0	05/30/25	06/04/25	IFC
08 33 23	OVERHEAD COILING DOORS	0	05/30/25	06/04/25	IFC
08 41 13	ALUMINUM-FRAMED ENTRANCES AND STOREFRONTS	0	05/30/25	06/04/25	IFC
08 53 13	VINYL FRAMED WINDOWS	0	05/30/25	06/04/25	IFC
08 71 00	DOOR HARDWARE	2	10/31/25	11/10/25	Addendum 004
08 80 00	GLAZING	0	05/30/25	06/04/25	IFC
08 83 00	MIRRORS	0	05/30/25	06/04/25	IFC
08 90 00	LOUVERS AND VENTS	0	05/30/25	06/04/25	IFC
08 95 16	EXTERIOR FIXED LOUVERS AND VENTS	0	05/30/25	06/04/25	IFC
09 - Finishes					
09 21 16.23	GYPSUM BOARD SHAFT WALL ASSEMBLIES	0	05/30/25	06/04/25	IFC
09 29 00	GYPSUM BOARD	0	05/30/25	06/04/25	IFC
09 30 00	TILING	2	08/19/25	08/19/25	Addendum 003
09 30 33	STONE TILING	1	08/19/25	08/19/25	Addendum 003
09 65 19	RESILIENT VINYL PLANK & TILE FLOORS	1	08/19/25	08/19/25	Addendum 003
09 68 10	CARPETING	0	08/19/25	08/19/25	Addendum 003
09 72 00	WALL COVERINGS	0	05/30/25	06/04/25	IFC
09 91 10	PAINTING	1	08/19/25	08/19/25	Addendum 003
10 - Specialties					
10 14 23	SIGNAGE	0	05/30/25	06/04/25	IFC
10 28 00	TOILET, BATH AND JANITORIAL ACCESSORIES	0	05/30/25	06/04/25	IFC
10 28 19	FRAMELESS SHOWER DOORS & ENCLOSURES	0	05/30/25	06/04/25	IFC
10 31 00	MANUFACTURED FIREPLACES	0	05/30/25	06/04/25	IFC
10 44 13	FIRE EXTINGUISHERS AND CABINETS	0	05/30/25	06/04/25	IFC
10 55 00	POSTAL SPECIALTIES	0	05/30/25	06/04/25	IFC
10 73 13	AWNINGS	0	05/30/25	06/04/25	IFC
11 - Equipment					
11 06 30	WINDOW WASHING SYSTEMS	0	05/30/25	06/04/25	IFC
11 31 00	RESIDENTIAL APPLIANCES	1	08/19/25	08/19/25	Addendum 003
11 82 26	SOLID WASTE COMPACTORS	0	05/30/25	06/04/25	IFC
12 - Furnishings					
12 21 15	WINDOW SHADES	0	05/30/25	06/04/25	IFC
12 35 30	RESIDENTIAL CASEWORK & CABINETRY	0	05/30/25	06/04/25	IFC
12 36 41	GRANITE COUNTERTOPS	0	05/30/25	06/04/25	IFC
12 48 13	ENTRANCE FLOOR MATS AND FRAMES	0	05/30/25	06/04/25	IFC
12 93 00	SITE FURNISHINGS	0	05/30/25	06/04/25	IFC

Arch-Con Corporation

Initials: _____

Printed on Thu Jan 29, 2026 at 02:26 pm CST

Job #: 2507007 The Silos
1235 Shadowdale Drive
Houston, Texas 77043

Number	Description	Revision	Issued Date	Received Date	Set
13 - Special Construction					
13 11 10	SWIMMING POOL AND SPA	0	05/30/25	06/04/25	IFC
14 - Conveying Equipment					
14 21 23.16	MACHINE ROOM-LESS ELECTRIC TRACTION ELEVATORS	1	08/19/25	08/19/25	Addendum 003
14 91 00	FACILITY CHUTES	0	05/30/25	06/04/25	IFC
21 - Fire Suppression					
21 00 00	FIRE PROTECTION GENERAL	0	08/13/25	08/13/25	Addendum 002
21 08 00	COMMISSIONING OF FIRE SUPRESSION	0	08/13/25	08/13/25	Addendum 002
21 30 00	ELECTRIC FIRE PUMP AND ACCESSORIES	0	08/13/25	08/13/25	Addendum 002
22 - Plumbing					
22 00 00	PLUMBING GENERAL	0	08/13/25	08/13/25	Addendum 002
22 08 00	COMMISSIONING OF PLUMBING	0	08/13/25	08/13/25	Addendum 002
22 11 23	DOMESTIC WATER PRESSURE BOOSTER SYSTEM	0	08/13/25	08/13/25	Addendum 002
22 16 00	NATURAL GAS PIPING SYSTEM	0	08/13/25	08/13/25	Addendum 002
22 40 00	PLUMBING FIXTURES	0	08/13/25	08/13/25	Addendum 002
23 - Heating, Ventilating, and Air Conditioning (HVAC)					
23 00 00	HVAC GENERAL	0	08/13/25	08/13/25	Addendum 002
23 05 93	TESTING, ADJUSTING AND BALANCING (TAB)	0	08/13/25	08/13/25	Addendum 002
23 07 00	HVAC INSULATION	0	08/13/25	08/13/25	Addendum 002
23 07 14	FIRE-RATED INSULATION SYSTEMS	0	08/13/25	08/13/25	Addendum 002
23 08 00	COMMISSIONING OF HVAC SYSTEMS	0	08/13/25	08/13/25	Addendum 002
23 09 20	VARIABLE FREQUENCY DRIVES	0	08/13/25	08/13/25	Addendum 002
23 23 00	REFRIGERANT PIPING, INSULATION AND ACCESSORIES	0	08/13/25	08/13/25	Addendum 002
23 31 00	DUCTWORK AND ACCESSORIES	0	08/13/25	08/13/25	Addendum 002
23 34 00	UNITARY EXHAUST, SUPPLY FANS, AND VENTILATORS	0	08/13/25	08/13/25	Addendum 002
23 35 02	PARKING GARAGE VENTILATION SYSTEM	0	08/13/25	08/13/25	Addendum 002
23 37 00	LOUVERS, GRILLES, REGISTERS AND DIFFUSERS	0	08/13/25	08/13/25	Addendum 002
23 74 00	SINGLE PACKAGE ROOFTOP AIR CONDITIONERS	0	08/13/25	08/13/25	Addendum 002
23 81 23.12	DUCTLESS COOLING ONLY SPLIT SYSTEMS	0	08/13/25	08/13/25	Addendum 002
23 81 26	SPLIT SYSTEM AIR CONDITIONERS	0	08/13/25	08/13/25	Addendum 002
23 81 28	SPLIT SYSTEM HEAT PUMPS	0	08/13/25	08/13/25	Addendum 002
23 81 28.12	DUCTLESS COOLING ONLY SPLIT SYSTEMS	0	08/13/25	08/13/25	Addendum 002
23 81 28.13	DUCTLESS SPLIT SYSTEM HEAT PUMPS	0	08/13/25	08/13/25	Addendum 002
23 82 39	ELECTRIC UNIT HEATERS	0	08/13/25	08/13/25	Addendum 002
23 82 39.19	ELECTRIC WALL HEATERS	0	08/13/25	08/13/25	Addendum 002
26 - Electrical					
26 00 00	ELECTRICAL GENERAL	0	08/13/25	08/13/25	Addendum 002

Arch-Con Corporation

Initials: _____

Printed on Thu Jan 29, 2026 at 02:26 pm CST

Job #: 2507007 The Silos
1235 Shadowdale Drive
Houston, Texas 77043

Number	Description	Revision	Issued Date	Received Date	Set
26 05 19	CONDUCTORS	0	08/13/25	08/13/25	Addendum 002
26 05 26	GROUNDING	0	08/13/25	08/13/25	Addendum 002
26 05 30	FIRESTOPPING FOR ELECTRICAL SYSTEMS	0	08/13/25	08/13/25	Addendum 002
26 05 33	CONDUIT AND RACEWAYS	0	08/13/25	08/13/25	Addendum 002
26 05 34	OUTLET BOXES AND JUNCTION BOXES	0	08/13/25	08/13/25	Addendum 002
26 09 23	OCCUPANCY SENSORS	0	08/13/25	08/13/25	Addendum 002
26 24 13	SWITCHBOARDS	0	08/13/25	08/13/25	Addendum 002
26 24 16	PANELBOARDS	0	08/13/25	08/13/25	Addendum 002
26 26 53	ELECTRIC VEHICLE CHARGING EQUIPMENT	0	08/13/25	08/13/25	Addendum 002
26 27 13	MODULAR METERING EQUIPMENT	0	08/13/25	08/13/25	Addendum 002
26 27 26	WIRING DEVICES	0	08/13/25	08/13/25	Addendum 002
26 28 16	DISCONNECT SWITCHES	0	08/13/25	08/13/25	Addendum 002
26 28 18	ENCLOSED CIRCUIT BREAKERS	0	08/13/25	08/13/25	Addendum 002
26 43 13	SURGE PROTECTIVE DEVICES (SPD)	0	08/13/25	08/13/25	Addendum 002
26 51 00	LIGHTING	0	08/13/25	08/13/25	Addendum 002
28 - Electronic Safety and Security					
28 30 00	TWO-WAY EMERGENCY COMMUNICATION SYSTEM	0	08/13/25	08/13/25	Addendum 002
28 31 11	FIRE DETECTION & ALARM SYSTEM	0	05/30/25	06/04/25	IFC
28 31 11.1	FIRE ALARM – ADDRESSABLE	0	08/13/25	08/13/25	Addendum 002
28 31 13	FIRE ALARM – SPRINKLER MONITORING	0	08/13/25	08/13/25	Addendum 002
31 - Earthwork					
31 20 00	EARTH MOVING	0	05/30/25	06/04/25	IFC
31 31 16	TERMITE CONTROL	0	05/30/25	06/04/25	IFC
32 - Exterior Improvements					
32 13 13	CONCRETE PAVING	0	05/30/25	06/04/25	IFC
32 13 16	DECORATIVE CONCRETE PAVING	0	05/30/25	06/04/25	IFC
32 13 73	CONCRETE PAVING JOINT SEALANTS	0	05/30/25	06/04/25	IFC
32 14 00	UNIT PAVERS	0	05/30/25	06/04/25	IFC
32 17 23	PAVEMENT MARKINGS	0	05/30/25	06/04/25	IFC
32 31 19	DECORATIVE METAL FENCES AND GATES	0	05/30/25	06/04/25	IFC
32 84 00	PLANTING IRRIGATION	0	05/30/25	06/04/25	IFC
32 92 00	TURF AND GRASSES	0	05/30/25	06/04/25	IFC
32 93 00	PLANTS	0	05/30/25	06/04/25	IFC
33 - Utilities					
33 05 00	COMMON WORK RESULTS FOR UTILITIES	0	05/30/25	06/04/25	IFC
33 41 00	STORM UTILITY DRAINAGE PIPING	0	05/30/25	06/04/25	IFC
34 - Transportation					

Arch-Con Corporation

Initials: _____

Printed on Thu Jan 29, 2026 at 02:26 pm CST

Job #: 2507007 The Silos
1235 Shadowdale Drive
Houston, Texas 77043

Number	Description	Revision	Issued Date	Received Date	Set
34 60 13	ELECTRIC VEHICLE CHARGING STATIONS	0	05/30/25	06/04/25	IFC
